

# Weekly Report W28



# BOP-IDOM-EHSS – SAFETY MOMENT- Peer pressure W28



## SAFETY MOMENT

### PEER PRESSURE IN CONSTRUCTION






OUR GOAL:  
Everyone goes home  
SAFE, EVERY DAY.

EVERY DAY YOU INFLUENCE OTHERS. CHOOSE TO BE A POSITIVE INFLUENCE!



### NEGATIVE PEER PRESSURE

It can put you and others at risk!



It will only take a minute!

Nobody wears it around here.

Don't be a baby!

We need to finish today. Skip the safety stuff.



### POSITIVE PEER PRESSURE

It protects you and your team!



Let's do it the right way. Safety first.

Good catch! You protected us all.

Check your harness and connect 100%.

We stop the job if it's not safe. That's how we look out for each other.



#### EXAMPLES

- Skipping fall protection to save time
- Bypassing lockout/tagout (LOTO)
- Not wearing required PPE
- Ignoring exclusion zones
- Using damaged tools or equipment
- Taking shortcuts to meet production



#### CONSEQUENCES

- Falls, fractures, head injuries
- Electrocutation, burns, amputations
- Serious injuries or fatalities
- Equipment damage
- Delays and rework
- Legal and financial consequences
- Impact on families and team

#### TECHNICAL EXAMPLES – NEGATIVE vs POSITIVE

|                                                                                                        | NEGATIVE BEHAVIOR<br>(Short term gain – Long term pain) | POSITIVE BEHAVIOR<br>(Do it right – Go home safe)                            |
|--------------------------------------------------------------------------------------------------------|---------------------------------------------------------|------------------------------------------------------------------------------|
|  WORKING AT HEIGHT    | ✗ Skip harness or anchor to wrong point.                | ✓ Use full body harness, correct anchor, maintain 3-point contact.           |
|  ELECTRICAL WORK      | ✗ Work on live equipment or temporary bypass.           | ✓ De-energize, verify zero energy, lock, tag, and test.                      |
|  LOTO               | ✗ Remove someone else's lock or don't apply your own.   | ✓ Apply your personal lock and tag, verify isolation before work.            |
|  LIFTING OPERATIONS | ✗ Stand under/near load, don't check rigging.           | ✓ Inspect rigging, use tag lines, stay clear of suspended loads.             |
|  SCAFFOLDING        | ✗ Use damaged scaffold, remove components.              | ✓ Use inspected scaffold, keep all components in place, follow access rules. |
|  PPE                | ✗ No eye/ear protection during grinding.                | ✓ Wear eye shield/ear protection. Check and maintain PPE.                    |



#### EXAMPLES – WHAT POSITIVE PEER PRESSURE LOOKS LIKE



##### WEAR YOUR PPE

Encourage full PPE: hard hat, safety glasses, hi-vis, gloves, safety boots, hearing protection. It reduces injury risk.



##### USE FALL PROTECTION – 100% TIE OFF

Always use a properly fitted harness and connect to an approved anchor point when working at height. Inspect before use.



##### FOLLOW LOTO PROCEDURES

Verify isolation of energy sources, apply lock, tag, and try-before-touch. Never bypass LOTO.



##### RESPECT EXCLUSION ZONES

Keep out of the line of fire from suspended loads, equipment, and excavation edges.



##### USE THE RIGHT TOOLS & EQUIPMENT

Use the right tool for the job. Inspect tools, ladders, and scaffolds before use. Report and remove damaged items.



##### SPEAK UP & LISTEN

If you see something unsafe, say something. Listen when others speak up. We all look out for each other.



##### PLAN THE WORK, WORK THE PLAN

Review the task, hazards, and controls (JSA). Understand the plan before you start.



##### KEEP COMMUNICATION OPEN

Clear communication prevents mistakes. Ask questions. Confirm understandings.



### BE A LEADER. BE A GOOD INFLUENCE.

### SAFETY STARTS WITH YOU!

### SAFETY IS NOT A SLOGAN.

### IT'S A CHOICE WE MAKE EVERY DAY.

### REMEMBER:

Your attitude influences the site.  
Be the reason someone goes home safe.



Stegra

2

Type of information: General (CUSTOM)


# BOP-IDOM-EHSS – DASHBOARD Summary (Week 28)

For information


## Lagging Performance Indicators

394 Days LTI Free!!!!

### All Incidents & Risks

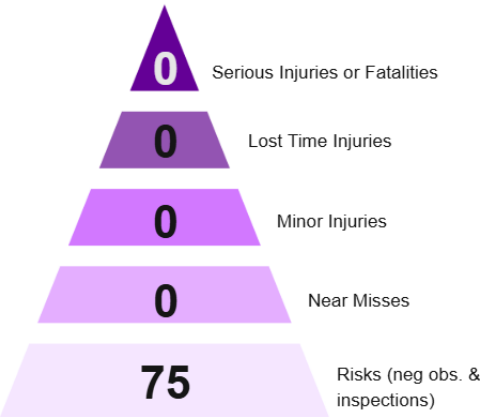

### SIF Potential Classification

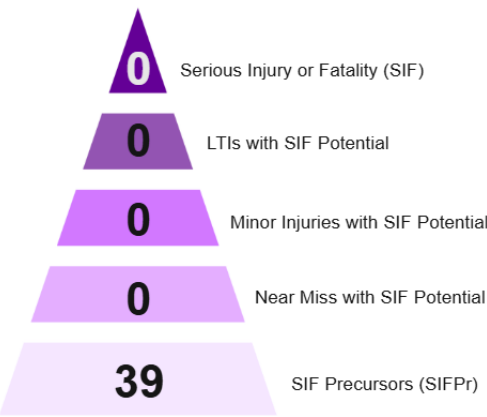

|       | Project to date | UE Construction | Benchmarking sector |
|-------|-----------------|-----------------|---------------------|
| LTIFR | 1,55            | 5               | 2                   |
| TRIFR | 5,15            | N/A             | N/A                 |


## Highlights/Downlights of the week:

Continuous BOP specific induction delivered by Idom HSE team to contractors.  
08<sup>th</sup> July: Pneumatic pressure test LNG safely performed .


## Leading Performance Indicators

|                                                 | Week | Last week | Project to date |
|-------------------------------------------------|------|-----------|-----------------|
| SITE WALKS                                      | 22   | 10        | 966             |
| OBSERVATIONS                                    | 107  | 112       | 5951            |
| BBS INSPECTIONS                                 | 25   | 19        | 625             |
| TARGET INSPECTIONS                              | 19   | 43        | 310             |
| NEAR-MISS                                       | 0    | 0         | 48              |
| ENVIRONMENTAL IN                                | 0    | 0         | 17              |
| Environmental Corrective Actions Closed on Time | 0    | 1         | 16              |
| PERMITS TO WORK                                 | 44   | 52        | 731             |
| RAMS APPROVED                                   | 2    | 4         | 87              |
| REWARDS                                         | 6    | 0         | 35              |
| SENDING OFFS                                    | 0    | 0         | 0               |


### Observations by Reporting Company



### Observations by Type

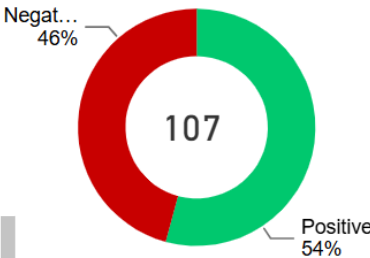


### Observations by Resp. Main Contractor



### Observations by Category



### Site Walks by Reporting Company



### Site Walks by Type

|                        |                          |                |                 |                                         |
|------------------------|--------------------------|----------------|-----------------|-----------------------------------------|
| Total Actions Reported | Open Actions (Clickable) | Closed Actions | Closed Past Due | Open/Closed Overdue Actions (Clickable) |
| 254                    | 47                       | 207            | 52              | 22                                      |







# BOP-IDOM-EHSS – BBS Dashboard (Week 28)

## Behaviour Based Safety Assessments


Last Update:  
13 iul. 2026 03:21

Checklist Name: Toate  
Related to Main Contractor: Toate  
Major Area: BOP  
From Week: 25W24  
To Week: 26W28


### Safety Performance With TRIF

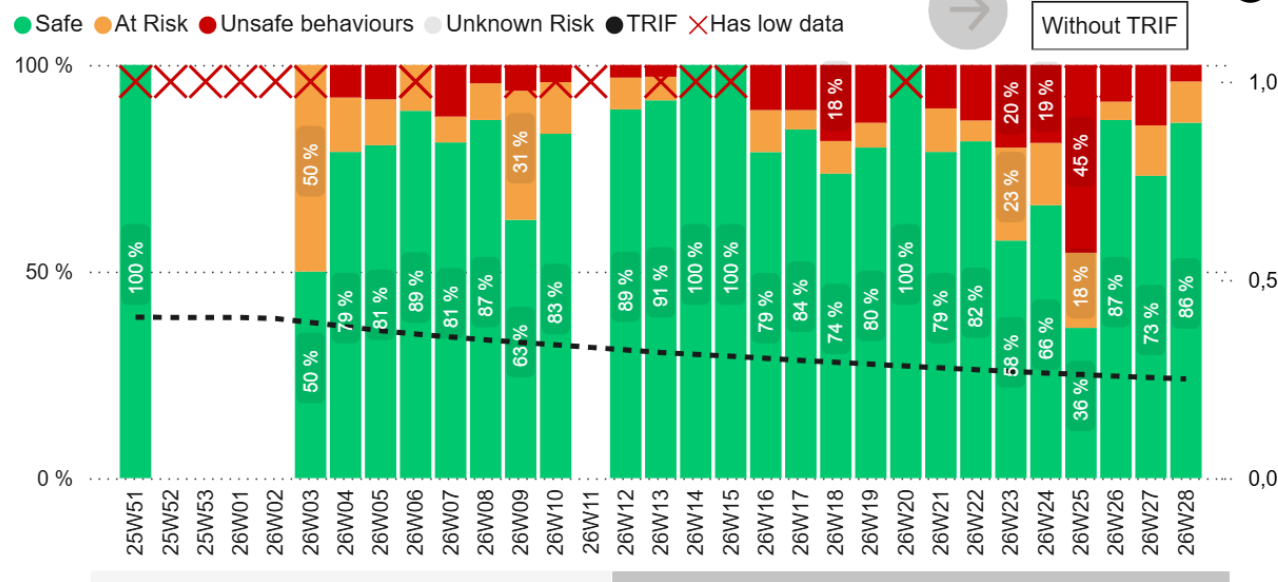


### Safety Performance by Category

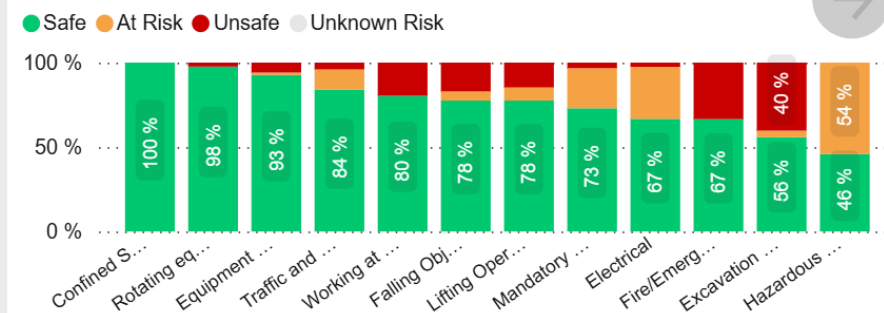


### Assessment Timeline

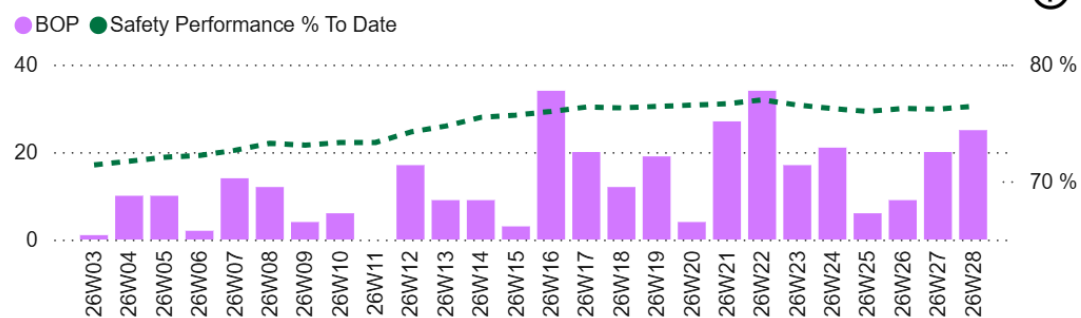

### Assessments related to Main Contractor



### Feedback distribution

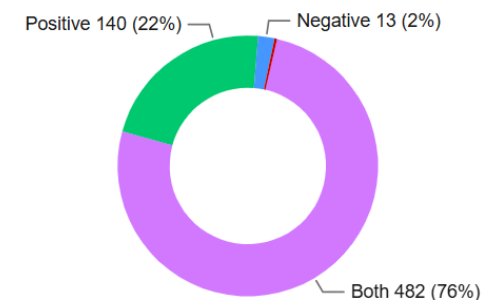



# BOP | IDOM Summary – QA/QC Site Quality (W28)

## Key Achievements

- 1.The ITPs for Nordic have been approved.
- 2. ITPs for GRK Rail has been submitted , after allignment meeting took place Stergra/ EPCM/GRK Rail.
- 3. Allignment meeting has been took place with GRK Pounds. The ITPs for East Pond has been submitted and Reviewed with Comments.
- 4. 3 Chart Pressure Test has been took place succesfully.
- 5. Allignment meeting took place for HO in PDOP Area -Anfra/STS
- 6. 1 TPs for Fermmix has been submitted

## Look Ahead Week 25


- 1. Pressure Test for Chart Ferroxx to take place. Pending 7 TPs to be submitt for the review.
- 2.1 TPs Fermmix to be approve and PT to take place.
- 3. GRK TPs priority 1 to be submitted for review and approval.
- 4.Stegra BOP Quality Audit to proceed this week.

## Major Risk


- 1. GRK ITP Roads to be resubmitted.
- 2. Partial Handovers GRK/ Nordic ( RW, PB, LNG Area) and ANFRA/STS ( PDOP area)

BOP | IDOM Summary – QA/QC Site Quality (W28)

| Weekly Progress Summary - QA |        |     |           |        |        |        |
|------------------------------|--------|-----|-----------|--------|--------|--------|
| Type                         | Owner  | New | # to date | # open | >30 d. | >60 d. |
| Quality Observation (QOC)    | EPCM   | 10  | 238       | 33     | 10     | 5      |
|                              | Stegra | 2   | 748       | 30     | 17     | 11     |
|                              | Total  | 12  | 986       | 63     | 27     | 16     |
| Non Conformance Report (NCR) | EPCM   | 0   | 23        | 3      | 0      | 1      |
|                              | Stegra | 0   | 83        | 10     | 2      | 8      |
|                              | Total  | 0   | 106       | 13     | 2      | 9      |

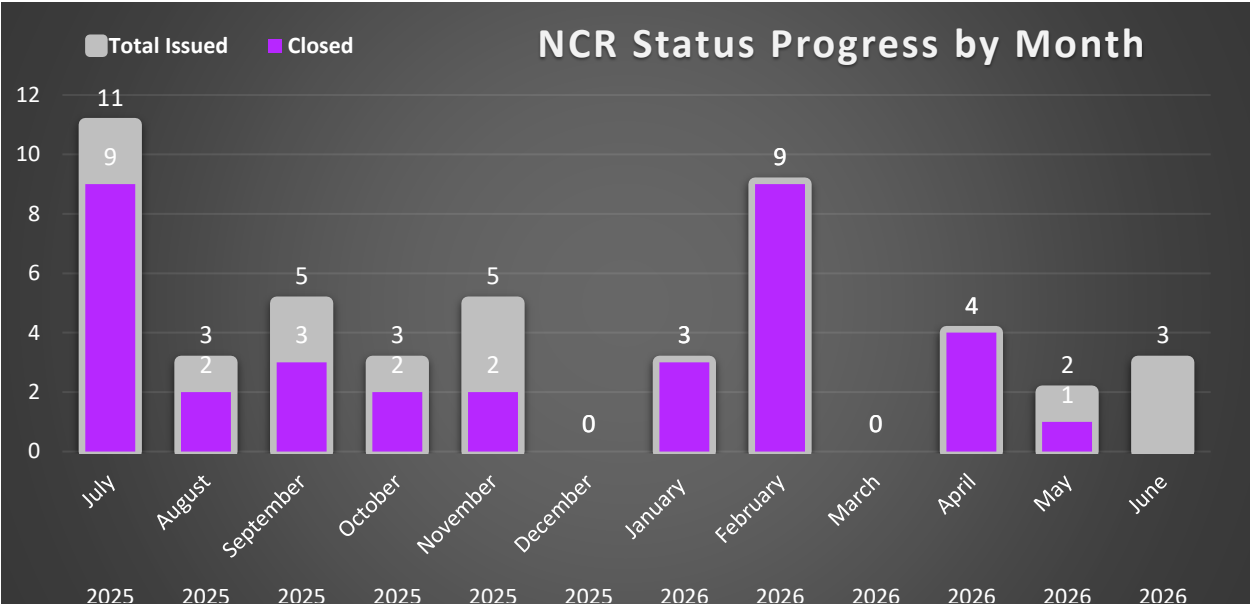



Test Pack Status

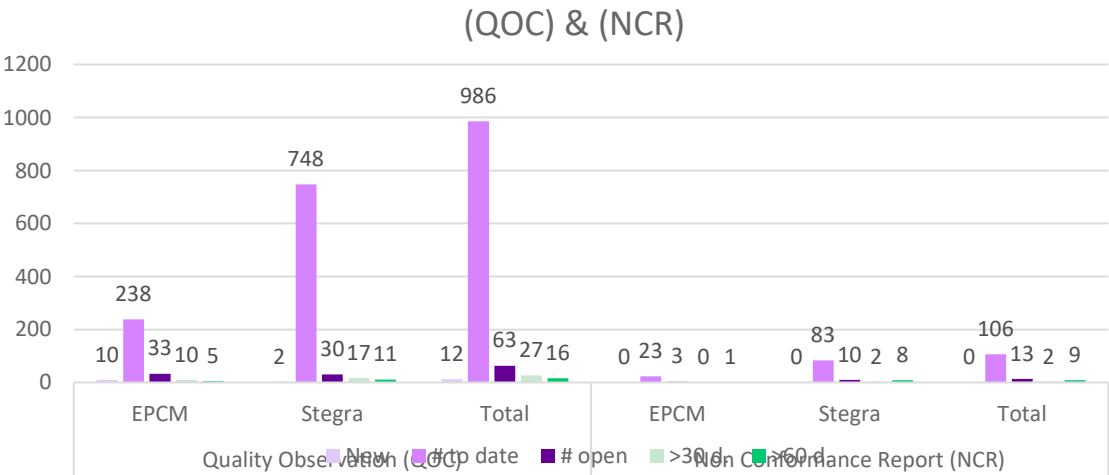

| Test Packs  | Planned Test Packs | Submitted Test Packs | Reviewed Test Packs (IDOM) | Approved for testing | Completed | As Built |
|-------------|--------------------|----------------------|----------------------------|----------------------|-----------|----------|
| Ferrmix     | 31                 | 2                    | 1                          | 1                    | 1         | 1        |
| CHART Ferox | 14                 | 7                    | 7                          | 7                    | 6         | 0        |
| GRK         | 8 / P1             | 1                    | 1                          | 0                    | 0         | 0        |

# BOP | IDOM Summary – QA/QC Site Quality (W28)

| Weekly NOI Issuance by Contractors |      |      |      |      |      |      |      |      |      |      |      |      |
|------------------------------------|------|------|------|------|------|------|------|------|------|------|------|------|
| Inspection Status                  | W19  | W20  | W21  | W22  | W23  | W24  | W25  | W26  | W27  | W28  | W29  | W30  |
| Accepted                           | 20   | 34   | 33   | 52   | 58   | 47   | 62   | 43   | 48   | 80   | 0    | 0    |
| Rejected                           | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    |
| Postponed                          | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    |
| Rejection Rate                     | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    | 0    |
| KPI Threshold                      | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% | 5.0% |

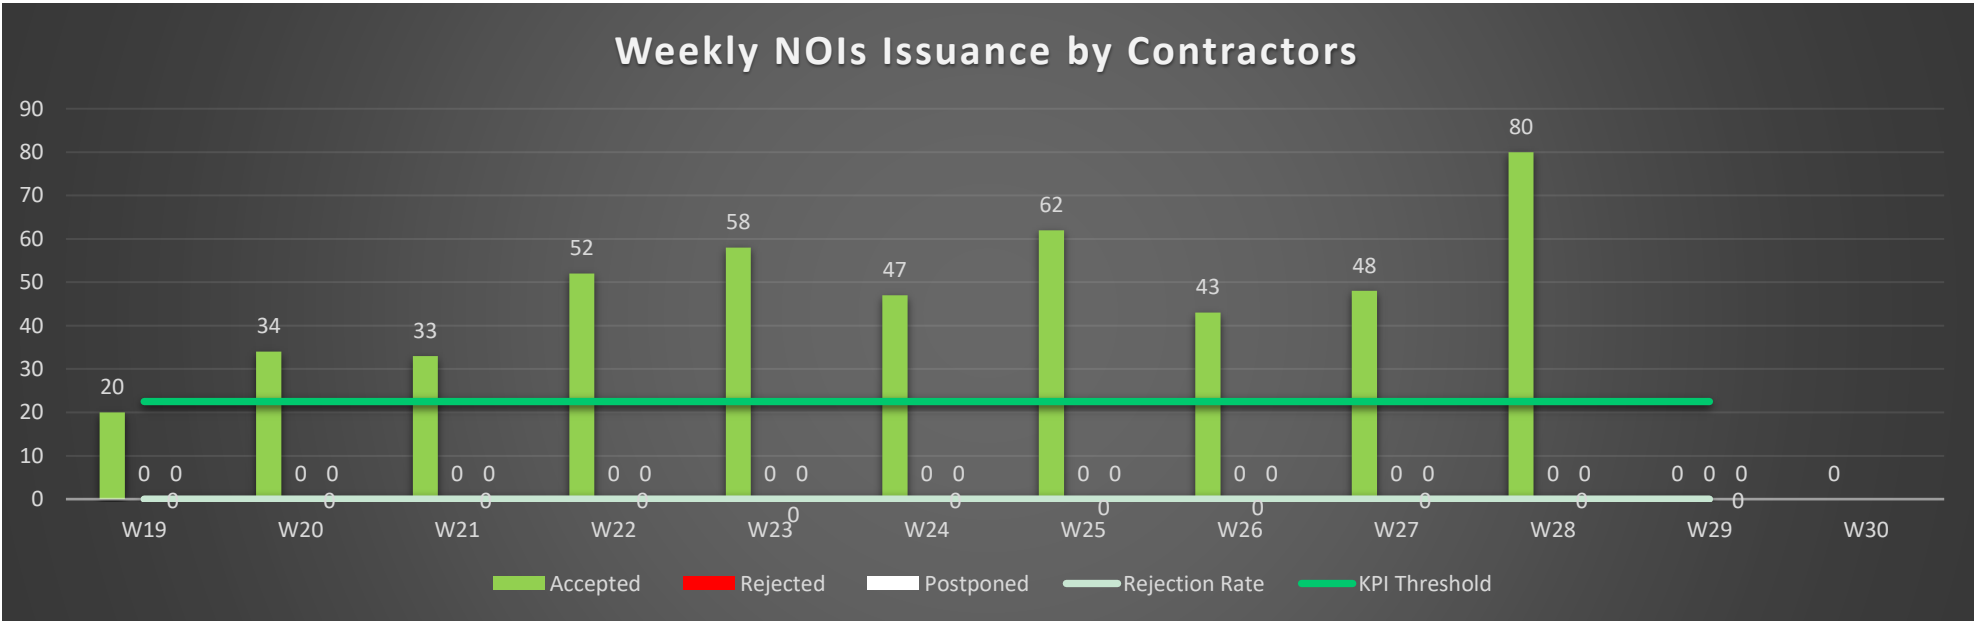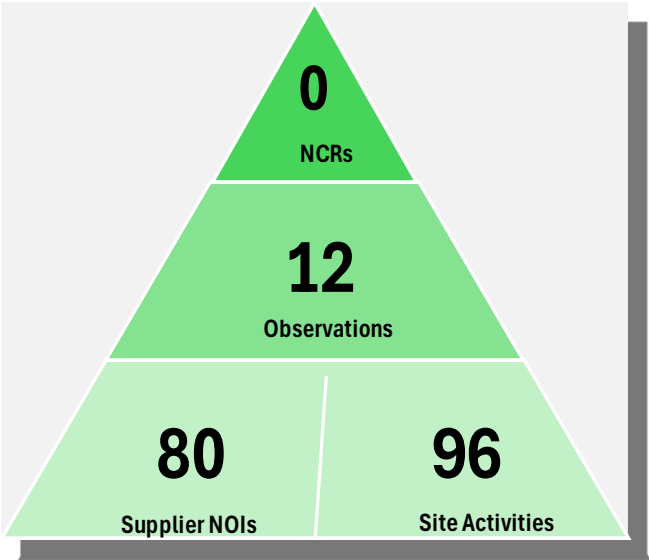



# BOP | IDOM Summary – QA/QC Site Quality (W28)

| Partial Handover between       |              |                 |                                         |       |      |           |            |           |
|--------------------------------|--------------|-----------------|-----------------------------------------|-------|------|-----------|------------|-----------|
| Contractors                    |              |                 |                                         |       |      |           |            |           |
| Definition                     | System       | Subsystem       | Tag No                                  | ITRs  | TCCC | Walkdowns | Punch List | Completed |
| GRK-Stegra-Municipality Piping | SIN-800-TEMP | SIN-800-01-TEMP | TEMP-BOP-1001-WRW-0800-10P1-NI          | P-02A | TCCC | Done      | None       | Completed |
| GRK-Stegra-Municipality Civil  | SIN-800-TEMP | TBD             | TEMP-BOP-Civil_Works_ Temporary<br>Line | C-25A | TCCC |           |            |           |
| GRK-Nordic RW Area             | SIN-907A     | SIN-907-01,02   | RW Receiving &Pumping Station           | TCCC  | TCCC |           |            |           |
| GRK -Nordic LNG Area           | SIN-909A     | SIN-909A-101    | LNG-TCCC from GRK to NOR                | TCCC  | TCCC |           |            |           |
| GRK-Fermmix PB Area            | SIN-980      | SIN/980/01,02   | Pipe Racks, Columns,Foudations 1-5      | TCCC  | TCCC |           |            |           |
| ANFRA/STS PDOP Area            | SIN-987      | SIN/987-02      | PDOP Capacitor Bank Trenches            | TCCC  | TCCC |           |            |           |

# Project Risk Update – Balance of Plant

- 41 total BOP Type 2 risks identified – 20 active, 2 draft, 0 parked, 0 submitted, 16 retired, 3 expired
- Out of 20 active risk – 0 critical, 5 major, 11 moderate, 4 minor risks assessed
- 60 total mitigation actions planned for all active risks – 5 overdue, 23 open, 30 closed, 2 canceled

Data Date: 10 July 2026

| Risk ID     | Function                      | Risk Title                                                                                                                                                                     | Current Score | Risk Mitigation Actions                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   | Predicted Score |
|-------------|-------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------|
| B1.BOP.R22  | Construction & Site Execution | GNRL - Misaligned area schedules and complex multi-contractor interfaces lead to blocked BOP Workfront and delayed equipment deliveries resulting in schedule and cost impacts | 30            | <ul style="list-style-type: none"> <li>- Sequence UGP and piping to avoid SMS install clashes; await SMS schedule (31/07/2026 - Open) @Marten Sonnerup</li> <li>- Interface Meeting with STM and BOP Construction team to align UGP works and SMS equipment deliveries. (31/07/2026 - Open) @Marten Sonnerup</li> <li>- Prepare reforecast schedule for BOP and Interface dates with STM and other areas <b>(07/07/2026 - Open) @Reghardt Heunes / Comment: It is under discussion and waiting for the STM-McDermott rebaseline, which currently they are working on</b></li> <li>- Align and finalize with WTP1 and WTP2 for access dates (31/07/26 - Open) @Marten Sonnerup / Comment: Ongoing discussion, as there is interference with Eiffage due to road works in front of WTP2, where Eiffage is scheduled to carry out works; an alternative northern access is also under discussion.</li> </ul> | 19              |
| B1.BOP.R10  | Construction & Site Execution | RAIL - Late Handover of STM Construction Areas (Scrapyard, CLP) – Impacting Rail                                                                                               | 25            | <ul style="list-style-type: none"> <li>- Follow up on Micropiling progress in Scrapyard area (15/08/2026 – Open) @Roger Campbell / Comment : Work must be completed by mid-August to allow follow-on activities. Delays beyond early September will impact rail works and may place them on the critical path, with potential multi-month delays due to winter. <b>The micro-piling contract has not yet been awarded by STM-McDermott, there might not be a short list in place; since execution takes ~8 weeks, award is required within the next few days to enable rail works to start in September as planned.</b> Stegra have instructed STM-McDermott to provide an acceptable rebaseline.</li> </ul>                                                                                                                                                                                              | 23              |
| B1.BOP.R548 | Construction & Site Execution | Pipe Bridge (21) Modules Install blockage by STM and may need to be paused                                                                                                     | 21            | <ul style="list-style-type: none"> <li>- Finalize decision on BOP continuation of 19 modules and confirm if need by dates of utilities will still be met (31/07/2026 – Open) @Chris Van Der Berg</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | 14              |
| B1.BOP.R387 | Construction & Site Execution | PDOP - Uncoordinated Installation of HV and Control Cables leading to blocked handover by HESE resulting in delay of permanent power                                           | 19            | <ul style="list-style-type: none"> <li>- HESE to review IFC prior to Production &amp; Construction (31/08/2026 - Open) @Tomas Winter</li> <li>- HESE to define required documentation prior to Handover (31/08/2026 - Open) @Tomas Winter</li> <li>- [Stegra to] review and possibly revise [its] handover procedure to include electrical installation works (31/08/2026 - Open) @Tomas Winter</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | 11              |
| B1.BOP.R565 | Project Delivery General      | UGNW - Av 9 Underground piping installation may not be completed by end of 2026                                                                                                | 19            | <ul style="list-style-type: none"> <li>- Award Avenue 9 scope to another contractor who is already working on site (to avoid loss of time due to running a tender and subsequent mobilisation) (31/07/2026 – Closed) @Tuncay Ozel</li> </ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | 19              |

\*\*\* Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.

# Project Risk Update – Balance of Plant (2/2)

*(Reviewed by Stegra and Idom Risk Management)*

*Status and summary comments as per previous week.*

| Risk ID     | Function          | Risk Tit                                                                                                                            | Current Score | Risk Mitigation Actions                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            | Predicted Score |
|-------------|-------------------|-------------------------------------------------------------------------------------------------------------------------------------|---------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------|
| B1.BOP.R434 | Supply Chain FWRW | Management - Delay in the signing process for the RW and FF steel structure contract (Structural contract with KSH) for PS and FWPS | 10            | - Proceed to award RW&FF steel structure erection given TG4 stage (13/07/26 – Closed) @Guillaume Camerini / Comment: KSH has signed the contract. STEGRA's signature is urgently needed to maintain the fabrication schedule. At the KOM, KSH stressed that contract execution and advance payment are required to start material procurement on time.                                                                                                                                                                                             | 10              |
| B1.BOP.R391 | Engineering       | MHST - Delay in foundation design for MHS                                                                                           | 10            | - Identify contracting strategy for MHS system with a separate call for civil works (31/07/26 – Open) @Ahmed Elroba / Comment: Once the bidders are selected, the next step will be to negotiate the split between the engineering scope and the supply and installation scope. The shortlist is expected to be issued in Week 28<br>- Determine a worst-case max load for MHS foundations (as a back-up plan) (18/07/26 – Open) @Katherine Lopez.<br>- Idom to confirm duration required for piling activities (31/08/26 – Open) @Katherine Lopez | 6               |
| B1.BOP.R513 | Supply Chain FWRW | M&P contract may not be awarded in time for PS (Pumping Management Station) and FWPS                                                | 20            | - Obtain approval to award contract (30/06/26 – Closed) @Chris Van den Berg / Comment: Follow-up requests were sent to Ruhrpumpen Germany and Sulzer for their outstanding proposals. RP confirmed an updated proposal is to be submitted on W28, while Sulzer remains out of office until 03-Aug. Commitment 0799 has been uploaded to ACC for Stegra's review and approval.                                                                                                                                                                      | 20              |

*\*\*\* Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.*




100 MW SUBSTATION


IC01 COMPLETED - 100%



PIPE BRIDGE (Target W35)



NPB-511 (Target W37)



- BLOCKERS

RESPONSIBLE
- PB EARTHING DELAYS ON INSTALLATION, INSPECTION & TESTING → FERRMIX

Siemens CR approval pending → STEGRA/IDOM

4

Milestone

3

High priority

W33

Target

Oct

NIWA on site

## Status by Milestone

|   |                                                                                                                                                                               | Progress                   | Priority / target* |
|---|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------|--------------------|
| 1 | <b>Permanent RW pipes around RW Chamber</b><br>Approved commitment since 11 May by STEGRA PM; no action taken from GRK                                                        | <div><div></div></div> 50% | High<br>W33        |
| 2 | <b>Temporary spool + RW tank inlet</b><br>CR-04387 raised 14 May. Commercial agreement still open. Since May, GRK only submitted price proposal on one occasion.              | <div><div></div></div> 0%  | High<br>W31        |
| 3 | <b>Temporary lines TWTP → ASP</b><br>CR-4359 raised 5 May for connection to ASP. Commercial agreement still open. Since May, GRK only submitted price proposal in 2occasions. | <div><div></div></div> 95% | High<br>W30        |
| 4 | <b>RW tank watertightness test</b><br>Test done W26. Test failed. C3C to come W32 to repair.                                                                                  | <div><div></div></div> 90% | Low<br>W33         |

\*Targets can be achieved only if blockers are resolved this week.

## BLOCKERS / CONTRAINS

- 1

**Commercial action to GRK**  
Apply pressure / penalty if no action is taken
- 2

**CR Review resources**  
Add resources to reduce CR review time. Average review time in ACC 70 days
- 3


**Strategic route GRK TEMP or NIWA**  
Strategic Decision Required: Proceed with the temporary water solution or transition to the permanent solution. NIWA to install → milestone 2 and 3. NIWA starts in October and finalize January as per contractual schedule



BOP | IDOM Level 1

Schedule

Progress

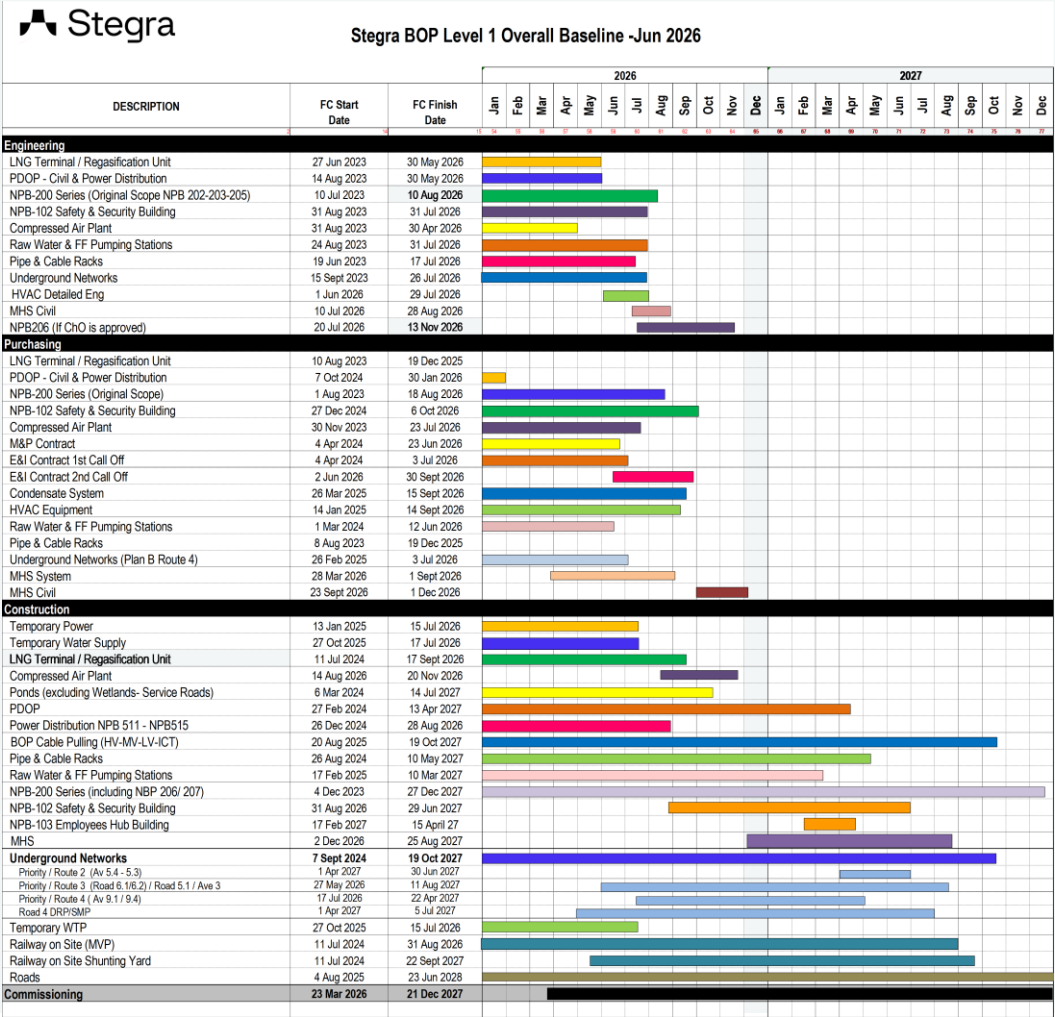


June 2026 Will be Updated next week


# BOP | IDOM Summary – Activities and Progress

## Progress

| Overall Progress                                        | W28-26 (Last W)<br>06/07-11/07 |                           |        |                   |                     | W29-26 (Current W)<br>13/07-18/07 |        |                   | 6-month key Waypoints                                 |              |               |
|---------------------------------------------------------|--------------------------------|---------------------------|--------|-------------------|---------------------|-----------------------------------|--------|-------------------|-------------------------------------------------------|--------------|---------------|
|                                                         | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC     | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan   | Ach. <sup>1</sup> | Key Waypoints                                         | Planned date | Forecast date |
| Engineering                                             | 0,08%                          | 0,19%                     | 0,18%  | 47%               | 43%                 | 0,18%                             | 0,19%  | 95%               | Temporary Water (Ready to Supply)                     | 31 Jul 2026  | 30 Oct 2026   |
|                                                         | 97,06%                         | 97,72%                    | 97,15% | 100%              | 99%                 | 97,34%                            | 97,91% | 99%               | Temporary Power (Ready to Operate)                    | 30 Jul 2026  | 30 Sep 2026   |
| Procurement (TG - Purchasing Process)                   | 0,15%                          | 2,12%                     | 0,15%  | 100%              | 7%                  | 1,33%                             | 2,70%  | 49%               | Power Supply from NPB-511 to ASP                      | 31 Jul 2026  | 30 Sep 2026   |
|                                                         | 67,26%                         | 71,25%                    | 67,27% | 100%              | 94%                 | 68,60%                            | 73,95% | 93%               | Piping Connections - Priority 1 Finish                | 28 Aug 2026  | 28 Aug 2026   |
| Manufacturing<br>(On a Monthly Basis - Monthly Cut Off) | 0,00%                          | 0,00%                     | 0,00%  | 100%              | 100%                | 0,00%                             | 0,00%  | 100%              | P2 – Pipebridge Installed + Piping Connections Finish | 23 Oct 2026  | 23 Oct 2026   |
|                                                         | 92,56%                         | 92,56%                    | 92,56% | 100%              | 100%                | 92,56%                            | 92,56% | 100%              | P5 – Pipebridge Installed + Piping Connections Finish | 28 Aug 2026  | 28 Aug 2026   |
| Construction                                            | 0,36%                          | 0,40%                     | 0,50%  | 72%               | 90%                 | 1,07%                             | 0,38%  | 284%              | P4 – Pipebridge Installed + Piping Connections Finish | 19 Nov 2026  | 27 Nov 2026   |
|                                                         | 50,74%                         | 52,32%                    | 50,94% | 100%              | 97%                 | 52,01%                            | 52,70% | 99%               | Priority 1 UG piping installation completion          | 17 Jul 2026  | 30 Sep 2026   |
| Overall                                                 | 0,22%                          | 0,33%                     | 0,32%  | 71%               | 69%                 | 0,70%                             | 0,33%  | 209%              | Electrical Works by STS Start                         | 06 Jul 2026  | 20 Jul 2026   |
|                                                         | 67,04%                         | 68,18%                    | 67,17% | 100%              | 98%                 | 67,87%                            | 68,51% | 99%               | Railway Groundworks Crossings Start                   | 15 Jun 2026  | 20 Jul 2026   |

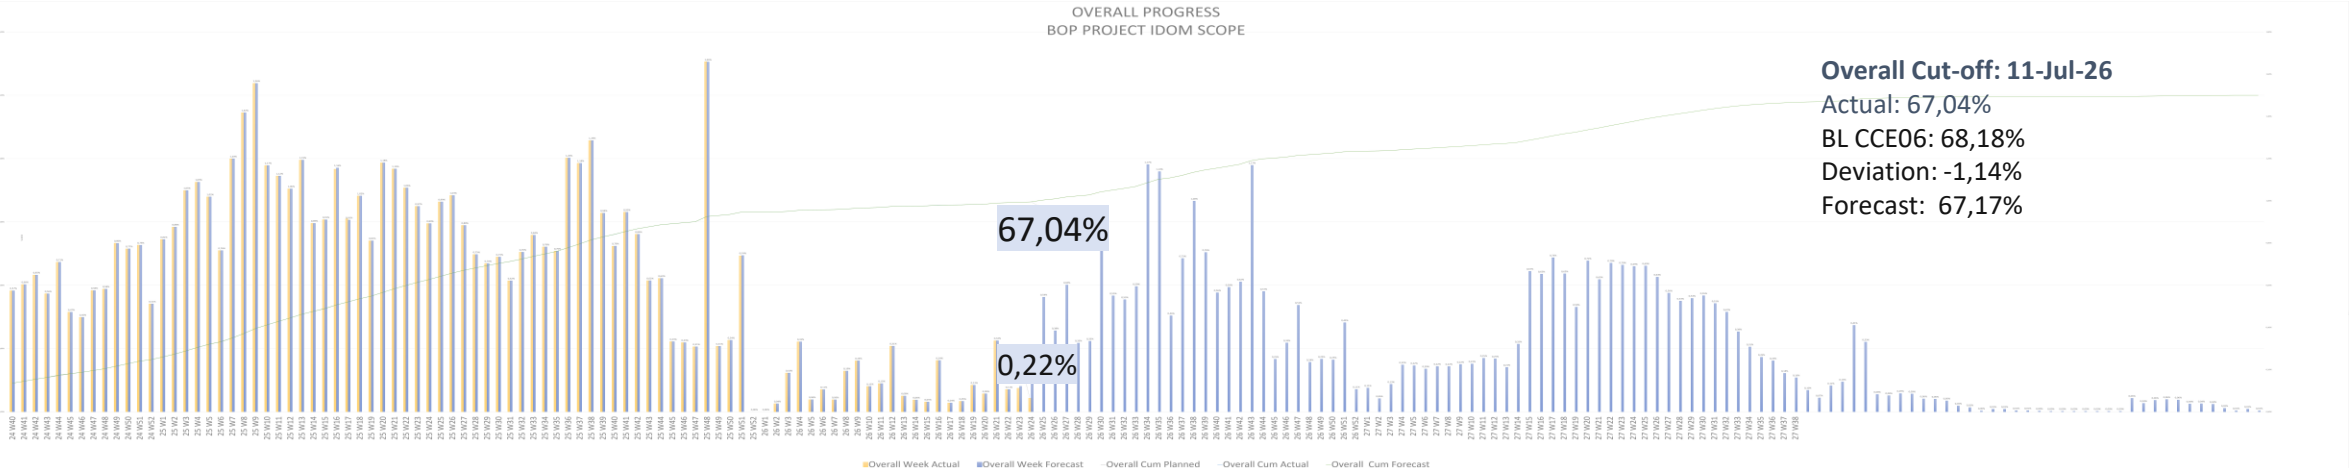

# BOP - 6 Weeks Look Ahead

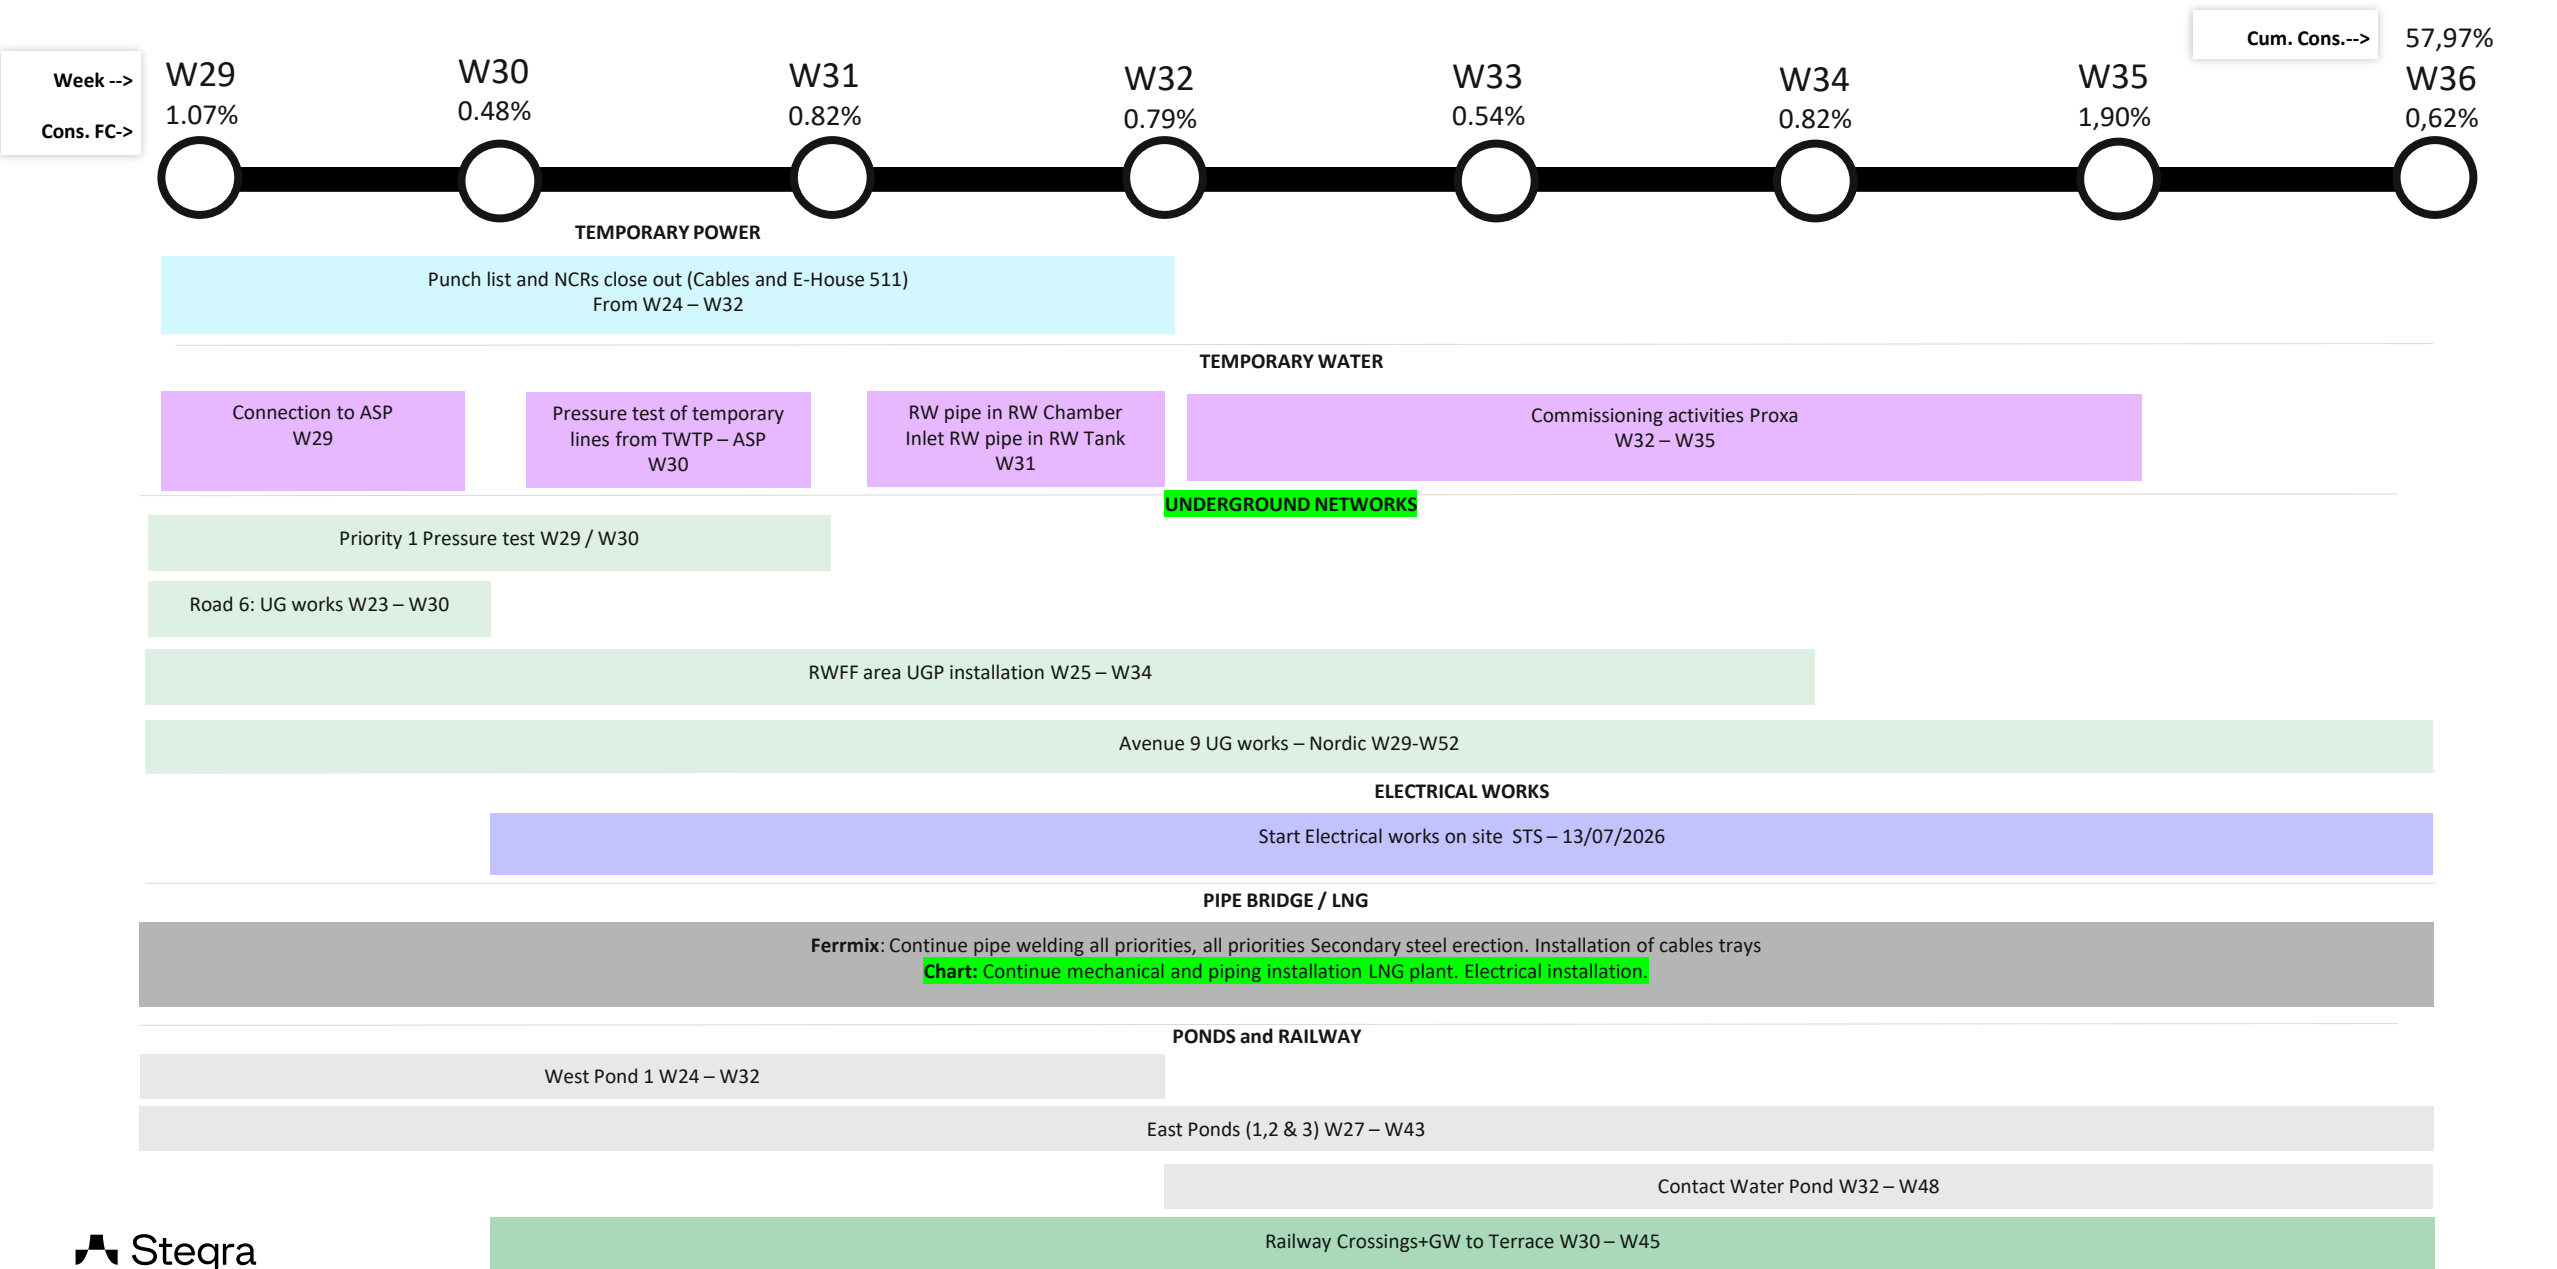

# BOP | IDOM Summary – Activities and Progress -100 days look ahead

W28

## Main deviations and mitigating actions

| Discip | Red Activity                                                      | Due date | Mitigation Action                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |
|--------|-------------------------------------------------------------------|----------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Proc   | Civil Works in RW-FF area + RW chamber + NPB-515 + DC1 – Retender | W26      | • Call-off #1: Signed. Stegra will share the signed contract with Nordic.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
| Proc   | LNG Civil Works - Retender                                        | W27      | • Call-off #2: pending last version of A7 from Nordic and final version of TG4 by IDOM, under revision after some new inclusion. Stegra is progressing with Budget Approval and PGB (W28). In parallel, IDOM is finalizing the review of the appendices to proceed as soon as approval is confirmed.                                                                                                                                                                                                                                                                                         |
| Proc   | PB & Air Compressor found. - Retender                             | W27      | • Call-off #3: pending the quotation from Nordic and TG4 by IDOM to be submitted in W26.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |
| Proc   | UG Piping Avenue 9+6                                              | W27      | • Nordic to submit the last version of A1 (W27) and Nordic and Stegra to confirm all the contract documentation already shared by IDOM. Review is ongoing, will be ready to move to Omega for the formal approval process. No winter costs will be allowed and no additional cost for 2nd sift after agreement.                                                                                                                                                                                                                                                                              |
| Proc   | E&I Call-Off 1                                                    | W27      | • STS to submit the final version of A5 and A7, and IDOM final version of A1, all the contract documents to be shared in W27. Ongoing.                                                                                                                                                                                                                                                                                                                                                                                                                                                       |
| Proc   | GW commitments                                                    | W26      | • East ponds, Contact water pond and GW+crossings railway are executed. Ponds KoM held in W25. GW workshop w31.<br>• East ditch. Status: Acknowledge. Pending to be executed. Warning! This is a predecessor for ROS GW in sections 4 and 5.                                                                                                                                                                                                                                                                                                                                                 |
| Eng    | Sweco                                                             | W30      | • Road design packages expected before summer break will come after w36. No clear delivery dates available.<br>• Rail Memo 20. Received only partially on 03/07. Missing service roads update and GW deliverables. Railway memo 21 will come after summer break.<br>• Earthing. Ongoing discussions to clarify the scope. In parallel, Sweco is analyzing the existing information and preparing the team to start the production.<br>• Fencing. Sweco will raise two CR: CR-4433 for BOP/Steel Mill and a new one for HMP. Stegra (&IDOM's) to provide feedback on the 4,250 hours for BOP. |
| Eng    | Hydrogen pipeline crossing (Railway Section 4A)                   | W52      | • Hydrogen pipeline crossing. Alternative 3 is the chosen solution. Sweco raised CR-04439 for the Geotechnical investigations required for the Hydrogen pipebridge design, CR-04441 for the culvert under the railway (w38 expected the IFC if the CO is ready by w33) and they will raise a third CR for the design works for the civil work design on the pressure berm.                                                                                                                                                                                                                   |
| Con    | Field Change Requests                                             | W31      | • Stegra/IDOM to define the procedure on site for Filed Change Request and the Red-marked drawings, to establish how to include changes in the design due to construction reasons.                                                                                                                                                                                                                                                                                                                                                                                                           |
| Con    | PB Piping Connections + Pending Fittings                          | W35      | • WK28 2026- <b>20 welders</b> working vs 20 forecast. 660 Forecast inches/week, Actual 709 inches/week                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |
| Con    | GRK - Temporary power and                                         | W35      | • RW: temporary line in RW chamber CR discussion ongoing, RW tank filling pipe and overflow system Material delivery Week 28, temporary pipes to TWTP to                                                                                                                                                                                                                                                                                                                                                                                                                                     |



## Last Week Key Achievements


- ✓ **Significant progress:** Piping welding all Priority: 709 Inches welded and 4% progress achieved during this week. Total 13.127 inches out of 20.841 welded done **63% progress achieved.**
- ✓ LNG:3 pressure tests performed
- ✓ 3462 m cables pulled
- ✓ Diesel generator installed
- ✓ Av 9.5 Backfilling completed
- ✓ East ponds excavated 6900 m3 out of 71000m3 - **10% progress achieved**

Distribution (Power) – Activities and Progress

Progress

| PDOP Progress                  | W28-26 (Last W)<br>06/07-11/07 |                           |         |                   |                     | W29-26 (Current W)<br>13/07-18/07 |         |                   |
|--------------------------------|--------------------------------|---------------------------|---------|-------------------|---------------------|-----------------------------------|---------|-------------------|
|                                | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC      | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan    | Ach. <sup>1</sup> |
| Engineering (MDR)              | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                                | 100,00%                        | 100,00%                   | 100,00% | 100%              | 100%                | 100,00%                           | 100,00% | 100%              |
| Procurement (TG)               | 0,11%                          | 0,00%                     | 0,11%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                                | 99,25%                         | 99,25%                    | 99,25%  | 100%              | 100%                | 99,25%                            | 99,25%  | 100%              |
| Construction - PDOP            | 0,09%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                                | 92,82%                         | 92,68%                    | 92,56%  | 100%              | 100%                | 92,56%                            | 92,68%  | 100%              |
| Construction - NPB 511         | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                                | 84,69%                         | 84,69%                    | 84,69%  | 100%              | 100%                | 84,69%                            | 84,69%  | 100%              |
|                                |                                |                           |         |                   |                     |                                   |         |                   |
| Temporary Power                | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC      | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan    | Ach. <sup>1</sup> |
| Construction - Temporary Power | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 3,00%   | 0%                |
|                                | 99,00%                         | 99,00%                    | 99,00%  | 100%              | 100%                | 99,00%                            | 98,00%  | 101%              |

| Main deviations and mitigating actions |                                                      |                                                                               |
|----------------------------------------|------------------------------------------------------|-------------------------------------------------------------------------------|
| Discipline                             | RED Activity                                         | Mitigating action                                                             |
| Con                                    | Actemium: Delay PB and NPB511 UG earthing completion | Pending contractual agreement Stegra/Actemium                                 |
| Con                                    | SIEMENS: Delay to finalising NPB511 punch items      | Siemens mobilization to site (expect WK33). 1 week is needed to close punches |

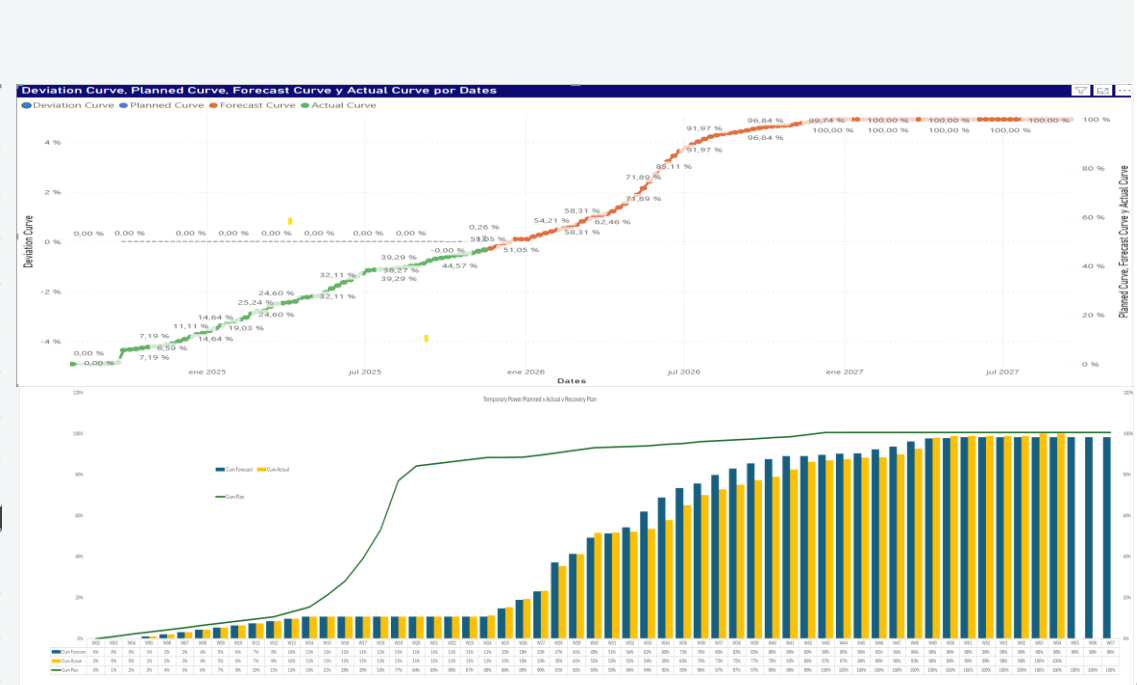

| 6-month key Waypoints            |              |               |
|----------------------------------|--------------|---------------|
| Key Waypoints                    | Planned date | Forecast date |
| Mechanical Completion Temp Power | 30 Jul 2026  | 30 Sep 2026   |


# BOP | Gas LNG – Activities and Progress

## Progress

| LNG Progress      | W28-26 (Last W)<br>06/07-11/07 |                           |         |                   |                     | W29-26 (Current W)<br>13/07-18/07 |         |                   |
|-------------------|--------------------------------|---------------------------|---------|-------------------|---------------------|-----------------------------------|---------|-------------------|
|                   | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC      | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan    | Ach. <sup>1</sup> |
| Engineering (MDR) | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                   | 100,00%                        | 100,00%                   | 100,00% | 100%              | 100%                | 100,00%                           | 100,00% | 100%              |
| Procurement (TG)  | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                   | 100,00%                        | 100,00%                   | 100,00% | 100%              | 100%                | 100,00%                           | 100,00% | 100%              |
| Construction -LNG | 2,87%                          | 2,12%                     | 3,69%   | 78%               | 136%                | 3,73%                             | 1,86%   | 200%              |
|                   | 87,02%                         | 90,13%                    | 87,97%  | 99%               | 97%                 | 91,70%                            | 91,99%  | 100%              |

## Main deviations and mitigating actions

| Discipline | RED Activity                                               | Mitigating action |
|------------|------------------------------------------------------------|-------------------|
| MEC        | MV Transformer delivery date postponed to end of September | Expediting action |

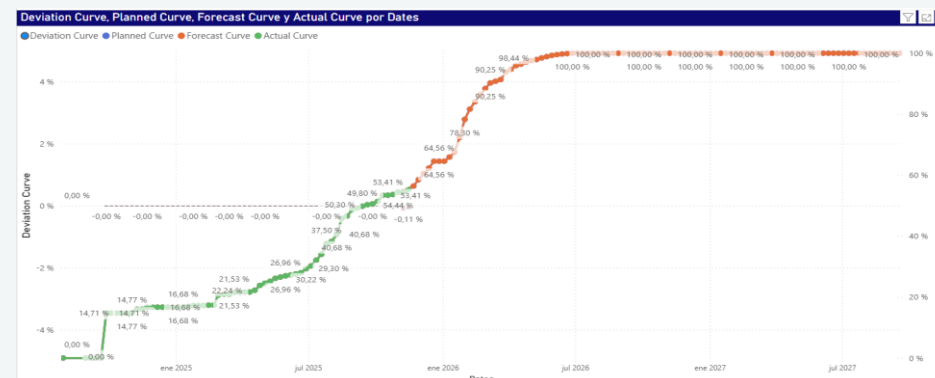

## 6-month key Waypoints

| Key Waypoints                                | Planned date | Forecast date |
|----------------------------------------------|--------------|---------------|
| Civil Works complete (remaining civil works) | 17 July 2026 | 08 Oct 2026   |
| Commence Control System Cabinet installation | 08 Jul 2026  | 10 Aug 2026   |

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern  
Behind




# BOP | Distribution (Pipe Bridges) – Activities and Progress

## Progress

### PB & UGP Progress

|                                | W28-26 (Last W)<br>06/07-11/07 |                           |         |                   |                     | W29-26 (Current W)<br>13/07-18/07 |         |                   |
|--------------------------------|--------------------------------|---------------------------|---------|-------------------|---------------------|-----------------------------------|---------|-------------------|
|                                | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC      | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan    | Ach. <sup>1</sup> |
| Engineering (MDR)              | 0,18%                          | 0,18%                     | 0,18%   | 100%              | 100%                | 0,18%                             | 0,18%   | 100%              |
|                                | 99,67%                         | 99,67%                    | 99,67%  | 100%              | 100%                | 99,85%                            | 99,85%  | 100%              |
| Procurement (TG)               | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                                | 100,00%                        | 100,00%                   | 100,00% | 100%              | 100%                | 100,00%                           | 100,00% | 100%              |
| Pipe Bridge (Foundation+Steel) | 0,56%                          | 0,12%                     | 0,56%   | 100%              | 480%                | 0,44%                             | 0,31%   | 144%              |
|                                | 84,34%                         | 83,68%                    | 84,52%  | 100%              | 101%                | 84,96%                            | 83,99%  | 101%              |

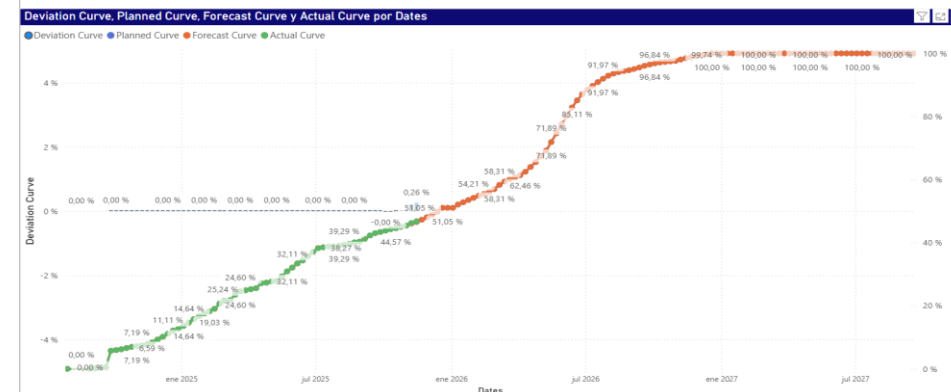

### 6-month key Waypoints

| Key Waypoints                          | Planned date | Forecast date |
|----------------------------------------|--------------|---------------|
| Piping Connections - Priority 1 Finish | 28 Aug 2026  | 28 Aug 2026   |
| Piping completion Priority 1 Finish    | 23 Oct 2026  | 23 Oct 2026   |
| Pipe rack Modules - Priority 4 Finish  | 24 Aug 2026  | 01 Sep 2026   |
| Pipe rack Modules - Priority 3 Finish  | 25 Sep 2026  | 09 Oct 2026   |
| Pipe rack Columns - Priority 4 Finish  | 20 Aug 2026  | 27Aug 2026    |

### Main deviations and mitigating actions

| Discipline | RED Activity                                                                                                        | Mitigating action                                                                                |
|------------|---------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------|
| Con        | PB- Piping connections + pending fittings                                                                           | WK28 2026- 20 welders working vs 20 forecast. 660 Forecast inches/week, Actual 709 inches/week   |
| Con        | PB02. Foundation not possible due to works by Mc Dermott                                                            | McDermott piping pending. Focus on other areas/ Award civil works contractor to start works.     |
| Con        | PB03. Foundation in the WTP2 area no possible to works by Mc Dermott                                                | Confirmation from Stegra to proceed with execution/ Award civil works contractor to start works. |
| Con        | Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott. | Foundations can be start when McDermott release the area                                         |


Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
 ■ Behind

# BOP | Distribution (UG piping) – Activities and Progress

## Progress

| PB & UGP Progress    | W28-26 (Last W)<br>06/07-11/07 |                           |         |                   |                     | W29-26 (Current W)<br>13/07-18/07 |         |                   |
|----------------------|--------------------------------|---------------------------|---------|-------------------|---------------------|-----------------------------------|---------|-------------------|
|                      | ACT                            | Plan<br>(BL CCE06<br>TBA) | FC      | Ach.<br>(Act./FC) | Ach.<br>(Act./Plan) | FC                                | Plan    | Ach. <sup>1</sup> |
| Engineering (MDR)    | 0,18%                          | 0,18%                     | 0,18%   | 100%              | 100%                | 0,18%                             | 0,18%   | 100%              |
|                      | 99,67%                         | 99,67%                    | 99,67%  | 100%              | 100%                | 99,85%                            | 99,85%  | 100%              |
| Procurement (TG)     | 0,00%                          | 0,00%                     | 0,00%   | 100%              | 100%                | 0,00%                             | 0,00%   | 100%              |
|                      | 100,00%                        | 100,00%                   | 100,00% | 100%              | 100%                | 100,00%                           | 100,00% | 100%              |
| UG Piping (Schedule) | 0,17%                          | 0,66%                     | 0,54%   | 31%               | 26%                 | 0,74%                             | 0,61%   | 122%              |
|                      | 17,55%                         | 18,30%                    | 17,92%  | 98%               | 96%                 | 18,66%                            | 18,91%  | 99%               |

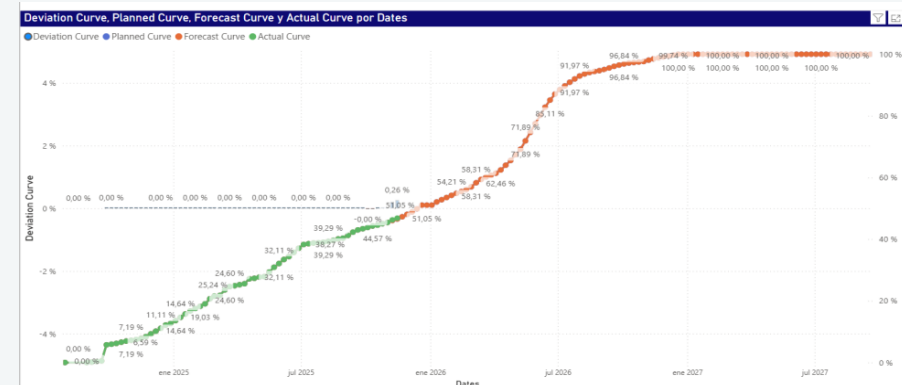

## 6-month key Waypoints

| Key Waypoints                        | Planned date | Forecast date |
|--------------------------------------|--------------|---------------|
| UGP – Route 0 testing complete       | 26 Jun 26    | 26 Jul 26     |
| UGP – Route 1 Completion Av. 9.5     | 31 Jul 26    | 31 Jul 26     |
| UGP – Route 2 Commencement           | 01 Apr 27    | 01 Apr 27     |
| UGP – Route 4 Commencement (Rd. 9.4) | 17 Jul 26    | 17 Jul 26     |
| UGP – Route 5 Completion             | 11 Nov 26    | 11 Nov 26     |
| UGP – RW & FW Completion             | 06 Oct 26    | 06 Oct 26     |

## Main deviations and mitigating actions

| Discipline | RED Activity                                                   | Mitigating action                             |
|------------|----------------------------------------------------------------|-----------------------------------------------|
| Piping     | Priority 0 (Potable water tank area) UG piping to be connected | Fire hydrant to be relocated by site services |
| QAQC/Proc  | Pressure tests in Priority 1 to be done                        | Test pack approval and CO signature           |
| QAQC/Eng   | Road 6 - Backfilling                                           | ITP to be approved                            |

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue


Risk / Concern

Behind

# BOP | Buildings & Other IDOM – Activities and Progress

## Progress

| Buildings & Others Progress | W28-26 (Last W)<br>06/07-11/07 |                     |        |                |                  | W29-26 (Current W)<br>13/07-18/07 |        |                   |
|-----------------------------|--------------------------------|---------------------|--------|----------------|------------------|-----------------------------------|--------|-------------------|
|                             | ACT                            | Plan (BL CCE06 TBA) | FC     | Ach. (Act./FC) | Ach. (Act./Plan) | FC                                | Plan   | Ach. <sup>1</sup> |
| Engineering (MDR)           | 0,05%                          | 0,05%               | 0,05%  | 100%           | 100%             | 0,04%                             | 0,04%  | 100%              |
|                             | 97,23%                         | 97,23%              | 97,23% | 100%           | 100%             | 97,27%                            | 97,27% | 100%              |
| Procurement (TG)            | 0,54%                          | 1,20%               | 0,54%  | 100%           | 45%              | 0,74%                             | 0,46%  | 161%              |
|                             | 77,22%                         | 81,36%              | 77,27% | 100%           | 95%              | 77,96%                            | 81,82% | 95%               |
| Construction - RWPS & FF    | 0,00%                          | 0,00%               | 0,00%  | 100%           | 100%             | 0,07%                             | 0,07%  | 99%               |
|                             | 74,65%                         | 74,65%              | 74,79% | 100%           | 100%             | 74,72%                            | 74,72% | 100%              |
| Construction - NPB 200      | 0,00%                          | 0,00%               | 0,00%  | 100%           | 100%             | 0,00%                             | 0,00%  | 100%              |
|                             | 55,95%                         | 55,95%              | 55,95% | 100%           | 100%             | 55,95%                            | 55,95% | 100%              |

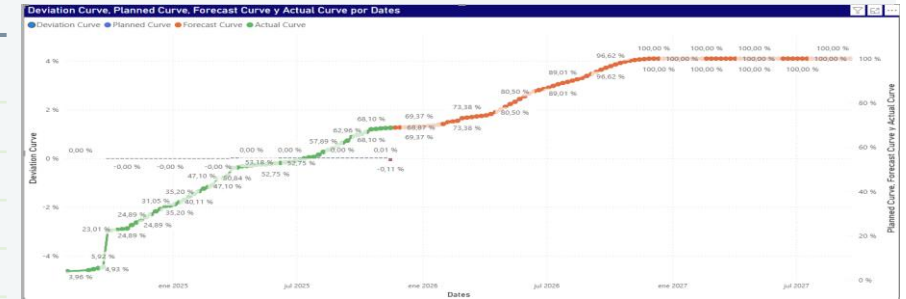

## 6-month key Waypoints

| Key Waypoints                                   | Planned date | Forecast date |
|-------------------------------------------------|--------------|---------------|
| Commence RW Pumping station building erection   | 10 Sep 2026  | 10 Sep 2026   |
| Commence FF Pumping station civil works         | 14 Sep 2026  | 14 Sep 2026   |
| Commence RW Pumping station equip. installation | 30 Nov 2026  | 30 Nov 2026   |
| Commence FF Pumping station building erection   | 19 Oct 2026  | 19 Oct 2026   |
| Commence NPB205 civil work                      | 19 Aug 2026  | 19 Aug 2026   |
| Commence NPB102 civil work                      | 31 Aug 2026  | 31 Aug 2026   |
| Temporary WTP start operation                   | 31 Jul 2026  | 30 Oct 2026   |

## Main deviations and mitigating actions


| Discipline | RED Activity                                                                                                                                                                                                            | Mitigating action                                                                                                                                                   |
|------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Eng        | NPB 207 – Crane Maintenance Workshop: Meeting conducted with STEGRA. Progress has been made but there are still open points.                                                                                            | Confirm whether building is required, define procurement strategy and utilities needs                                                                               |
|            | NPB 202 – Building on hold due to ongoing discussions concerning storage capacity and need for sprinkler system                                                                                                         | Fire extinguishing system needed<br>Pending building layout and rack distribution<br>Chemical storage room layout, fire resistance requirements, containment method |
|            | NPB 203 – Refractory Warehouse                                                                                                                                                                                          | Confirm design change insulated vs non-insulated building concept                                                                                                   |
|            | Chemical Container – oils and lubricants and Supplier container outside NPB 202: STEGRA engineering has retained three alternatives                                                                                     | Stegra to communicate power needed and any other utility depending on network under IDOM scope of design                                                            |
|            | Review of fire detection and alarm and sprinkler system drawing by certified engineer - Pending to have a plan from certified engineer to complete the review of the BOP documentation. No review has been started yet. | Stegra to expedite this process to avoid major impacts to procurement, installation...                                                                              |
| Con        | RW Chamber temporary spool and RW Tank inlet pipe                                                                                                                                                                       | CR to be approved                                                                                                                                                   |

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue 
 ■ Risk / Concern 
 ■ Behind

# BOP | Engineering

## Progress

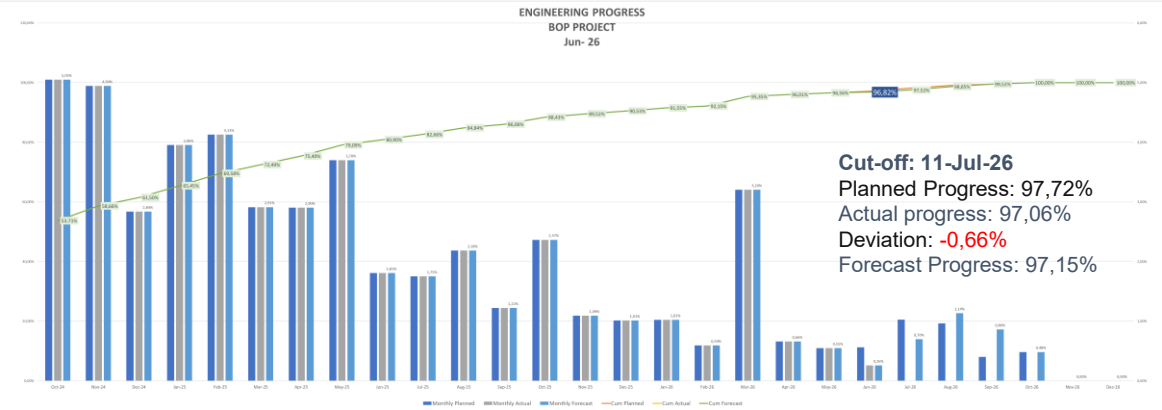

## Plan deviations

| RED Activity                               | Plan date | Fcst date | CP impact | Mitigating action                                                                                                                          | Who                     | When |
|--------------------------------------------|-----------|-----------|-----------|--------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|------|
| UG system PB02 and other areas excav. dwg. | Jun-26    | Jun-26    | Y         | <ul style="list-style-type: none"><li>Monitoring Sweco contractual commitments</li><li>Splitting UG works in several contractors</li></ul> | Sweco<br>IDOM<br>Stegra |      |


## Key issues/potential risks and mitigation actions

| Key issue / potential risk                                                                            | Mitigation action                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | Owner       | Due date | Status | Progress |
|-------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|----------|--------|----------|
| IDOM Integration Drawings & Excavation models UGP                                                     | IDOM has communicated to Sweco the deadlines by which they must provide the inputs for UGP design of all areas pending combined drawings and excavation models.<br><br>Upcoming deadlines for Sweco: <ul style="list-style-type: none"><li>CSP-WTP2 Area (Av. 6.0-6.1): 08-05-2026 (<b>Delivered</b>)</li><li>Priority 4 (Av. 9.3-9.4): 13-05-2026 (<b>Delivered</b>)</li><li>Priority 3 zone D (Av. 2.0): 20-05-2026 (<b>Delivered</b>)</li><li>Priority 5 (Road 7.5): 20-05-2026 (<b>Delivered</b>)</li><li>Finishing Area: 29-05-2026 (<b>Delivered</b>)</li><li>DRP-SMP area (Road 4): 26-06-2026 → <b>Sweco to deliver drawings in September. 2D and 3D models were provided in w27</b></li><li>DRP-Scrap yard area (Av. 9.1-9.2): 17-06-2026 (<b>Delivered</b>)</li></ul> | IDOM/Stegra | Sep-26   | Open   | Ongoing  |
| Underground Piping Priority 0<br>Underground Piping Priority 4<br>Underground Piping Road 5.1 and 5.2 | <ul style="list-style-type: none"><li>Prio 0: Final revision removing holds in the roundabout in Av. 1 is moved to September.</li><li><b>Prio 4: Sweco provided 3D model and 2D CAD in w27 and delivered the IFC pdf drawings in Omega in w28. IDOM is progressing with combined UGP IFC drawings</b></li><li>Road 5.1 and 5.2: IDOM and Sweco UGP IFC drawings have holds from pipes going to NPB 207 – the design for this building is not developed. IDOM shall resubmit the IFC for combined drawings for Road 5. Sweco design is available.</li></ul>                                                                                                                                                                                                                      | IDOM/Stegra | Sep-26   | Open   | Ongoing  |

Achievement    Actual / Plan OR Forecast / Plan as percentage

On track / no issue     Risk / Concern  
 Behind

# BOP | Sweco Engineering Management (IDOM EPCM – SWECO)

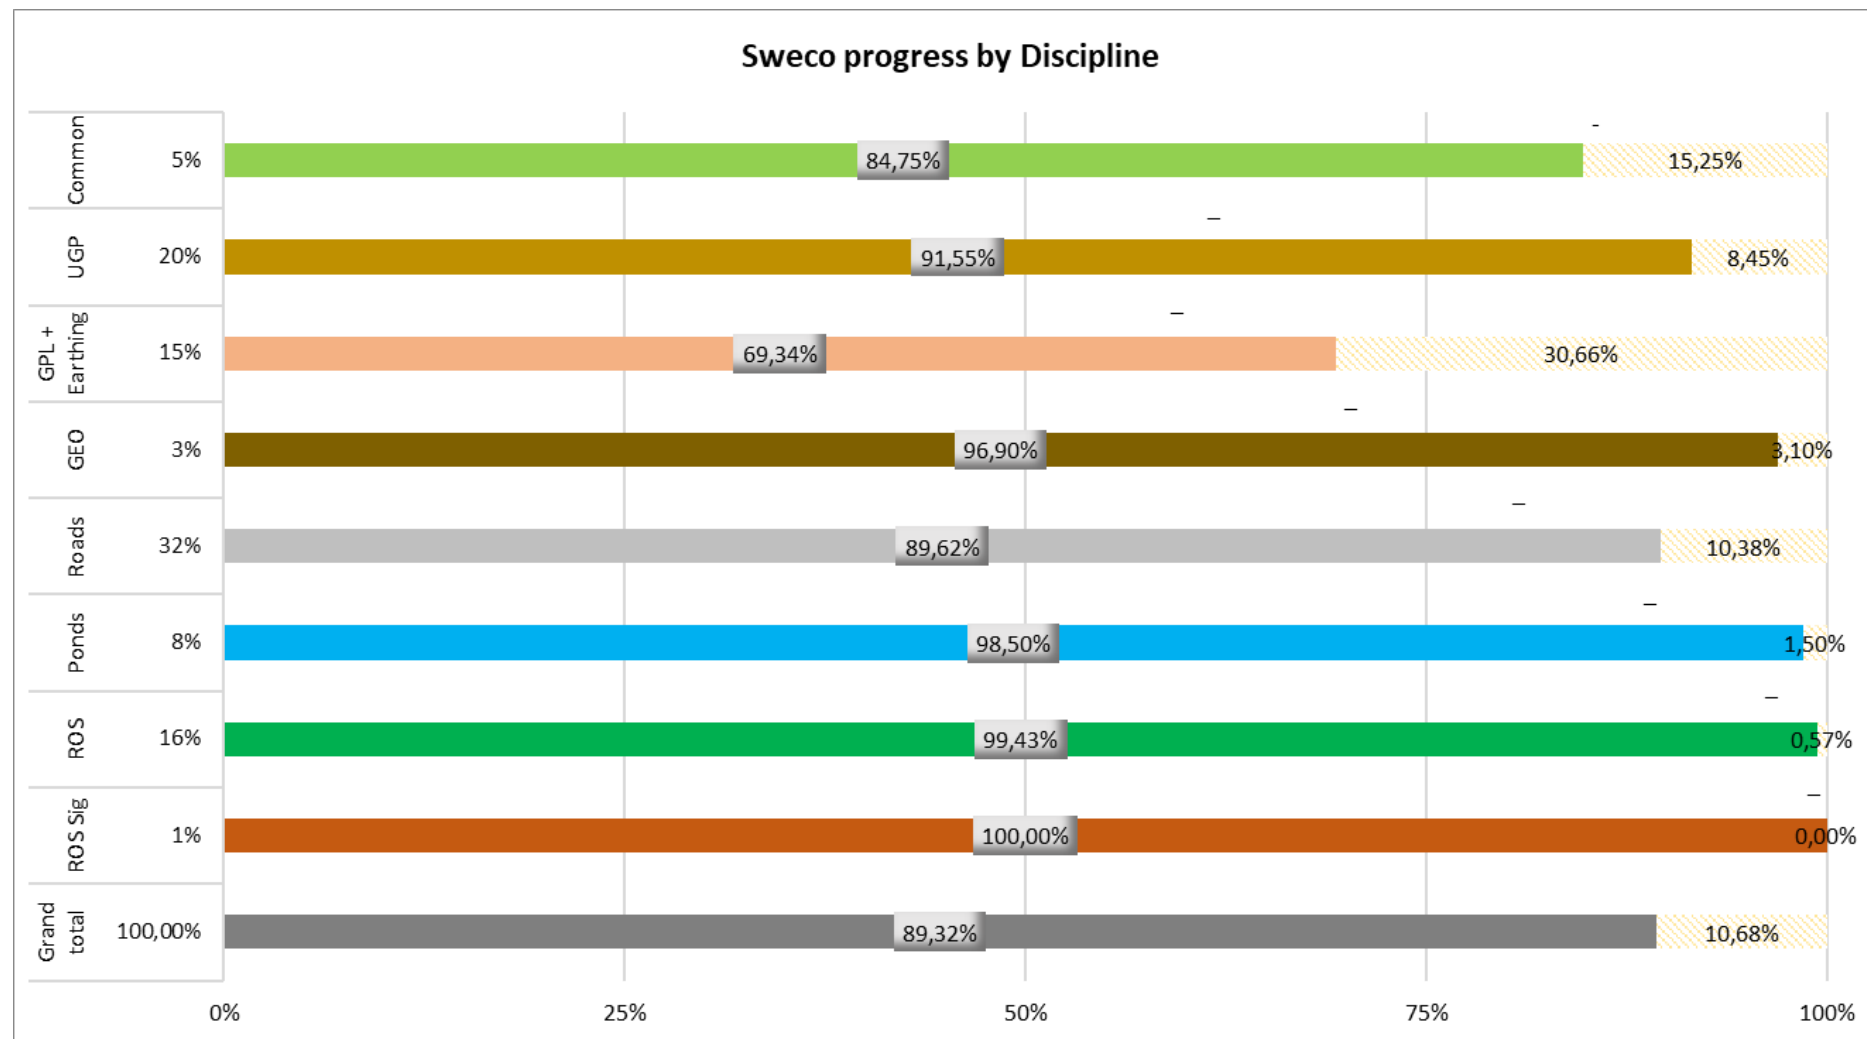

Achievement    Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue    ■ Risk / Concern  
■ Behind

# BOP | Sweco UGP Construction Readiness


## Sweco UGP

| Sweco |                                |                  |                 |            |            |            |                                                                                                                                                                                                                                                                                                               |
|-------|--------------------------------|------------------|-----------------|------------|------------|------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Phase | Package                        | Construction Sta | Construction En | IFR        | IFC        | BoQ        | Comments                                                                                                                                                                                                                                                                                                      |
| 1     | Road 7.1 (Priority 1)          | abr-26           | ago-26          | -          | 23/01/2026 | 14/11/2025 | Package 1 BoQ (no dedicated BoQ for Priority 5)                                                                                                                                                                                                                                                               |
| 1     | Av. 9.5 (Priority 1)           | abr-26           | jul-26          | -          | 21/01/2025 | 14/11/2025 | Package 1 BoQ (no dedicated BoQ for Priority 5)                                                                                                                                                                                                                                                               |
| 1     | Road 7.5 + Road 9 (Priority 5) | abr-26           | jul-26          | -          | 10/12/2025 | 14/11/2025 | - There is an area on-hold for the pipes going into STM cold mill and the railway area (BOD-SIN-UPB-CIV-DRWGA-00015)<br>- Package 1 BoQ (no dedicated BoQ for Priority 5)                                                                                                                                     |
| 1     | Road 6.2                       | abr-26           | jul-26          | -          | 11/02/2026 | 17/04/2026 | Package 2 BoQ is already available in IFC (Dedicated BoQ for Road 6 delivery date is indicated)                                                                                                                                                                                                               |
| 1     | RW+FW tanks area + Road 8      | abr-26           | ago-26          | -          | 23/01/2025 | 18/03/2026 | Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads                                                                                                                                                                                                                   |
| 1     | Scrap road 1                   | abr-26           | ago-26          | -          | 21/01/2026 | 08/05/2026 | Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads                                                                                                                                                                                                                   |
| 1     | Av. 9.3-9.4 + Av. 6.0          | may-26           | -               | 21/01/2026 | 12/05/2026 | 08/05/2026 | - IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due clashes with McDermott in Av. 9.3 (BOD-SIN-UPB-CIV-DRWGA-00023 + BOD-SIN-UPB-CIV-DRWGA-00027)<br>- Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 (Av. 6 not included) |
| 2     | Road 5.1                       | jul-26           | oct-26          | -          | 05/12/2025 | 26/03/2026 | - Area on-hold due to missing TOPs to NPB207 (BOD-SIN-UPB-CIV-DRWGA-00022)<br>- Package 5.1 BoQ includes all of Road 5 (no dedicated BoQ for Road 5.1)                                                                                                                                                        |
| 2     | Av. 9.1-9.2                    | jul-26           | mar-27          | 16/12/2026 | 08/07/2026 | 08/05/2026 | - IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due to the slope designed in Av. 9.1 (east of DRP) (BOD-SIN-UPB-CIV-DRWGA-00027)<br>- Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4                                       |
| 2     | ELA01 & PDOP                   | jul-26           | oct-26          | -          | 21/01/2026 | 08/05/2026 | Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads                                                                                                                                                                                                                   |
| 2     | Parking 1 area                 | jul-26           | oct-26          | 23/01/2026 | 29/05/2026 | 08/07/2026 | - IFC drawings in Omega are available, however there will be a new revision due to UGP being on-hold in this area (BOD-SIN-UPB-CIV-DRWGA-00017 + BOD-SIN-UPB-CIV-DRWGA-00013)<br>- Package 0 (no dedicated BoQ for UGP in Parking 1). BoQ available is in IFR from 30/09/2025                                 |
| 4     | Road 4 + Av. 2.0               | abr-27           | oct-27          | 11/07/2025 | 30/08/2026 | 30/08/2026 | Drawings in Omega are IFC but there will be an additional revision due to multiple adjustments (TOP changes, etc.)                                                                                                                                                                                            |
| 4     | Av. 6                          | abr-27           | oct-27          | 25/03/2026 | 12/05/2026 | 08/05/2026 |                                                                                                                                                                                                                                                                                                               |
| 4     | Av. 5                          | abr-27           | oct-27          | 11/02/2025 | 01/04/2026 | 20/05/2026 | Drawings are IFC in Omega, however there will be another revision due to TOP & design changes due to McD STM                                                                                                                                                                                                  |
| 4     | Av. 4.1                        | abr-27           | ago-27          | -          | 11/02/2026 | 27/05/2026 |                                                                                                                                                                                                                                                                                                               |
| 4     | Av. 3.4                        | abr-27           | ago-27          | -          | 11/02/2026 | 03/06/2026 |                                                                                                                                                                                                                                                                                                               |
| 4     | Av. 3.2 + 3.3 + Road 5.3       | abr-27           | ago-27          | -          | 11/02/2026 | 02/04/2026 |                                                                                                                                                                                                                                                                                                               |



# BOP | Procurement

## Progress

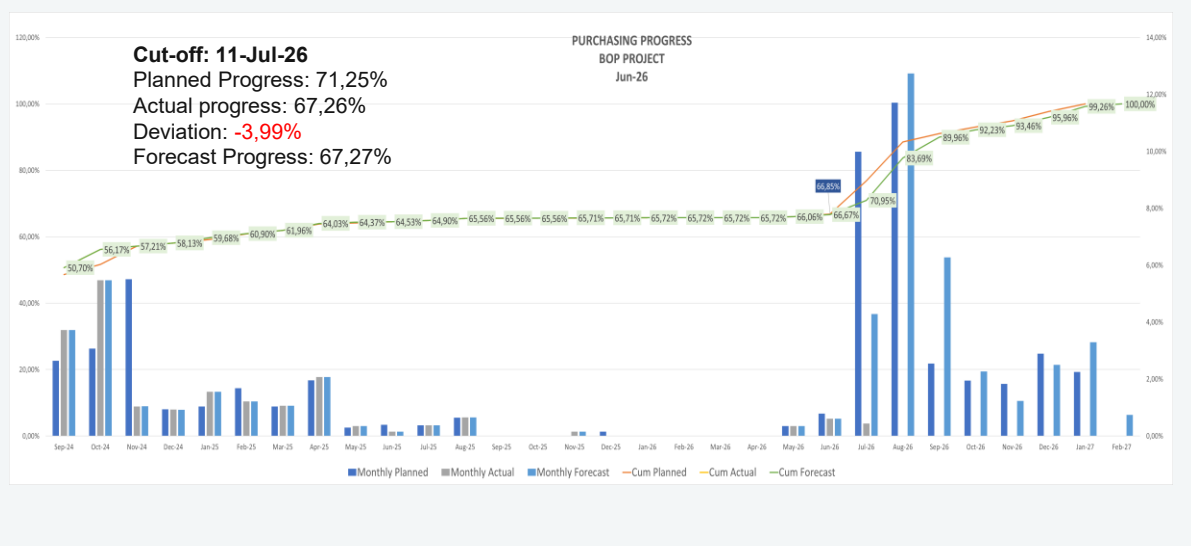

## Plan deviations

| RED Activity                               | Plan date | Fcst date | CP impact? | Mitigating action                                                                                                                                                                                                                                                             | Who            | When |
|--------------------------------------------|-----------|-----------|------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------|------|
| RW + FFPS steel struct. and cladding (ROS) | 05/02/26  | 08/07/26  | Y          | LNTP: Confirmed by KSH<br>Contract: Approved by both parties<br>Approval of TG4 by PGB w19, contract to be signed w21.                                                                                                                                                        | Stegra         | TBC  |
| M&P Contractor (ROS)                       | 19/12/25  | 13/09/26  | Y          | Awaiting NIWA's confirmation or comments on the proposed schedule. IDOM has also shared with NIWA the list of deliverables regarding pre-commissioning, cold and hot commissioning. TG4 PGB approval for w21.                                                                 | Stegra<br>IDOM | TBC  |
| E&I Contractor (ROS)                       | 19/12/25  | 28/08/26  | Y          | Initially, the plan was for the works to begin in June; however, since the approval process for TG4 may take approximately six weeks (GPB), it has been postponed to late June or early July. TG4 will be issued on W16. LOI approved(PGB) w19 and to be shared with STS w20. | Stegra         | TBC  |

## Key issues/potential risks and mitigation actions

| Key issue / potential risk                                                  | Mitigation action                                                                                                                                                                                                                                                                                                                                                                                                                      | Owner | Due date | Status | Progress |
|-----------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------|----------|--------|----------|
| Packages that will be proposed by Stegra-BOP as critical for ramp up (PGB): | <ul style="list-style-type: none"><li>E&amp;I - STS to submit the final version of A5 and A7, and IDOM final version of A1, all the contract documents to be shared in W26.</li><li>UG Piping Av. 9&amp;6: Nordic to submit the last version of A7 and Nordic and Stegra to confirm all the contract documentation already shared by IDOM.</li><li>M&amp;P Package – Contract signed.</li><li>RW&amp;FF SS: Contract signed.</li></ul> |       |          |        |          |

# BOP | Procurement (IDOM)

## Main Packages Status

| PACKAGE NUMBER | ITEMS                                                    | NEXT TG | TG FORECAST | Expected value<br>MMEUR | TG4 forecast date      | Contract signing<br>forecast date | Forecast Arrival on<br>Site |
|----------------|----------------------------------------------------------|---------|-------------|-------------------------|------------------------|-----------------------------------|-----------------------------|
|                |                                                          |         |             |                         |                        |                                   | (ROS forecast)              |
| BOD-BOP-019EA  | Underground Services & Roads<br>Avenue 9.1, 2,3,4 Road 4 | TG4     | 20/05/2026  | 35.9                    | 20/05/2026             | 30/06/2026                        | 01/07/2026                  |
| MISC           | Remaining Civil Works                                    | TG3     | 19/06/2026  |                         | 10/07/2026             | 30/07/2026                        | 30/08/2026                  |
| BOD-BOP-027C   | HVAC engineering for BOP                                 | TG5     | 22/05/2026  | 0.2                     | Approved 05/05/2026    | 15/05/2026                        | 13/08/2026                  |
|                | Engineering as priority                                  |         |             |                         |                        |                                   |                             |
| BOD-BOP-020A   | M&P Contractor                                           | TG4     | 21/04/2026  | 4.3                     | 21/04/2026             | Signed<br>23/06/2026              | 30/08/2026<br>TBC           |
|                |                                                          | (NIWA)  |             |                         |                        |                                   |                             |
| BOD-BOP-020C   | E&I Contractor                                           | TG4     | 15/04/2026  | 32.7                    | 15/04/2026             | 03/07/2026                        | 06/07/2026                  |
|                |                                                          | (STS)   |             |                         |                        |                                   |                             |
| BOD-BOP-051B   | RW and FFPS Steel structure and Cladding                 | TG4     | 30/03/2026  | 0.9                     | Approved<br>11/05/2026 | Signed<br>23/06/2026              | 15/08/2026                  |
|                |                                                          | (KSH)   |             |                         |                        |                                   |                             |
| BOD-BOP-043    | MHS for Slag and DRP by-products                         | TG3     | 29/05/2026  | 13.9                    | 23/06/2026             | 14/07/2026 TBC                    | 01/12/2026                  |

Achievement    Actual / Plan OR Forecast / Plan as percentage

On track / no issue   
  Risk / Concern  
 Behind

# BOP | Pipe Bridge Manufacturing Progress - Ferrmix

Week 28 2026


| PROJECT PHASE   |                          | Priority | P1                       |       | P2                       |       | P3                       |       | P4                       |       | P5                       |       |
|-----------------|--------------------------|----------|--------------------------|-------|--------------------------|-------|--------------------------|-------|--------------------------|-------|--------------------------|-------|
|                 |                          |          | Completed<br>Cummulative | Total | Completed<br>Cummulative | Total | Completed<br>Cummulative | Total | Completed<br>Cummulative | Total | Completed<br>Cummulative | Total |
| Steps           |                          |          |                          |       |                          |       |                          |       |                          |       |                          |       |
| Steel Structure | Assembled column         |          | 45                       | 45    | 11                       | 11    | 64                       | 64    | 20                       | 20    | 6                        | 6     |
|                 | Assembled modules        |          | 67                       | 67    | 10                       | 10    | 59                       | 59    | 37                       | 37    | 8                        | 8     |
|                 | Painted Columns          |          | 45                       | 45    | 11                       | 11    | 64                       | 64    | 20                       | 20    | 6                        | 6     |
|                 | Painted modules          |          | 67                       | 67    | 10                       | 10    | 59                       | 59    | 37                       | 37    | 8                        | 8     |
|                 |                          |          |                          |       |                          |       |                          |       |                          |       |                          |       |
| Piping          | Modules with pipe inside |          | 45                       | 45    | 10                       | 10    | 59                       | 59    | 18                       | 20    | 8                        | 8     |
|                 |                          |          |                          |       |                          |       |                          |       |                          |       |                          |       |
| Heat tracing    | Modules with tracing     |          | 45                       | 45    | 10                       | 10    | 59                       | 59    | 18                       | 20    | 8                        | 8     |

| ERECTION STEEL STRUCTURE | TOTAL unit | ERECTED | REMAINING |
|--------------------------|------------|---------|-----------|
| <b>Columns</b>           |            |         |           |
| PB01                     | 45         | 45      | 0         |
| PB02                     | 11         | 8       | 3         |
| PB03                     | 64         | 63      | 1         |
| PB04                     | 20         | 9       | 11        |
| PB05                     | 6          | 6       | 0         |
| <b>Modules</b>           |            |         |           |
| PB01                     | 67         | 67      | 0         |
| PB02                     | 10         | 9       | 1         |
| PB03                     | 59         | 57      | 2         |
| PB04                     | 37         | 16      | 21        |
| PB05                     | 8          | 8       | 0         |

Week 28 2026

| Area    | Description                                                                                                                                                                         |
|---------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| General | FERRMIX manpower: number of critical resources remains unchanged (average of 20 welders) with a good performance.                                                                   |
| General | FERRMIX is still underperforming in relation to Earthing. Only 97% progress have been achieved at P1. FERRMIX has announced mobilization of additional electricians for this Scope. |


Weekly Welding by Welders

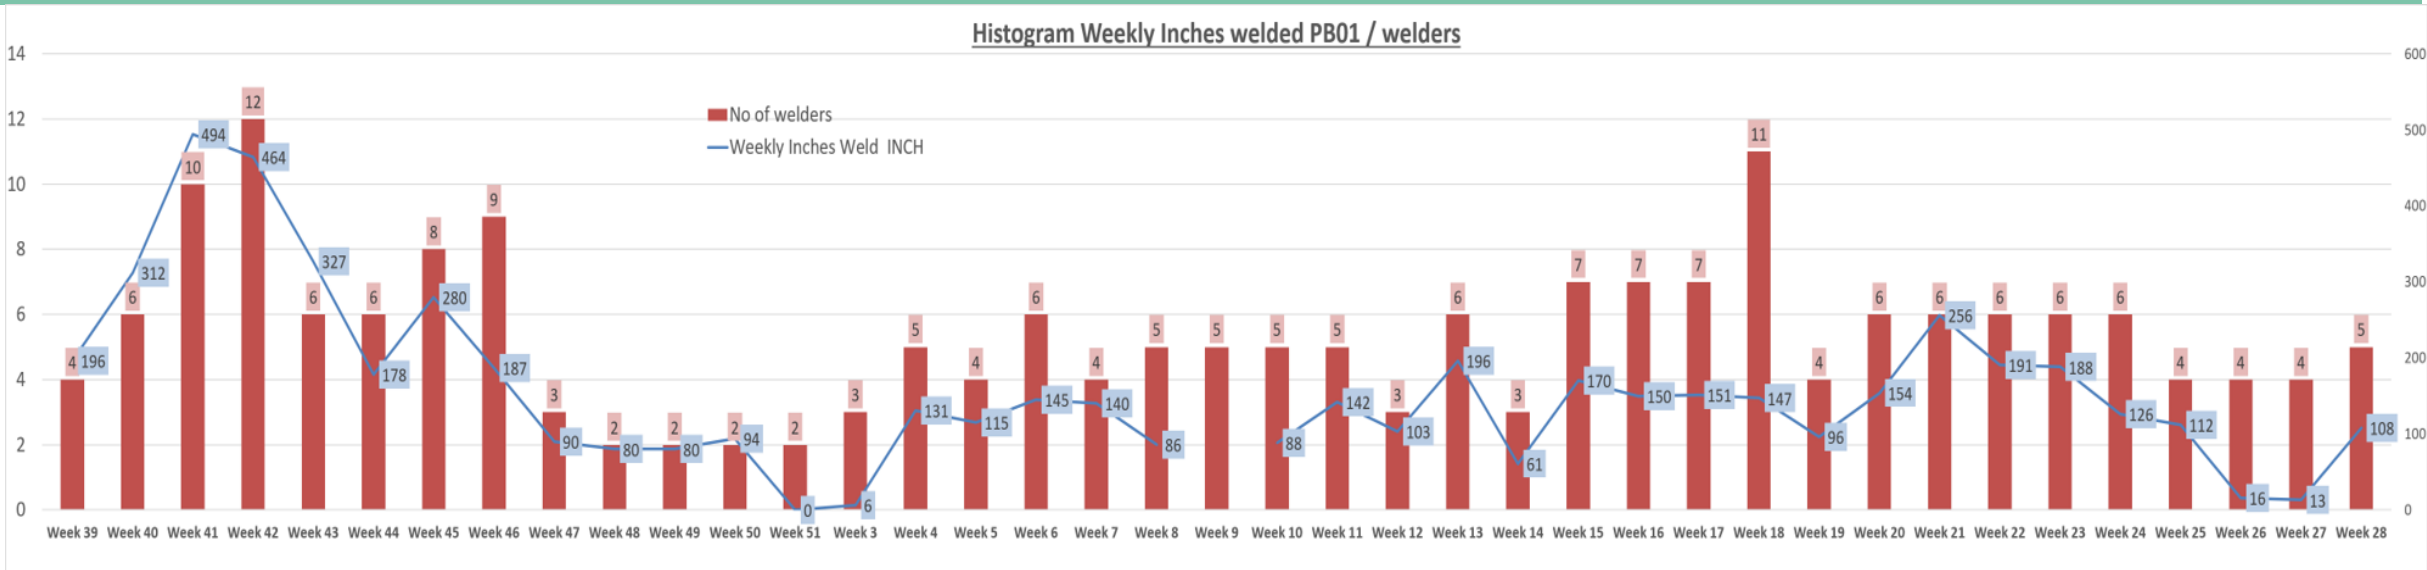

# BOP | Pipe Bridge General Comments - Ferrmix

## Weekly Welding by Welders


PB01 PRODUCTIVITY WELDING / WEEK

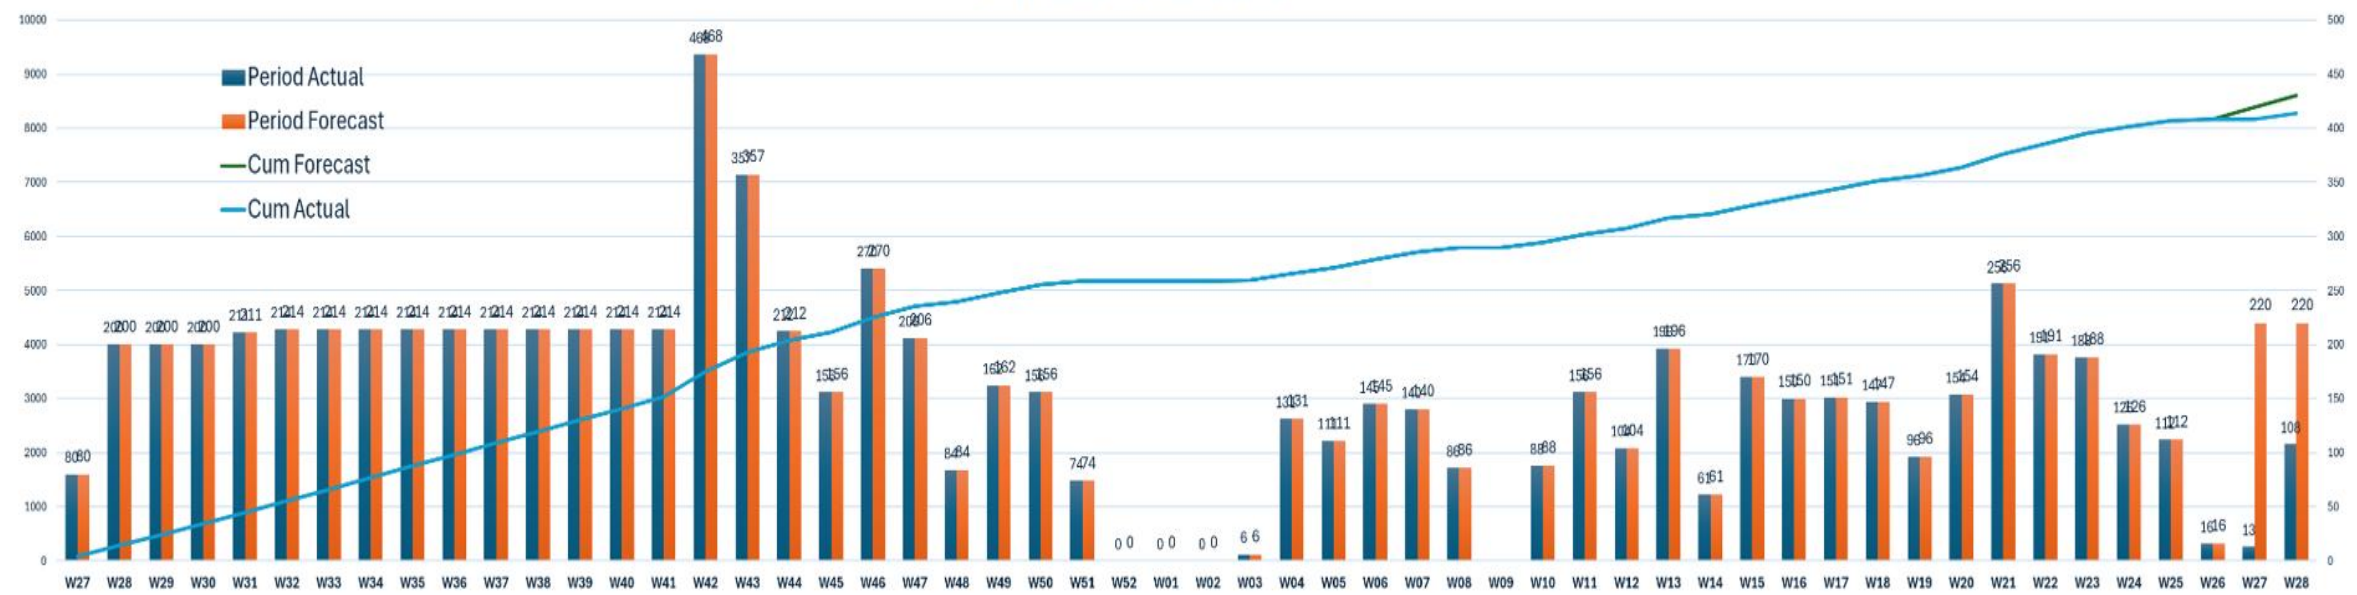

## Status Piping Welding by Priorities

| SUM<br>% PROG. | Total<br>Inch<br>Field | Accum.<br>Welded<br>Field | % Prog.<br>Welded<br>Field | Total Inch<br>Shop | Accum.<br>Welded<br>Shop | % Prog.<br>Welded<br>Shop | Total<br>Inch<br>F+S | Total Welded<br>F+S | Total<br>Weld<br>% |
|----------------|------------------------|---------------------------|----------------------------|--------------------|--------------------------|---------------------------|----------------------|---------------------|--------------------|
| P1             | 9.999                  | 8.208                     | 82%                        | 12.696             | 12.696                   | 100%                      | 22.694               | 20.778              | 92%                |
| P2             | 1.504                  | 916                       | 61%                        | 3.851              | 3.783                    | 98%                       | 5.355                | 4.643               | 87%                |
| P3             | 4.708                  | 2.125                     | 45%                        | 13.198             | 13.158                   | 100%                      | 17.905               | 14.888              | 83%                |
| P4             | 2.353                  | 1.768                     | 75%                        | 3.528              | 3.528                    | 100%                      | 5.881                | 5.146               | 88%                |
| P4.a           | 1.532                  | -                         | 0%                         | 4.021              | 3.991                    | 99%                       | 5.553                | 3.991               | 72%                |
| P5             | 746                    | 110                       | 15%                        | 1.596              | 1.473                    | 92%                       | 2.342                | 1.583               | 68%                |
|                | 20.841                 | 13.127                    | 63%                        | 38.888             | 38.627                   | 99%                       | 59.729               | 51.028              | 85%                |

## Progress

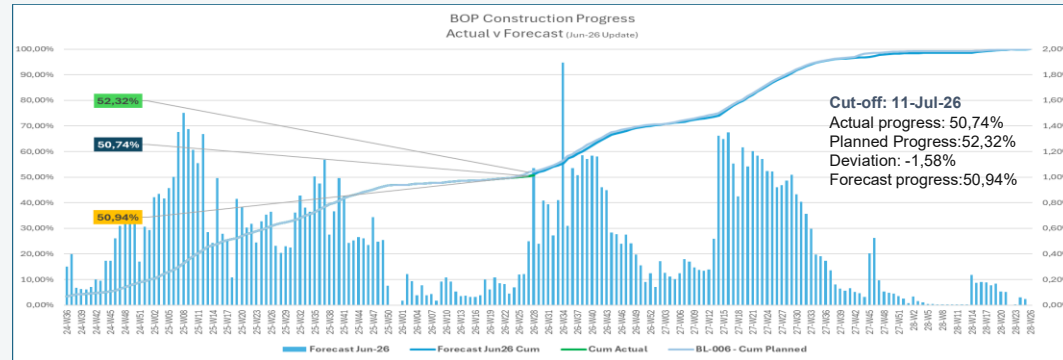

## Main deviations and mitigating actions

| Discipline | RED Activity                                                                                                              | Mitigating action                                                                                                                                                                                                                                                                                                                                                                                            |
|------------|---------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Con        | PB- Piping connections + pending fittings                                                                                 | <ul style="list-style-type: none"> <li>WK28 – Average 20 Welders, Ferrmix forecast 660 inches/week vs Actual 709 inches/week</li> <li>PB01 Welding productivity: 220 inches /week</li> <li>PB02 Welding productivity: 88 inches /week</li> <li>PB03 Welding productivity: 264 inches /week</li> <li>PB04 Welding productivity: 88 inches /week</li> <li>PB05 Welding productivity: 0 inches /week</li> </ul> |
| Con        | PB05 foundation for support pipes                                                                                         | McDermott to execute the piping in that area asap/ Contract with the new civil contractor is to be signed.                                                                                                                                                                                                                                                                                                   |
| Con        | SIEMENS: Delay to finalising NPB511 punch items                                                                           | Siemens mobilization to site (expect WK33). 1 week is needed to close punches                                                                                                                                                                                                                                                                                                                                |
| Con        | PB02. Foundation not possible due to works by Mc Dermott                                                                  | McDermott piping pending. Focus on other areas. / Contract with the new civil contractor is to be signed.                                                                                                                                                                                                                                                                                                    |
| Con        | PB03. Foundation in the WTP2 area no possible to works by Mc Dermott                                                      | Confirmation from Stegra to proceed with execution / Contract with the new civil contractor is to be signed.                                                                                                                                                                                                                                                                                                 |
| Con        | PB04. Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott. | Agreement reached to execute foundation. Steel structure installation pending for permission                                                                                                                                                                                                                                                                                                                 |
| Con        | Actemium: Delay PB and NPB511 UG earthing completion.                                                                     | Pending contractual agreement Stegra/Actemium                                                                                                                                                                                                                                                                                                                                                                |

## Plan

| Activity                                                            | Plan date | Fcst date | CP impact? | Mitigating action                         | Who  | When     |
|---------------------------------------------------------------------|-----------|-----------|------------|-------------------------------------------|------|----------|
| LNG Civils works complete (remaining works)                         | W32 26    | WK41 26   | Y          | Interface management                      | IDOM | WK29 26  |
| Commence FF Pumping station civil works (after piping installation) | W38 26    | WK38 26   | Y          | Interface management                      | IDOM | WK30 26  |
| Commence RW Pumping station building erection                       | W37 26    | WK37 26   | Y          | Interface management                      | IDOM | WK30 26  |
| PB1 connections complete                                            | W51       | WK35 26   | Y          | Ferrmix confirms more welders: 20 welders | FER  | WK35 26  |
| UGP1 completion (incl. Ave. 9.5)                                    | W31 26    | WK28 26   | Y          | Piping works completed                    | GRK  | WK28 26  |
| Start Electrical Works (PDOP area)                                  | WK 28 26  | WK28 26   | Y          | Start electrical works PDOP               | STS  | WK 30 26 |

Achievement Actual / Plan OR Forecast / Plan as percentage

  On track / no issue 
   Risk / Concern 
   Behind

# BOP | Construction (IDOM)

## Planned vs. Actual Week 28 2026

| Weight  | Activity                                                                 | Cum Actual    | Actual       | Plan (BL CCE06 TBA) | Forecast W28 | Dev. Forecast Vs Actual | Dev. Planned Vs Actual | Forecast W29 | Deviation (Against Forecast)                                                                                                                                                     | Mitigation Actions                                                                                                                                                                                                                                      |
|---------|--------------------------------------------------------------------------|---------------|--------------|---------------------|--------------|-------------------------|------------------------|--------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 6,83%   | Raw Water & FF Pumping Stations                                          | 74,65%        | 0,00%        | 0,00%               | 0,00%        | 0,00%                   | 0,00%                  | 0,07%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 0,25%   | Compressed Air Plant NPB-422                                             | 0,00%         | 0,00%        | 0,00%               | 0,00%        | 0,00%                   | 0,00%                  | 0,00%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 6,02%   | LNG Terminal / Regasification Unit                                       | 87,02%        | 2,87%        | 2,12%               | 3,69%        | -0,82%                  | 0,75%                  | 3,73%        | 1. Delay in electrical work for cable pulling<br>2. Delivery delay MV Transformer<br>3. Delivery delay Controll units                                                            | 1. Underground ducts de-icing and pits 1/2 modification were completed WK27. Chart is recovering the delay<br>2. MV Transformer TBC (Pending Stegra Technical deviation approval) (+11 Week from response to delivery).<br>3. Controll units ETA W32/33 |
| 5,11%   | PDOP Civil                                                               | 92,82%        | 0,09%        | 0,00%               | 0,00%        | 0,09%                   | 0,09%                  | 0,00%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 1,76%   | Power Distribution 51x                                                   | 84,69%        | 0,00%        | 0,00%               | 0,00%        | 0,00%                   | 0,00%                  | 0,00%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 8,07%   | NPB-200 Series                                                           | 55,95%        | 0,00%        | 0,00%               | 0,00%        | 0,00%                   | 0,00%                  | 0,00%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 1,00%   | NPB-102 Safety & Security Building                                       | 0,00%         | 0,00%        | 0,00%               | 0,00%        | 0,00%                   | 0,00%                  | 0,00%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 17,84%  | Pipe & Cable Racks                                                       | 84,34%        | 0,56%        | 0,12%               | 0,56%        | 0,00%                   | 0,44%                  | 0,44%        |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |
| 21,06%  | Underground Networks                                                     | 17,55%        | 0,17%        | 0,66%               | 0,54%        | -0,37%                  | -0,49%                 | 0,74%        | 1. RW/FF area: UG piping installation activities are underperforming<br>2. Prio 0 RW chamber not finish<br>3. Prio 1 Pressure test not yet performed<br>4. Electrical ducts PDOP | 1. GRK will send a recovery schedule<br>2. GRK will finalize in the coming weeks<br>3. Test pack rejected to be re-submitted<br>4. Release area by Hitachi in Week 29                                                                                   |
| 9,61%   | RailWay Package                                                          | 33,70%        | 0,00%        | 0,42%               | 0,00%        | 0,00%                   | -0,42%                 | 0,02%        | Pending approval of CO to proceed with the works                                                                                                                                 | Expedite the approval of CO                                                                                                                                                                                                                             |
| 22,45%  | Overall Construction Sweco Scope: Ponds, Roads & Temporary Power - Water | 34,18%        | 0,19%        | 0,30%               | 0,28%        | -0,09%                  | -0,11%                 | 2,69%        | 1. Completion of Mechanical completion of Temporary Power and TWTP<br>2. Completion of Mechanical completion of Temporary TWTP                                                   | 1. Completion of Testing Cables, testing earthing works by Ferrmix and Actemium, Siemens needs to close the Punches opens B.<br>2. Close commercial/ contracting CR                                                                                     |
| 100,00% | <b>Total</b>                                                             | <b>50,74%</b> | <b>0,36%</b> | <b>0,40%</b>        | <b>0,50%</b> | <b>-0,14%</b>           | <b>-0,04%</b>          | <b>0,60%</b> |                                                                                                                                                                                  |                                                                                                                                                                                                                                                         |


Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
  Risk / Concern
  Behind



# BOP | Railways Management (IDOM PCM – SWECO - GRK )

## Progress Status

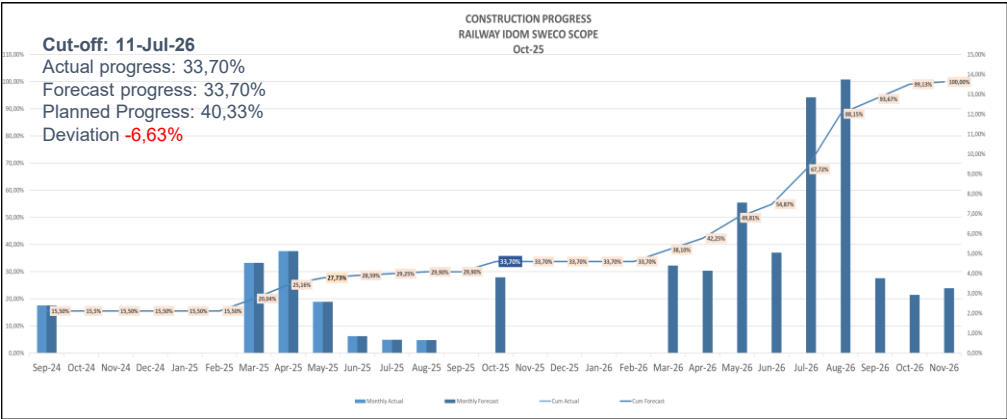

## 1+6 activities

Week 28 - KOM was performed 9th Jul. GRK submitted preliminary Schedule. ITP ground works and rail submitted by GRK and revised/approved by IDOM/Stegra completed.

Week 29 – Preparation of the area

Week 30 – Mobilisation to site. Start drainage piping installation under the rail and UG piping crossing. DRP need to start removing pipe material of section 3

Week 31 - Continue drainage piping installation under the rail and UG piping crossing. GW in section 6.

Week 32 - Continue drainage piping installation under the rail and UG piping crossing

Week 33 - Continue drainage piping installation under the rail and UG piping crossing

Week 34 - Continue drainage piping installation under the rail and UG piping crossing

## Main deviations and mitigating actions

| Discipline | RED Activity                                                                                                                            | Mitigating action                                                                   |
|------------|-----------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|
| CON        | Section 3 Interference with Hydrogen pipe                                                                                               | Expected IFC drawing for culvert end of September 26 (SWECO)                        |
| CON        | New pile deck in Scope of McDermott not interfere with railway truck, but interfere with the pressure bern, east ditch and service road | Alternative 3 Hidrogen pipeline                                                     |
| CON        | Scrap Yard micropilling Desing End of May (Done). Micropilling to be done by McDermott                                                  | Only for railway truck. East ditch and service road on the limit boundary can start |
| CON        | Activities planned to restart in Week 30 (Drainage piping)                                                                              | Pending CO for East ditch                                                           |

| TOTAL RAILWAY                         | Unit | Total  | Weight % | Contractor | Actual Progress | Category        | WK28 | WK29 | WK30 | WK31 | WK32  | WK33  | WK34 |
|---------------------------------------|------|--------|----------|------------|-----------------|-----------------|------|------|------|------|-------|-------|------|
| Underbelt Layer (Rein.)<br>DCH. 15    | m3   | 72973  | 20%      | GRK        | 31%             | Period Forecast | 0    | 0    | 9177 | 2955 | 10542 | 10542 | 8669 |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Underballest Layer (Frost)<br>DCH. 16 | m3   | 118902 | 20%      | GRK        | 30%             | Period Forecast | 0    | 0    | 3609 | 5390 | 14408 | 5605  | 0    |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Catenary Poles/ Struts                | ea   | 199    | 5%       | GRK        | 33%             | Period Forecast | 0    | 0    | 12   | 0    | 20    | 12    | 16   |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Construction of new Ballast track     | m    | 9602   | 15%      | GRK        | 40%             | Period Forecast | 0    | 0    | 0    | 384  | 383   | 184   | 184  |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Supplementation of ballast layer      | m3   | 30296  | 15%      | GRK        | 40%             | Period Forecast | 0    | 0    | 559  | 0    | 700   | 900   | 869  |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Construction of new Ballasttles track | m    | 4403   | 5%       | GRK        | 3%              | Period Forecast | 0    | 0    | 0    | 184  | 184   | 184   | 184  |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Switches                              | ea   | 18     | 5%       | GRK        | 39%             | Period Forecast | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Hanging Works                         | ea   | 22     | 15%      | GRK        | 27%             | Period Forecast | 0    | 0    | 0    | 0    | 3     | 0     | 0    |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
| Concrete Channel Section 7 - Track 1  | m    | 1000   | 1%       | GRK        | 100%            | Period Forecast | 0    | 0    | 0    | 0    | 0     | 0     | 0    |
|                                       |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0     | 0     | 0    |

## 6-month key Waypoints


| Key Waypoints                                       | Planned date | Forecast date |
|-----------------------------------------------------|--------------|---------------|
| Longitudinal drainage SSY (start)                   | 10 Nov 2025  | 30 Aug 2026   |
| Ballast & sub-ballast SSY (Start)                   | 17 Nov 2025  | 27 Jul 2026   |
| Trench excavation Track 1 – Section 6               | 28 Nov 2025  | 27 July 2026  |
| North Railway - Section 7 – Ready for commissioning | 29 May 2026  | 30 Sep 2026   |

Achievement    Actual / Plan OR Forecast / Plan as percentage

On track / no issue     Risk / Concern  
 Behind

# BOP | Roads & Ditches Management (IDOM EPCM – SWECO – GRK )

## Progress Status

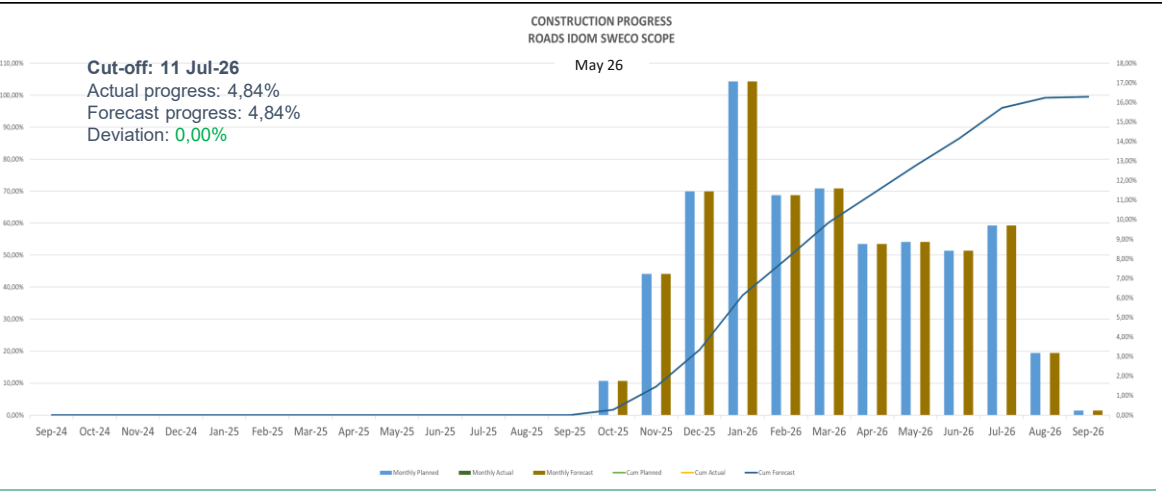

## 1+6 activities

Week 28 – CR already issued to start backfilling Ave 9.5 (estructural layers). CR was approved for Road 6.0. CR for backfilling for road 6.1 and 6.2 to be issued.

Week 29 - Activities on hold due to GRK mobilisation for road 6.0

Week 30 - Activities on hold. Expect to started permanents backfilling

Week 31 - Start permanent backfilling Road 6.1 and 9.5

Week 32 - Continued permanent backfilling Road 6.1 and 9.5

Week 33 – Continued permanent backfilling Road 6.1 and 9.5

Week 34 – Continued permanent backfilling Road 6.1 and 9.5

## Main deviations and mitigating actions

| Discipline | RED Activity | Mitigating action |
|------------|--------------|-------------------|
|            |              |                   |
|            |              |                   |
|            |              |                   |

| Avenue/Roads | Activity name                                    | Weight % | Weight % on Tot | Progress | Category        | WK28     | WK29     | WK30     | WK31     | WK32     | WK33     | WK34     |
|--------------|--------------------------------------------------|----------|-----------------|----------|-----------------|----------|----------|----------|----------|----------|----------|----------|
|              |                                                  |          |                 |          |                 | 11/07/26 | 18/07/26 | 25/07/26 | 01/08/26 | 08/08/26 | 15/08/26 | 22/08/26 |
| Av 1         | Avenue 1                                         | 100%     | 5%              | 34%      | % Cum Planned   | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      |
|              |                                                  |          |                 |          | % Cum Forecast  | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      |
|              |                                                  |          |                 |          | % Cum Actual    | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      | 34%      |
| Av 1         | Roads - Avenue 1 - Clearing and levelling ground | 23%      |                 | 100%     | Period Forecast | 0        | 0        | 0        | 0        | 0        | 0        | 0        |
|              |                                                  |          |                 |          | Cum Forecast    | 1        | 1        | 1        | 1        | 1        | 1        | 1        |
|              |                                                  |          |                 |          | % Cum Forecast  | 100%     | 100%     | 100%     | 100%     | 100%     | 100%     | 100%     |
|              |                                                  |          |                 |          | Period Actual   |          |          |          |          |          |          |          |
|              |                                                  |          |                 |          | Cum Actual      | 1        | 1        | 1        | 1        | 1        | 1        | 1        |
|              |                                                  |          |                 |          | % Cum Actual    | 100%     | 100%     | 100%     | 100%     | 100%     | 100%     | 100%     |

## 6-month key Waypoints


| Key Waypoints                    | Planned date | Forecast date |
|----------------------------------|--------------|---------------|
| Start sub-base laying Avenue 9.5 | 28 Sep 2026  | 19 Mar 2027   |
| Start Road Ave 1 Laying subbase  | 20 Jul 2026  | 20 Jul 2026   |
| Start sub-base laying Road 6     | 13 Jul 2026  | 25 Jul 2026   |

Achievement    Actual / Plan OR Forecast / Plan as percentage

On track / no issue     Risk / Concern  
 Behind

# BOP | Ponds Management (IDOM EPCM – SWECO – GRK)

## Progress Status

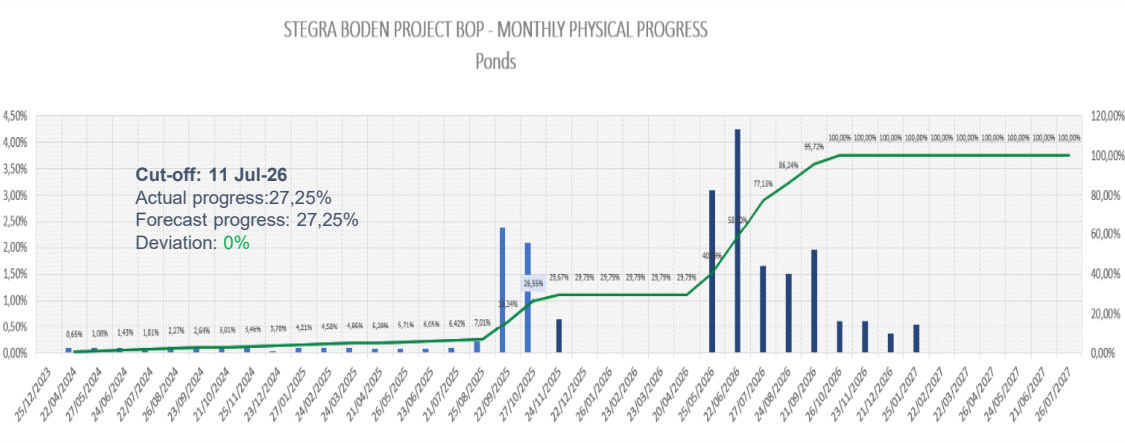

| PONDS TOTAL                     | Unit | Total  | Weight % | Contractor | Actual Progress | Category        | WK28 | WK29 | WK30 | WK31 | WK32 | WK33 | WK34  |
|---------------------------------|------|--------|----------|------------|-----------------|-----------------|------|------|------|------|------|------|-------|
| Surcharge placement and removal | m3   | 74900  | 15%      | GRK        | 98%             | Period Forecast | 9923 | 9923 | 4500 | 3500 | 1000 | 0    | 0     |
|                                 |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0    | 0    | 0     |
| Groundworks                     | m3   | 436954 | 30%      | GRK        | 88%             | Period Forecast | 5982 | 5982 | 7606 | 5982 | 5982 | 5982 | 3508  |
|                                 |      |        |          |            |                 | Period Actual   | 6900 | 0    | 0    | 0    | 0    | 0    | 0     |
|                                 |      |        |          |            |                 | Period Forecast | 0    | 0    | 10   | 47   | 382  | 0    | 0     |
| Pipes installation              | m    | 1199   | 20%      | GRK        | 50%             | Period Actual   | 0    | 0    | 0    | 0    | 0    | 0    | 0     |
| Geomembrane installation        | m2   | 34280  | 15%      | GRK        | 21%             | Period Forecast | 0    | 0    | 5000 | 5000 | 5511 | 7336 | 2336  |
|                                 |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0    | 0    | 0     |
| Erosion Protection (Riprap)     | m3   | 94071  | 20%      | GRK        | 36%             | Period Forecast | 3668 | 3668 | 0    | 0    | 0    | 4115 | 13657 |
|                                 |      |        |          |            |                 | Period Actual   | 0    | 0    | 0    | 0    | 0    | 0    | 0     |

## 1+6 activities

- Week 28 - Continue excavation East ponds.
- Week 29 - ITP to be resubmitted for West pond and Contact water pond. Continue excavation East ponds.
- Week 30 - Continue excavation East ponds. West pond 1 erosion protection cover installation.
- Week 31 - Continue excavation East ponds. West pond 1 erosion protection cover installation
- Week 32 - Continue excavation East ponds and Start excavation Contact water pond. West pond 1 erosion protection cover installation
- Week 33 - Continue excavation East ponds and Contact water pond
- Week 34- Continue excavation East ponds and Contact water pond

## Main deviations and mitigating actions



| Discipline | RED Activity                                                                                                           | Mitigating action                        |
|------------|------------------------------------------------------------------------------------------------------------------------|------------------------------------------|
| PRC        | Remaining works for West pond 3 completion (CR pending)                                                                | IDOM, GRK and Stegra to expedite process |
| QAQC       | ITP for West ponds pending revision by IDOM/Stegra. Works on hold.<br>Pending geomembrane testing sub-contractor award | GRK to award sub-contractor for test     |

## 6-month key Waypoints

| Key Waypoints          | Planned date | Forecast date |
|------------------------|--------------|---------------|
| Completion West Pond 1 | 30 Jun 2026  | 30 Jul 2026   |
| Completion West Pond 3 | 30 Jun 2026  | 30 Jul 2026   |

# Construction Manpower & Histogram for ongoing activities

| Week 28 2026                | GRK                | ANFRA              | ACTEMIUM           | FERRMIX            | CHART              | SIEMENS            | FORSSA             | LBS                | PROXA              | KSH                | STS                | NORDIC             |
|-----------------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|--------------------|
|                             | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual | Blue collar Actual |
| LNG                         | 0                  |                    |                    |                    | 11                 |                    |                    |                    |                    | 0                  |                    |                    |
| RAIL                        |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| PONDS                       | 7                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| RW AREA                     | 0                  |                    |                    |                    |                    |                    | 0                  |                    |                    |                    |                    | 6                  |
| UGP RW AREA                 | 5                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| UGP0 (Ave 1 & Ave 2)        | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| UGP1 (Road 7 Ave 9.5)       | 7                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| UGP3 (Road 6)               | 8                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| UGP4 (Ave 9)                | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| PDOP                        |                    | 8                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| 100 MW CABLE PULL (OFFSITE) |                    |                    | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| 100 MW CIVILS               | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| PB FOUNDATIONS              | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| PB ERECTION & FITUP         |                    |                    |                    | 65                 |                    |                    |                    |                    |                    |                    |                    |                    |
| TEMPORARY POWER ONSITE      |                    |                    | 0                  |                    |                    |                    |                    | 0                  |                    |                    |                    |                    |
| 515                         | 0                  |                    |                    |                    |                    | 0                  |                    |                    |                    |                    |                    |                    |
| 511                         |                    |                    |                    |                    |                    | 0                  |                    |                    |                    |                    |                    |                    |
| TEMPORARY PIPE BYPASS       | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| EARTHING WORKS              | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| Roads                       | 0                  |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| TWTP - Mechanical           | 0                  |                    |                    |                    |                    |                    |                    |                    | 1                  |                    |                    |                    |
| TWTP - Electrical           |                    |                    |                    |                    |                    |                    |                    |                    |                    | 0                  |                    |                    |
| TOTALS                      | 27                 | 8                  | 0                  | 65                 | 11                 | 0                  | 0                  | 0                  | 1                  | 0                  | 0                  | 6                  |
| BLTotal                     | 60                 | 0                  | 0                  | 65                 | 30                 | 0                  | 0                  | 0                  | 0                  | 0                  | 29                 | 100                |
| Actual Week Average         | 118                |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| BL Week Average             | 284                |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |
| Forecast Average            | 284                |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |                    |

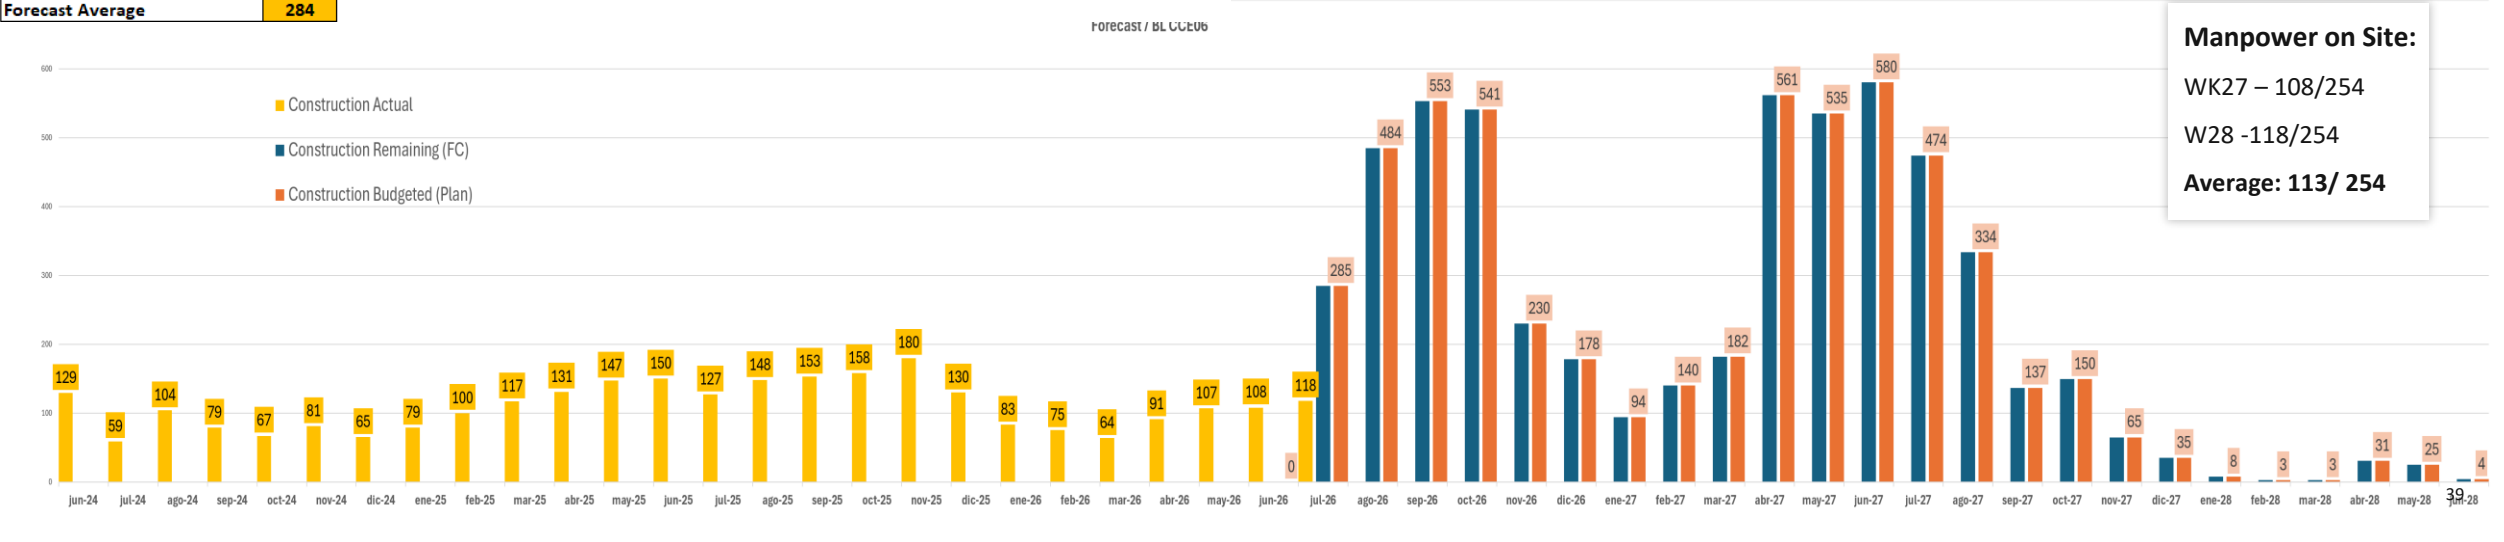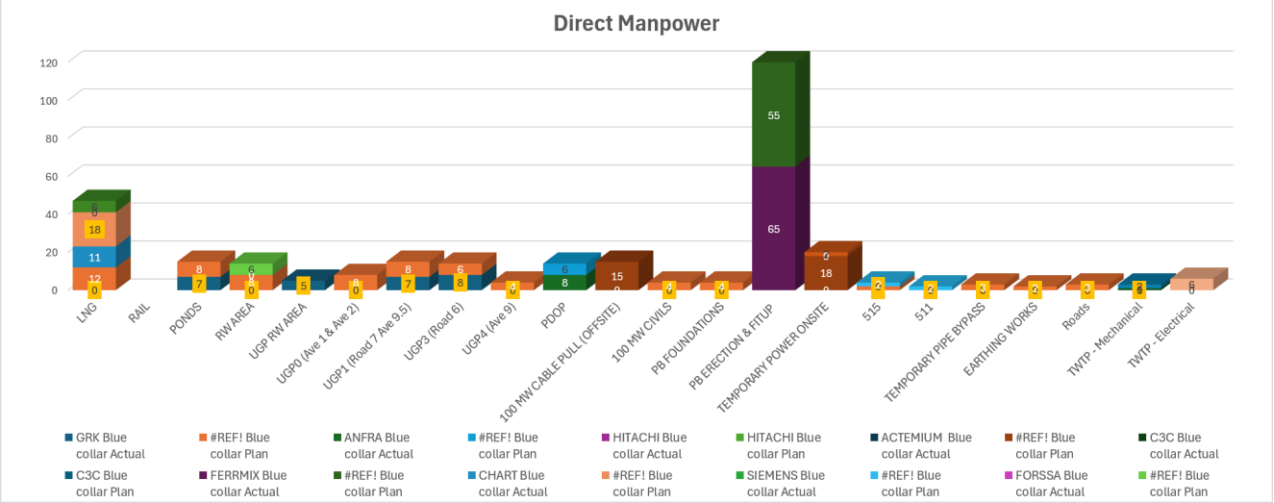

| Actions      |                                                                                                                     |          |                      |                                                                                                                                                                                                       |                                                |                                                                                                                                                                                                                                                       |
|--------------|---------------------------------------------------------------------------------------------------------------------|----------|----------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Sub-Area     | Key issue / potential risk                                                                                          | Due Date | Owner                | Description                                                                                                                                                                                           | Potential Impact                               | Mitigation                                                                                                                                                                                                                                            |
| Column2      | Column3                                                                                                             | Column4  | Column5              | Column6                                                                                                                                                                                               | Column7                                        | Column8                                                                                                                                                                                                                                               |
| PB02         | Erection of bridge & reinstall foundation PB02 to WTP1 blocked by Mc Dermott and Stegra                             | w42_25   | STEGRA/ Mc Dermott   | No access permission.                                                                                                                                                                                 | Delay to construction (pipes test)             | Confirmation from stegra to proceed with erection                                                                                                                                                                                                     |
| PB03         | PB03. Foundation in the WTP2 area no possible to works by Mc Dermott                                                | w45_25   | STEGRA/ Mc Dermott   | No access permission.                                                                                                                                                                                 | Delay to construction                          | Mc Dermott to be confirmed date to release the area                                                                                                                                                                                                   |
| PB04         | PB04: Foundation & Erection SS (columns and modules), due to constructability priorities of CAS/SMPT by Mc Dermott. | w36_25   | STEGRA/ Mc Dermott   | No access permission.                                                                                                                                                                                 | PB04 not ready as scheduled.                   | Agreement reached to execute foundation. Steel structure installation pending for permission.                                                                                                                                                         |
| Pipe Bridges | Pipebridge Piping Connections + Pending Fittings                                                                    | w25_25   | IDOM/STEGRA/FE RRMIX | Lack of welding Resources and low productivity                                                                                                                                                        | Delay in connections and pending fittings      | WK27 – Average 19 Welders, Ferrmix actual 793 inches/week                                                                                                                                                                                             |
| Rail South   | Unloading Station Tunnel                                                                                            | w35_26   | IDOM DRP             | Track 1 execution restricted for Tunnel                                                                                                                                                               | Construction delay                             | Review status weekly to make sure Tunnel is delivered on schedule. DRP confirmed August 24, 2026 as the completion date.                                                                                                                              |
| Rail South   | Road 2 retaining wall                                                                                               | w30_26   | IDOM BOP / GRK       | Track 1 execution restricted for retaining wall                                                                                                                                                       | Construction delay                             | Review weekly status to ensure the retaining wall is delivered on time w28 - IDOM to provide GRK with the documentation (BoQ & drawings) for the retaining wall for GRK to price.                                                                     |
| Roads/UGP    | Road 6.0 as laydown area for UGP                                                                                    | w28_26   | IDOM BOP             | Road 6.0 to be used as laydown area for execution of Road 6.1 and Road 6.2 UGP                                                                                                                        | Construction delay                             | w22 - CR for filling of Road 6.0 to be issued this week for pricing. w23/w24/w25/w26/w28 - Stegra to review and approve the Road 6.0 CR. w27 - Stegra engineering to approve the change via RFI 6308. Stegra/IDOM to define how to implement the FDC. |
| Rail         | Transversal and longitudinal drainage interface with loading station                                                | w29_26   | IDOM BOP/DRP         | Interface between the loading station and the transversal and longitudinal drainage.                                                                                                                  | Construction delay                             | w28 - Stegra identified potential issues with IDOM's proposed solution and will coordinate with IDOM site team to optimize the solution. w27 - Stegra to provide the teothermal levels for the cables if the already executed is not valid.           |
| Rail/Roads   | Clash with existing power supply at Section 5 Rail                                                                  | w30_26   | IDOM BOP / Stegra SS | Existing power supply to plant crosses eastern ditch and rail at Section 5. Until a solution if proposed, rail groundworks cannot start.                                                              | Construction delay , redesign may be required. | w28 - Stegra provided the theoretical levels and IDOM has reviewed them. IDOM construction team to establish a protocol to confirm they can proceed with the excavations.                                                                             |
| Ponds        | West Pond 2 cannot be finished until the northern area is handed back by DRP.                                       | w33_26   | IDOM BOP/DRP         | In 2025, DRP took over the northern wall area to use it as a laydown area. This area must be handed back to BOP in order to allow the raising of the northern wall and the completion of West Pond 2. | Construction delay                             | w26 - IDOM BOP team to coordinate with DRP in the internal interface meeting on w28. w28 - IDOM BOP meeting with IDOM DRP has been postponed to w29                                                                                                   |
| Temp Power   | Actemium: Delay PB and NPB511 UG earthing completion                                                                | WK25_26  | IDOM/STEGRA          | Actemium: Delay PB and NPB511 UG earthing completion                                                                                                                                                  | Delay to energization                          | Pending contractual agreement STEGRA/ACTEMIUM                                                                                                                                                                                                         |
| Roads        | Boden Energy switch houses                                                                                          | w38_26   | Stegra SS            | Switch houses are located at the same location than the service road over the East ditch. It is necessary either to remove the houses or to divert the road                                           | Construction delay , redesign may be required. | w25/w27 - Pending Stegra to make a decision on how to proceed w28 - Current plan is to execute the service road until the switch houses.                                                                                                              |



# BOP | Construction Pictures - Pipe Bridge

- Piping welding works (all priorities) 709 Inches welded



PB01 and PB05



PB03 Zone 1



PB03 Zone 2

Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind




## BOP | Construction Pictures - UG piping

- Avenue 9.5 piping installation and backfilling completed
- Road 6 Piping installation and backfilling ongoing





Avenue 9.5

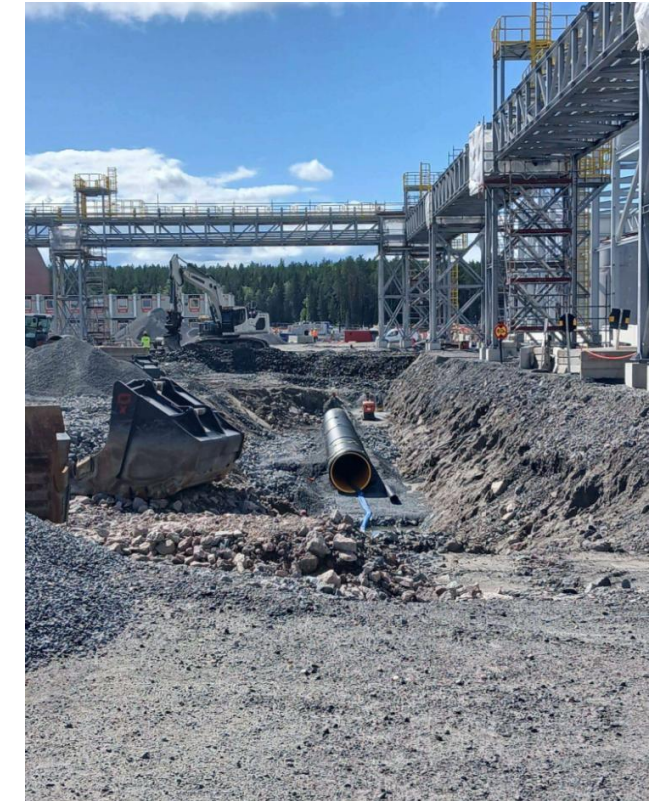

Road 6

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern  
 Behind



## BOP | Construction Pictures – NPB 511

- Punch list close out (by Actemium) ongoing
- Siemens mobilization to site (expect WK33). 1 week is needed to close punches



Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind

## BOP | Construction Pictures - LNG Terminal

- Pipe welding ongoing
- 3 Pressure test performed
- Cable pulling and connection ongoing
- Diesel generator installation



Cable pulling



Diesel generator

Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind



## BOP | Construction Pictures - RW+FF Area

✓ UG piping installation ongoing



Achievement    Actual / Plan OR Forecast / Plan as percentage

On track / no issue   
  Risk / Concern  
 Behind

## BOP | Construction Pictures - PDOP

- Backfilling ongoing
- Area between ELA01 and Transformers waiting for Transformers works completion (Hitachi) (Expected end of July 26)




Earthing grid

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern  
 Behind



## BOP | Construction Pictures - Temporary Power

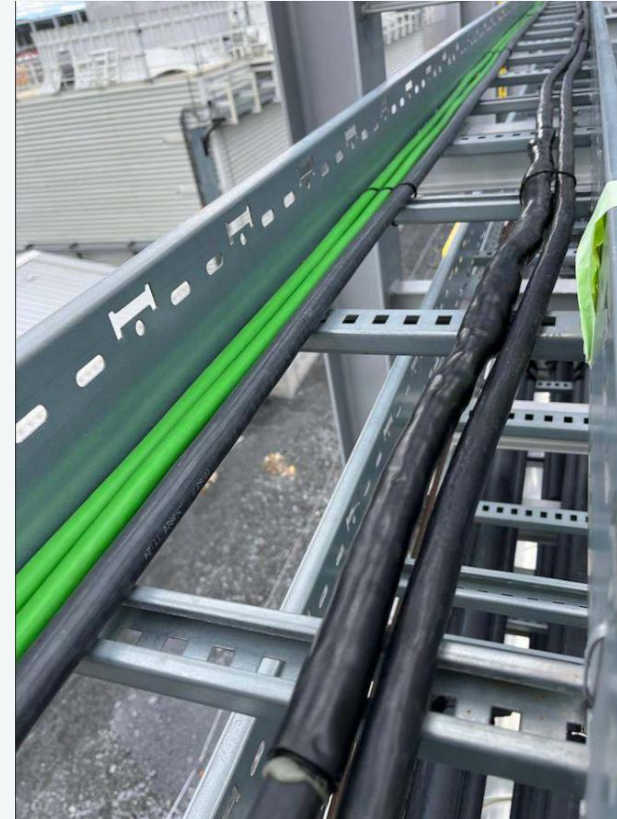

LV Cables repaired

Achievement    Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue    ■ Risk / Concern  
■ Behind

# BOP | Construction Pictures – Railways



Section 2 Unloading station



Section 3 Wet land view and  
Terrace of Tracks 10, 11 and  
12



Section 4A Scrap Yard Area for Track 1 ( exterior) and Tracks  
101 and 102 ( internal)

Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind



# BOP | Construction Pictures – Roads



Avenue 1 (Connection with municipality)

Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind

# BOP | Construction Pictures – Ponds

East ponds excavation ongoing



East ponds


Achievement    Actual / Plan OR Forecast / Plan as percentage

 On track / no issue     Risk / Concern  
 Behind



Actions

# BOP – 6 Week Look Ahead

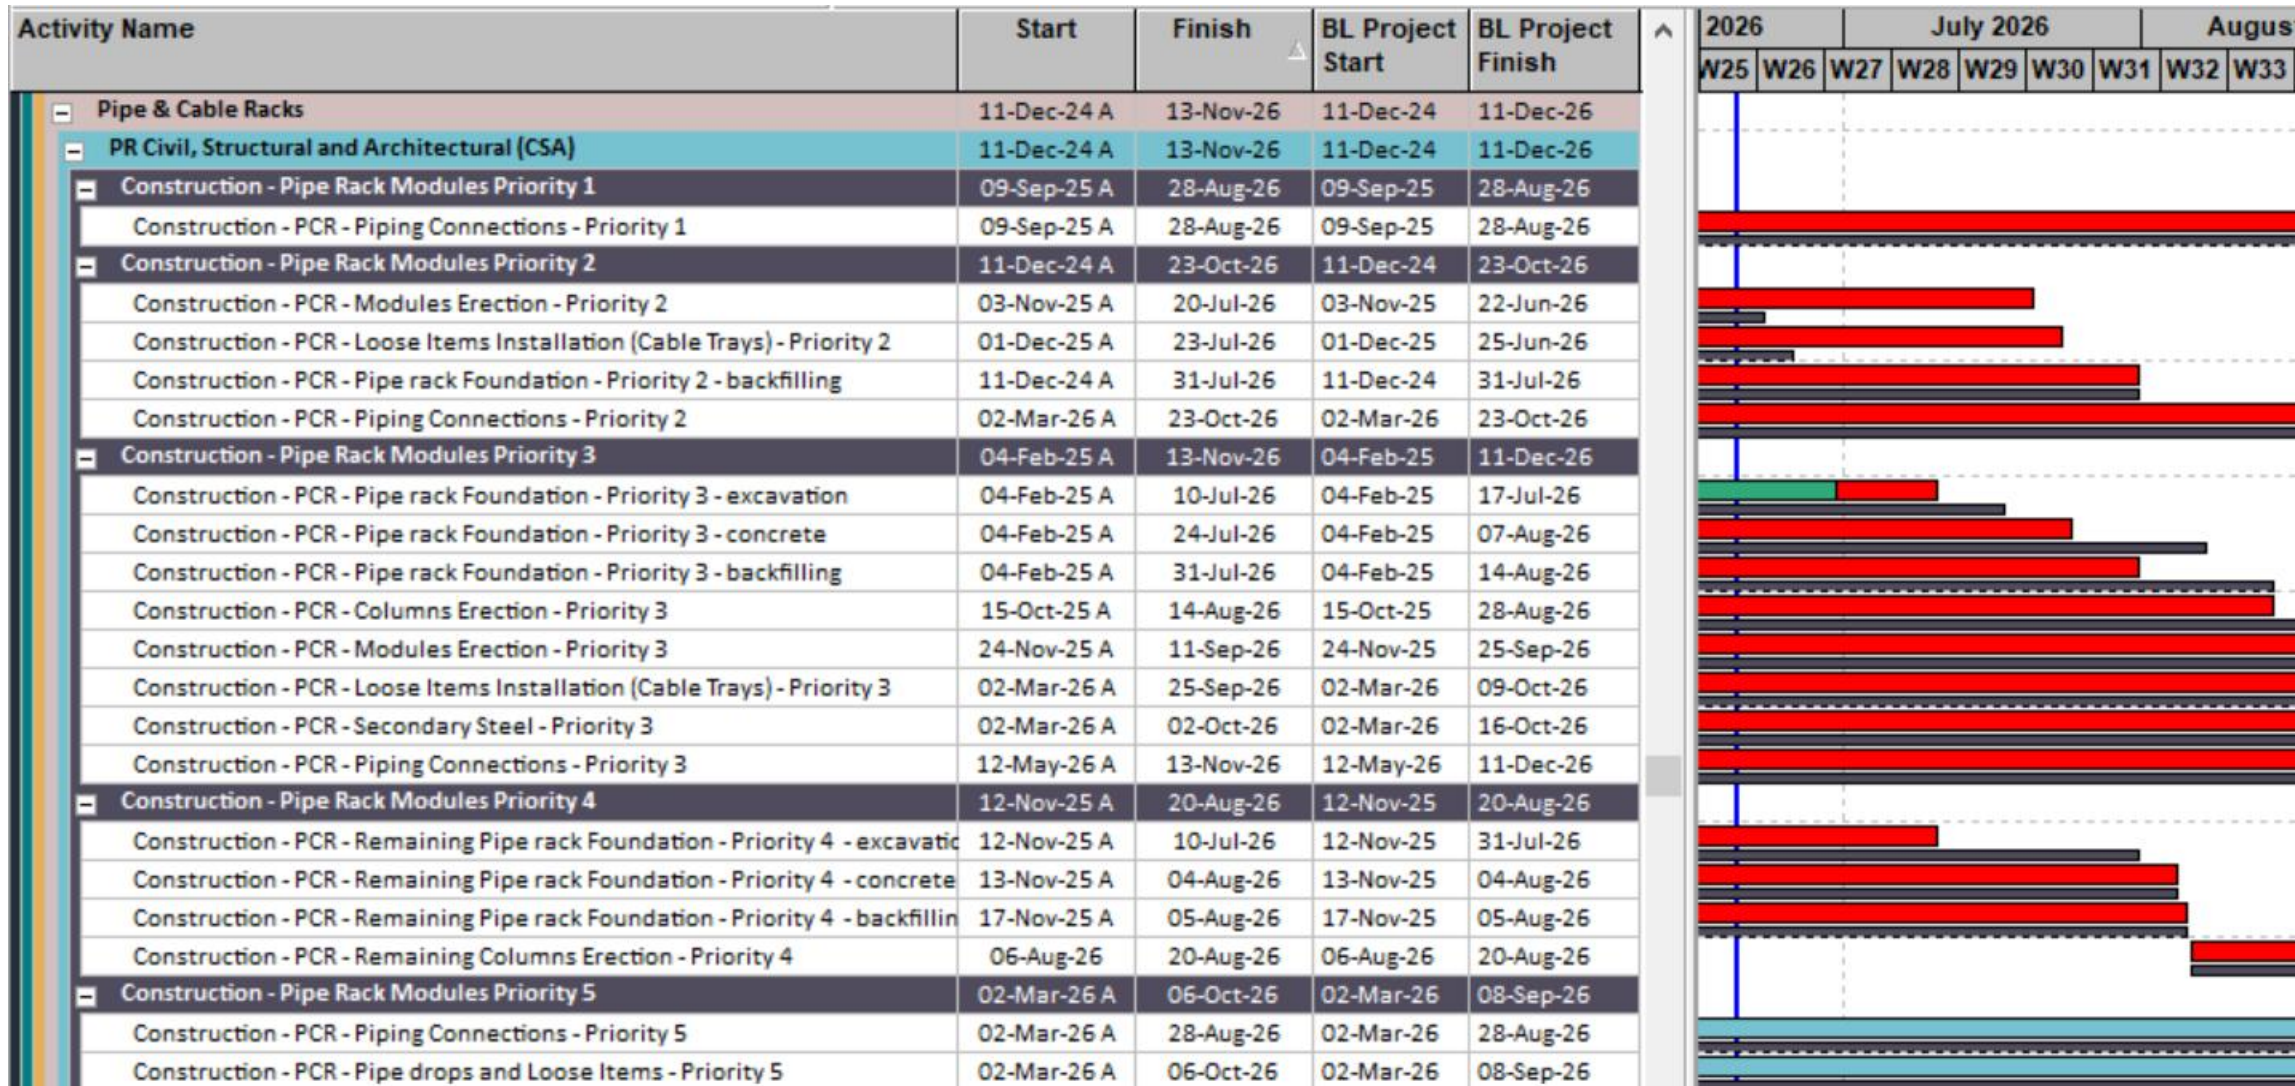

Actions

BOP – 6 Week Look Ahead

| Activity Name                                                                 | Start     | Finish    | BL Project Start | BL Project Finish | ^ | 2026 |     | July 2026 |     |     |     | August |     |     |
|-------------------------------------------------------------------------------|-----------|-----------|------------------|-------------------|---|------|-----|-----------|-----|-----|-----|--------|-----|-----|
|                                                                               |           |           |                  |                   |   | W25  | W26 | W27       | W28 | W29 | W30 | W31    | W32 | W33 |
| <div><div></div>Temporary Water Supply</div>                                  | 29-Jun-26 | 11-Jan-27 | 29-Jun-26        | 11-Jan-27         |   |      |     |           |     |     |     |        |     |     |
| Construction - Underground Networks - Route 0 - RW Chamber - Piping Arrang    | 29-Jun-26 | 17-Jul-26 | 29-Jun-26        | 17-Jul-26         |   |      |     |           |     |     |     |        |     |     |
| Construction - Excavation - Inst Contact Water pipe CW - Test backfilling (RW | 29-Jun-26 | 17-Jul-26 | 29-Jun-26        | 17-Jul-26         |   |      |     |           |     |     |     |        |     |     |
| Construction - Temporary Water Supply - TWTP Plant Operative                  | 03-Aug-26 | 11-Jan-27 | 03-Aug-26        | 11-Jan-27         |   |      |     |           |     |     |     |        |     |     |

Actions

BOP – 6 Week Look Ahead

| Activity Name                                                               | Start       | Finish    | BL Project Start | BL Project Finish |  | 2026 | July 2026 |     |     |     |     | August |     |     |
|-----------------------------------------------------------------------------|-------------|-----------|------------------|-------------------|--|------|-----------|-----|-----|-----|-----|--------|-----|-----|
|                                                                             |             |           |                  |                   |  | W25  | W26       | W27 | W28 | W29 | W30 | W31    | W32 | W33 |
| Temporary Power Transformers 2x63 MVA / 100 MW                              | 01-Oct-25 A | 09-Jul-26 | 01-Oct-25        | 09-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| 33 kV distribution from ELA to NPB511 and ASP - ON SITE                     | 01-Oct-25 A | 03-Jul-26 | 01-Oct-25        | 26-Jun-26         |  |      |           |     |     |     |     |        |     |     |
| ELA to NPB511 and ASP - Earthing Works - Installation & Connection by Ferrn | 01-Oct-25 A | 03-Jul-26 | 01-Oct-25        | 26-Jun-26         |  |      |           |     |     |     |     |        |     |     |
| Mechanical Completion & PreCom                                              | 06-Jul-26   | 09-Jul-26 | 29-Jun-26        | 09-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| Pre Commissioning - E-House NPB511 (Temporary Set) for WTP1, ASP, WPS, M    | 06-Jul-26   | 09-Jul-26 | 29-Jun-26        | 09-Jul-26         |  |      |           |     |     |     |     |        |     |     |



# Actions

## BOP – 6 Week Look Ahead

| Activity Name                                                                | Start       | Finish    | BL Project Start | BL Project Finish |  | 2026 | July 2026 |     |     |     |     | August |     |     |
|------------------------------------------------------------------------------|-------------|-----------|------------------|-------------------|--|------|-----------|-----|-----|-----|-----|--------|-----|-----|
|                                                                              |             |           |                  |                   |  | W25  | W26       | W27 | W28 | W29 | W30 | W31    | W32 | W33 |
| [-] LNG Terminal / Regasification Unit                                       | 04-May-26 A | 28-Aug-26 | 04-May-26        | 19-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| [-] LNG Terminal / Regasification Unit Civil                                 | 22-Jun-26   | 21-Aug-26 | 04-Jun-26        | 05-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| Construction - Roads Stage 2 + Fence, Final finishing excl tarmac and weight | 22-Jun-26   | 21-Aug-26 | 04-Jun-26        | 05-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| [-] LNG Terminal / Regasification Unit - Electromechanical                   | 04-May-26 A | 28-Aug-26 | 04-May-26        | 19-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| [-] Stage I                                                                  | 04-May-26 A | 28-Aug-26 | 04-May-26        | 03-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg1 - NDE, Pressure test Installation Ph1                | 01-Jun-26 A | 26-Jun-26 | 25-May-26        | 29-May-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg1 - Electrical Installation and completion check       | 04-May-26 A | 28-Aug-26 | 04-May-26        | 03-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| [-] Stage II                                                                 | 25-May-26 A | 07-Aug-26 | 25-May-26        | 10-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - NDE, Pressure test Stage II.                     | 01-Jun-26 A | 26-Jun-26 | 25-May-26        | 29-May-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - Process pipes insulation                         | 26-Jun-26   | 26-Jun-26 | 26-Jun-26        | 26-Jun-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - MV Transformer Unit (XE93)                       | 01-Jul-26   | 07-Jul-26 | 17-Jul-26        | 23-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - Electrical Installation and completion check     | 25-May-26 A | 15-Jul-26 | 24-Jul-26        | 10-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - Process pipes insulation                         | 22-Jun-26   | 17-Jul-26 | 25-May-26        | 19-Jun-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg II - Lighting (XE96)                                  | 27-Jul-26   | 07-Aug-26 | 01-Jul-26        | 14-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| [-] Stage III                                                                | 25-May-26 A | 28-Aug-26 | 27-May-26        | 21-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg III - Lightning Protection (XE95)                     | 22-Jun-26   | 03-Jul-26 | 24-Jun-26        | 07-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg III - VIP (B666)                                      | 29-Jun-26   | 24-Jul-26 | 24-Jun-26        | 21-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg III - CO_014_Odorization - Installation               | 27-Jul-26   | 07-Aug-26 | 29-Jun-26        | 10-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg III - NDE, Pressure test                              | 01-Jun-26 A | 14-Aug-26 | 15-Jul-26        | 21-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg III - Electrical Installation and completion check    | 25-May-26 A | 28-Aug-26 | 27-May-26        | 21-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| [-] Stage IV                                                                 | 25-May-26 A | 28-Aug-26 | 05-Jun-26        | 19-Aug-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg IV - Control System (XE90)                            | 08-Jul-26   | 14-Jul-26 | 08-Jul-26        | 14-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg IV - Diesel Generator (XE94)                          | 10-Jul-26   | 23-Jul-26 | 05-Jun-26        | 01-Jul-26         |  |      |           |     |     |     |     |        |     |     |
| LNG - Installation Stg IV - Electrical Installation                          | 25-May-26 A | 28-Aug-26 | 17-Jul-26        | 19-Aug-26         |  |      |           |     |     |     |     |        |     |     |

# Actions

## BOP – 6 Week Look Ahead

