

Weekly Report W29



BOP-IDOM-EHSS – SAFETY MOMENT-Handover in construction W29

SAFETY MOMENT

HANDOVER

IN A CONSTRUCTION PROJECT

A GOOD HANDOVER TODAY, A SAFE TOMORROW.

WHAT IS A HANDOVER?



A handover is the transfer of information, responsibilities and site conditions from one shift, team or contractor to another. It ensures everyone is aligned, aware of risks and ready to continue the work safely and efficiently.

WHY GOOD HANDOVER MATTERS



PREVENTS INCIDENTS
Ensures hazards and critical information are not missed.



IMPROVES TEAMWORK
Keeps everyone on the same page and supports safe collaboration.



INCREASES RELIABILITY
Reduces rework, delays and mistakes by maintaining continuity.



BUILDS ACCOUNTABILITY
Clarifies responsibilities and follow-up actions for all.

KEY ELEMENTS OF AN EFFECTIVE HANDOVER


-  **BE PREPARED** – Review the work, check the status and gather key information.
-  **COMMUNICATE CLEARLY** – Share information in a simple, concise and structured way.
-  **LISTEN ACTIVELY** – Ask questions and confirm understanding.
-  **DOCUMENT & RECORD** – Update logs, permits and action trackers accurately.
-  **CONFIRM & CLOSE** – Confirm the next steps and responsible persons.

OUR COMMITMENT

We commit to making handover a priority, every time.

- ☒ We take the time.
- ☒ We speak up.
- ☒ We listen.
- ☒ We confirm.
- ☒ We care for each other.

TOGETHER, WE BUILD SAFELY. EVERY DAY. 

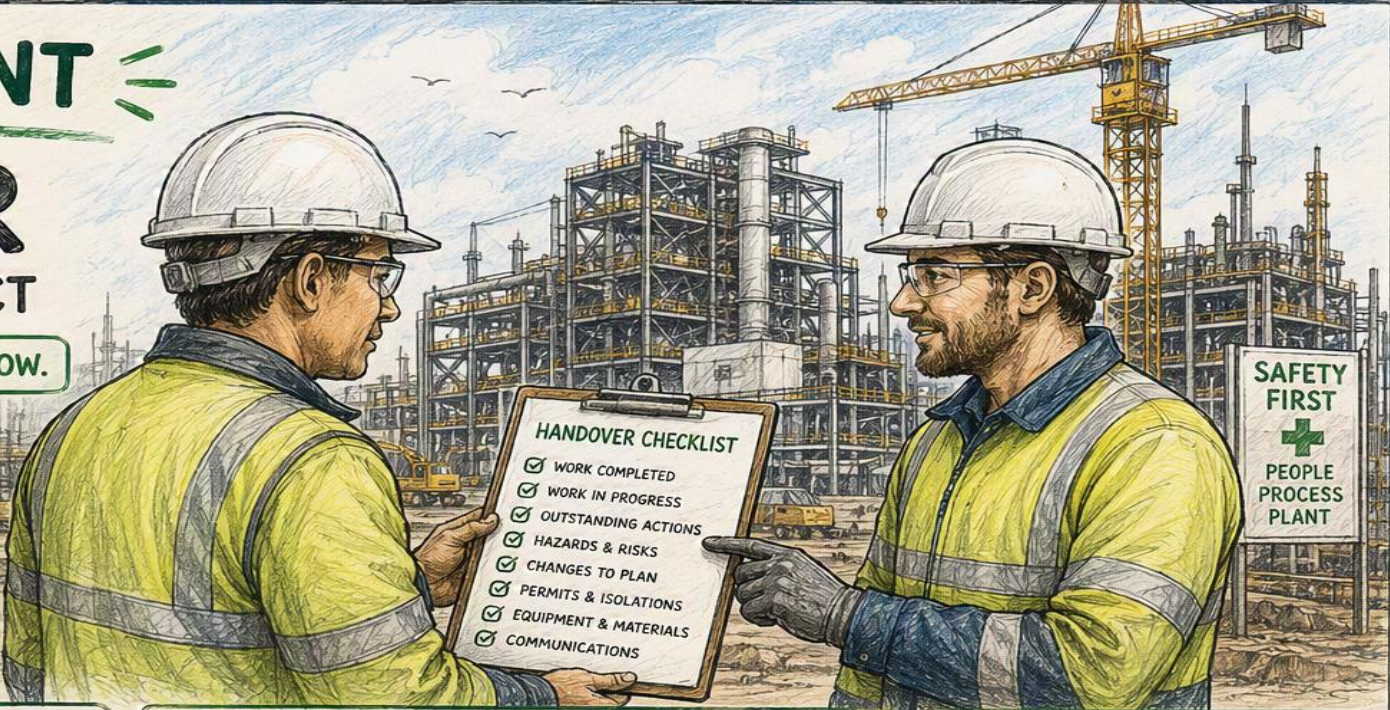

SAFETY FIRST
PEOPLE
PROCESS
PLANT



TAKE TIME. DO IT RIGHT. HAND OVER SAFELY.

SAFE HANDOVER. STRONGER TEAMS. SUCCESSFUL PROJECTS. 

BOP-IDOM-EHSS – DASHBOARD Summary (Week 29)

For information


Lagging Performance Indicators

401 Days LTI Free!!!!

All Incidents & Risks



SIF Potential Classification

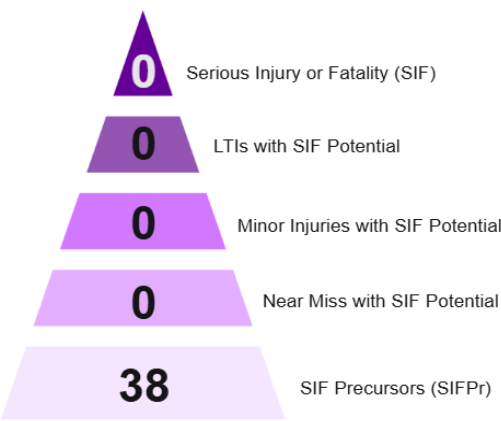

	Project to date	UE Construction	Benchmarking sector
LTIFR	1,55	5	2
TRIFR	5,15	N/A	N/A

Highlights/Downlights of the week:


- Environmental spill PDOP area. No contaminated soil.
- Confined space rescue training/drill with STEGRA ERT in RWFF basement area.
- Fire brigade familiarization/survey LNG Terminal.
- Safety Observations analytical review




Leading Performance Indicators

	Week	Last week	Project to date
SITE WALKS	14	22	980
OBSERVATIONS	77	107	9628
BBS INSPECTIONS	16	25	641
TARGET INSPECTIONS	18	19	328
NEAR-MISS	0	0	48
ENVIRONMENTAL IN	1	0	18
Environmental Corrective Actions Closed on Time	0	0	16
PERMITS TO WORK	48	44	779
RAMS APPROVED	4	2	1
REWARDS	2	6	37
SENDING OFFS	0	0	0


Observations by Reporting Company



Observations by Type

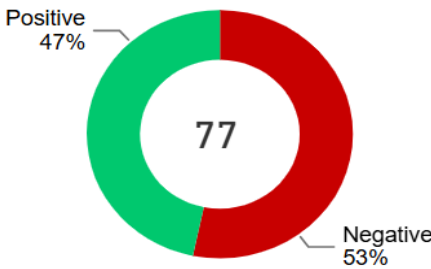

Observations by Resp. Main Contractor




Observations by Category



Total Actions Reported	Open Actions (Clickable)	Closed Actions	Closed Past Due	Open/Closed Overdue Actions (Clickable)
289	35	254	57	35



Site Walks by Reporting Company



Site Walks by Type





CONFIDENTIAL

3

Type of information: General (CUSTOM)

BOP-IDOM-EHSS – Highlights(Week 29)

- Confined space rescue training/drill with STEGRA ERT in RWFF basement area.

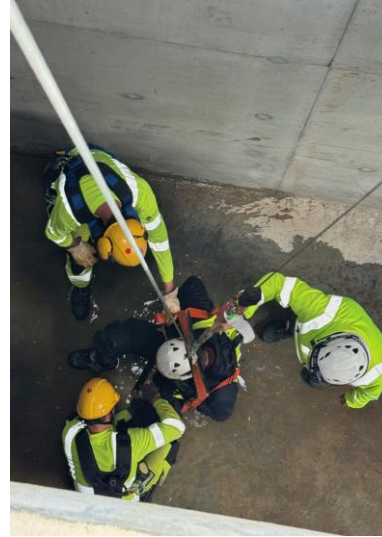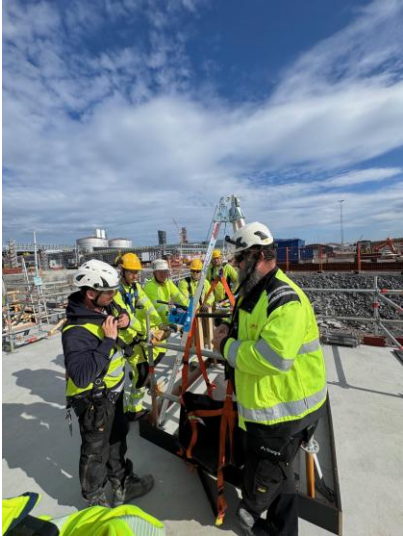

- Fire brigade familiarization/survey LNG Terminal.
- MEWP Training/Practice for Fermix employees




BOP-IDOM-EHSS – BBS Dashboard (Week 29)

Behaviour Based Safety Assessments

Last Update:
20 jul. 2026 03:21

Checklist Name: Toate
Related to Main Contractor: Toate
Major Area: BOP
From Week: 25W24
To Week: 26W29

Safety Performance With TRIF

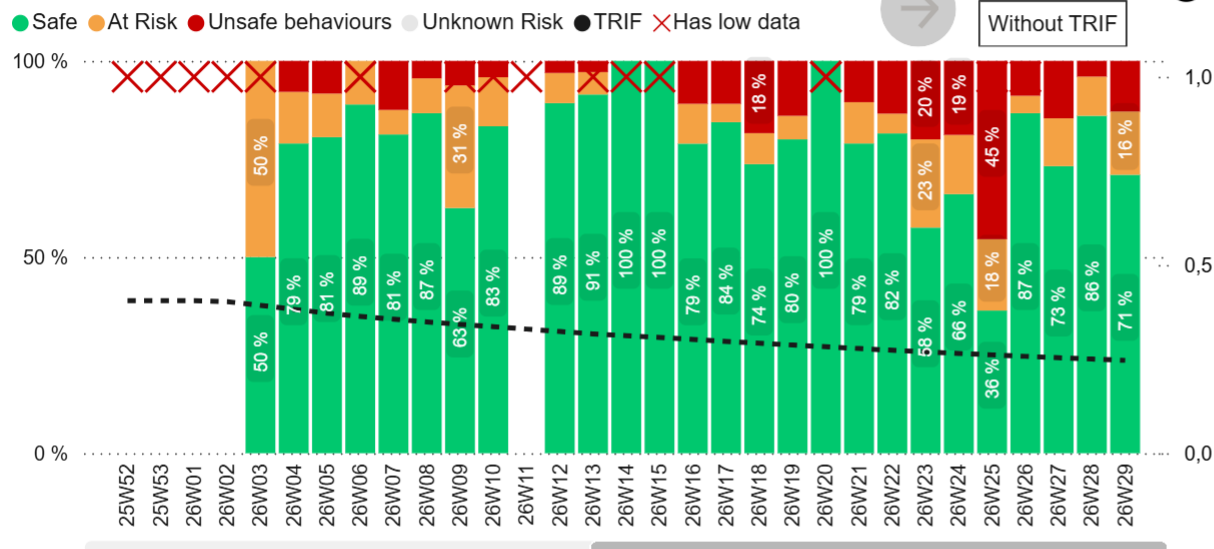


71%
Safety Performance (Last week)
▼ -7.9%
vs Previous period


12,9%
Unsafe behaviours (Last week)
▲ +1.3%
vs Previous period

70
Total assessments (Selected period)
▼ -8
vs Previous period


Safety Performance by Category

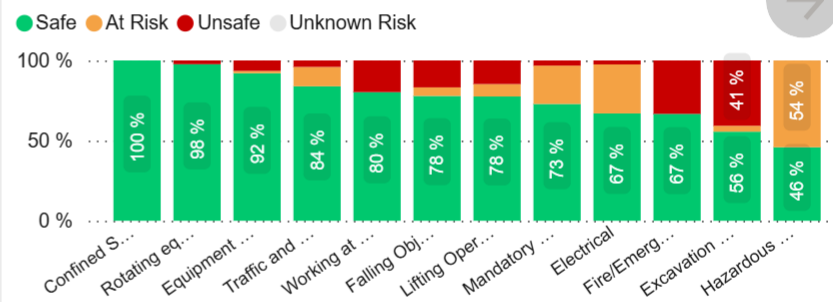


Assessment Timeline

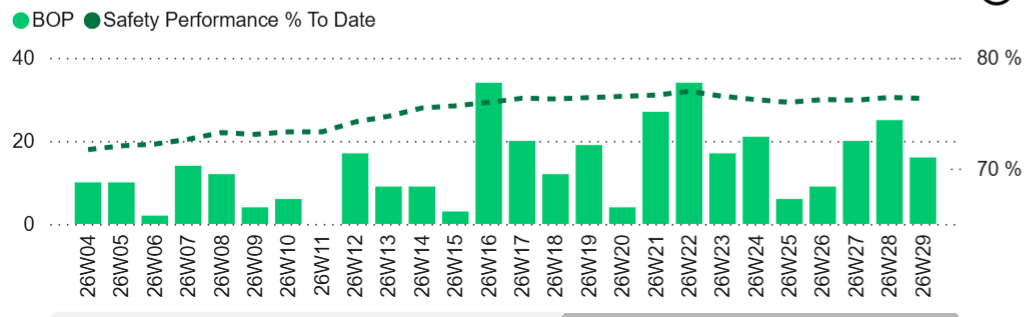

Assessments related to Main Contractor



Feedback distribution

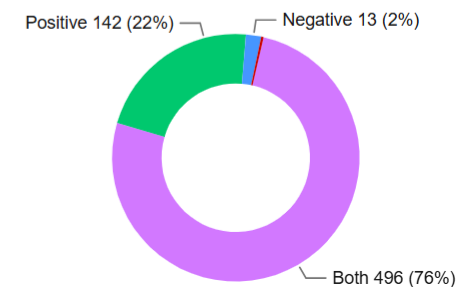

• PROJECT P-103475 · EPCM BODEN BOP

BOP Quality.

Centralized quality control workspace for the **Balance of Plant** scope of **STEGRA's** green steel facility in Boden — the world's first large-scale fossil-free steel plant. Inspection records, ITPs, audits, NCRs and procedures, governed by the IDOM site team.

QUICK LINKS

Team members

EXTERNAL TOOLS

 Airtable · QOC

 Airtable · NCR

 Airtable · NOI

 Omega 365 · EDMS

CLIENT	STAGE	QUALITY LEAD	LAST SYNC
--------	-------	--------------	-----------

QA/QC — Weekly Summary

● KEY ACHIEVEMENTS

- 1 Stegra EPCM Audit had taken place, including BOP and DRP Project. The findings will be communicated next week, clarifications meetings will be followed up, as well mitigation plans.
- 2 PIMs had taken place for Nordic Concrete. MOMs has been issued and distributed.
- 3 PIMs had taken place for STS. ITPs still need to be consolidated; Quality Plan will be review.
- 4 Partial Handover between GRK/Nordic Concrete in RW SIN-907A has been took place. PLs has been issued and follow up.
- 5 GRK-ITPs for Ponds, CW, UG Piping has been released. IDOM QC prepared the Quality Requirements for Moraine Testing for Ponds, Rail Road and agreed with IDOM Eng. and discussed with GRK.

● MAJOR RISKS

- 1 GRK Conducted backfilling activities without NOIs. Regarding UG Piping Construction, ITPs Req. shall be followed.

● LOOK-AHEAD · W30

- 1 Follow up the Partial Handover activities GRK/ Nordic Concrete and Anfra / STS.
- 2 Fermix Pressure Test NOI for Thursday
- 3 Chart Ferrox Pneumatic Test for NOI Wednesday
- 4 GRK- 8 TPs to be review and expedite
- 5 GRK-ITPs Road consolidated to be revised.



0

NEW NCR · W29
EPCM 0 · STEGRA 0

13

NCR OPEN
OF 106 TO DATE



66

QOC OPEN
OF 998 TO DATE




88%

NCR CLOSED
93 OF 106 TO DATE

NCR STATUS BY MONTH

ROLLING 12 MONTHS

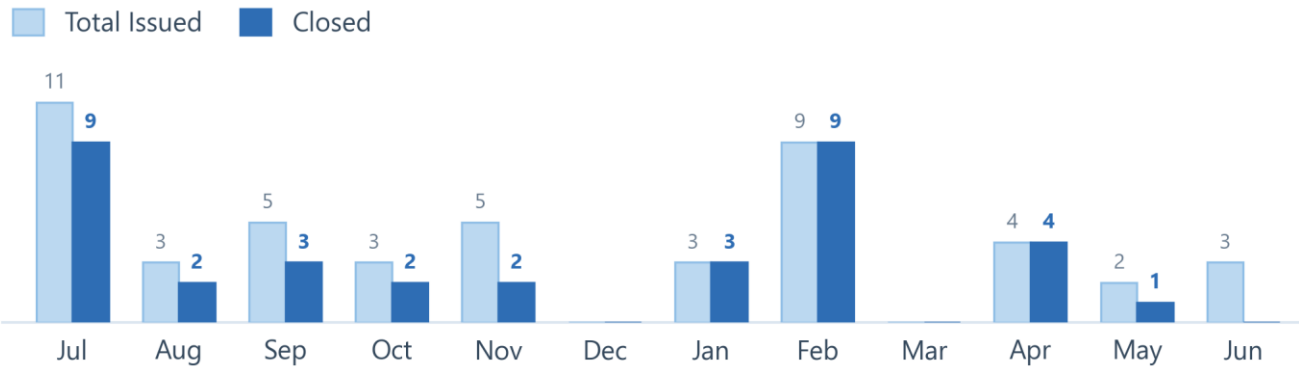

QUALITY OBSERVATIONS & NCR


OWNER	NEW	TO DATE	OPEN	> 30D	> 60D
QUALITY OBSERVATIONS · QOC					
EPCM	9	248	34	18	6
Stegra	2	750	32	15	14
TOTAL	11	998	66	33	20
NON-CONFORMANCE · NCR					
EPCM	0	23	3	1	2
Stegra	0	83	10	0	10
TOTAL	0	106	13	1	12

TEST PACK STATUS

Ferrmix
CHART Ferox
GRK
Nordic Concrete

PLAN	31	SUB	2	REV	1	APR	1	CMP	1	AB	1
PLAN	18	SUB	7	REV	7	APR	7	CMP	6	AB	0
PLAN	0	SUB	9	REV	1	APR	0	CMP	0	AB	0
PLAN	0	SUB	0	REV	0	APR	0	CMP	0	AB	0

PLANNED → SUBMITTED → REVIEWED → APPROVED → COMPLETED → AS-BUILT



QA/QC — NOI & Site Activity


QUALITY PYRAMID



Site activities = NOIs + QOCs + site surveillance

WEEKLY NOI ISSUANCE BY CONTRACTORS

ROLLING 12 WEEKS

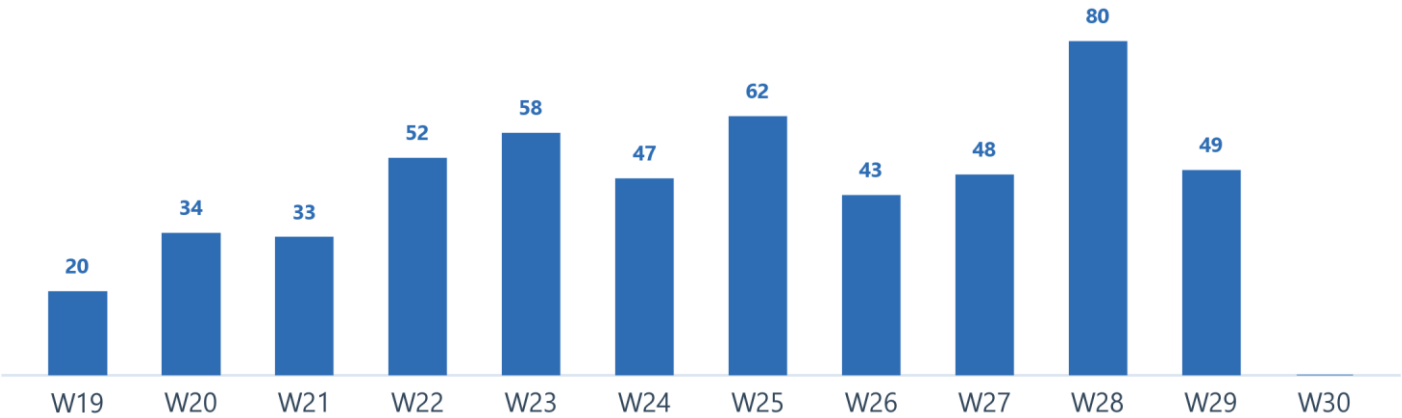

INSPECTION STATUS · W19–W30

Rejection rate 0% · KPI threshold ≤ 5%

METRIC	W19	W20	W21	W22	W23	W24	W25	W26	W27	W28	W29	W30
Accepted	20	34	33	52	58	47	62	43	48	80	49	0
Rejected	0	0	0	0	0	0	0	0	0	0	0	0
Postponed	0	0	0	0	0	0	0	0	0	0	0	0
Rejection Rate	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%

QA/QC — Partial Handover

6 partial handovers between contractors in progress · 1 completed

6 IN PROGRESS

1 COMPLETED

PARTIAL HANDOVER BETWEEN CONTRACTORS

6 RECORDS

DEFINITION	SYSTEM	SUBSYSTEM	TAG NO	ITRS	TCCC	WALKDOWNS	PUNCH LIST	COMPLETED
GRK-Stegra-Municipality Piping	SIN-800-TEMP	SIN-800-01-TEMP	TEMP-BOP-1001-WRW-0800-10P1-NI	P-02A	TCCC	Done	None	Completed
GRK-Stegra-Municipality Civil	SIN-800-TEMP	TBD	TEMP-BOP-Civil_Works_ Temporary Line	C-25A	TCCC	—	—	—
GRK-Nordic RW Area	SIN-907A	SIN-907-01,02	RW Receiving &Pumping Station	TCCC	TCCC	Done	Yes	—
GRK -Nordic LNG Area	SIN-909A	SIN-909A-101	LNG-TCCC from GRK to NOR	TCCC	TCCC	—	—	—
GRK-Nordic -Ferrmix PB Area	SIN-980	SIN/980/01,02	Pipe Racks, Columns,Foundations 1-5	TCCC	TCCC	—	—	—
ANFRA/STS PDOP Area	SIN-987	SIN/987-02	PDOP Capacitor Bank Trenches	TCCC	TCCC	—	—	—

Project Risk Update – Balance of Plant

- 41 total BOP Type 2 risks identified – 20 active, 1 draft, 0 parked, 0 submitted, 16 retired, 3 expired, 1 Canceled
- Out of 20 active risk – 0 critical, 5 major, 11 moderate, 4 minor risks assessed
- 60 total mitigation actions planned for all active risks – 4 overdue, 24 open, 30 closed, 2 canceled

Data Date: 17 July 2026

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R22	Construction & Site Execution	GNRL - Misaligned area schedules and complex multi-contractor interfaces lead to blocked BOP Workfront and delayed equipment deliveries resulting in schedule and cost impacts	30	- Sequence UGP and piping to avoid SMS install clashes; await SMS schedule (31/07/2026 - Open) @Marten Sonnerup - Interface Meeting with STM and BOP Construction team to align UGP works and SMS equipment deliveries. (31/07/2026 - Open) @Marten Sonnerup - Prepare reforecast schedule for BOP and Interface dates with STM and other areas (27/07/2026 - Open) @Reghardt Heunes / Comment: It is under discussion and waiting for the STM-McDermott rebaseline, which currently they are working on - Align and finalize with WTP1 and WTP2 for access dates (31/07/26 - Open) @Marten Sonnerup / Comment: Ongoing discussion, as there is interference with Eiffage due to road works in front of WTP2, where Eiffage is scheduled to carry out works; an alternative northern access is also under discussion.	19
B1.BOP.R10	Construction & Site Execution	RAIL - Late Handover of STM Construction Areas (Scrapyard, CLP) – Impacting Rail	25	- Follow up on Micropiling progress in Scrapyard area (15/08/2026 – Open) @Roger Campbell / Comment : Work must be completed by mid-August to allow follow-on activities. Delays beyond early September will impact rail works and may place them on the critical path, with potential multi-month delays due to winter. The micro-piling contract has not yet been awarded by STM-McDermott, there might not be a short list in place; since execution takes ~8 weeks, award is required within the next few days to enable rail works to start in September as planned. Stegra have instructed STM-McDermott to provide an acceptable rebaseline.	23
B1.BOP.R548	Construction & Site Execution	Pipe Bridge (21) Modules Install blockage by STM and may need to be paused	21	- Finalize decision on BOP continuation of 19 modules and confirm if need by dates of utilities will still be met (31/07/2026 – Open) @Chris Van Der Berg	14
B1.BOP.R387	Construction & Site Execution	PDOP - Uncoordinated Installation of HV and Control Cables leading to blocked handover by HESE resulting in delay of permanent power	19	- HESE to review IFC prior to Production & Construction (31/08/2026 - Open) @Tomas Winter - HESE to define required documentation prior to Handover (31/08/2026 - Open) @Tomas Winter - [Stegra to] review and possibly revise [its] handover procedure to include electrical installation works (31/08/2026 - Open) @Tomas Winter	11
B1.BOP.R565	Project Delivery General	UGNW - Av 9 Underground piping installation may not be completed by end of 2026	19	- Award Avenue 9 scope to another contractor who is already working on site (to avoid loss of time due to running a tender and subsequent mobilisation) (31/07/2026 – Closed) @Tuncay Ozel	19

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.

Project Risk Update – Balance of Plant (2/2)

(Reviewed by Stegra and Idom Risk Management)


Status and summary comments as per *previous* week.

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R323	Construction & Site Execution	PDNW - Resource shortfall for Power Distribution Network (Single Source E&I) may impact construction progress	14	- Engage additional E&I resources or contractors to meet required manpower levels (31/07/26 – Open) @Tuncay Ozel / Comment: The Call-Off package was shared with STS on 13 July, while the OMEGA workflow was launched to support Stegra’s internal approval. STS confirmation and the ongoing signature process remain pending. - Closely monitor workforce allocation between STM and BOP to avoid bottlenecks (30/04/27 – Open) @Guillaume Camerini	9
B1.BOP.R436	Supply Chain Management	TEMP - Availability of emergency Diesel Generator TG4	5	- TG4 is scheduled for late May, and the contract signing for mid-June. (14/08/26 – Open) @Tuncay Ozel / Comment: The bidder has confirmed updated proposal submission in W30. Subject to receipt and review of the revised proposal, TG4 is scheduled to be issued in W31.	5
B1.BOP.R484	Construction & Site Execution	PCRU - Pipe Bridge – Hydrotesting activities may get pushed into 2026–2027 winter period due to delayed prerequisites. (QLT)	15	- Develop an overall hydrotesting program, which final completion of last hydrotesting activity is before the start of the 2026–2027 winter.(30/09/26 – Open) @Javier Cervera / Comment: It is confirmed that glycol will not be used; therefore, no hydraulic piping tests will be conducted during winter.	11

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.



PIPE BRIDGE (Target W35)



NPB-511 (Target W37)



PROGRESS W29

- CR approved for Siemens repair works. Siemens confirmed start of repairs W32
- Inspections ongoing for Pipe Bridge earthing. ITP for testing released

BLOCKERS	RESPONSIBLE
----------	-------------

- | | |
|--|-------------|
| ● PB EARTHING DELAYS ON INSTALLATION, INSPECTION & TESTING → | FERRMIX |
| ● ACTEMIUM ITR APPROVAL → | STEGRA |
| ● GRK/FERRMIX ITR APPROVAL → | IDOM/STEGRA |

PENDING ACTEMIUM/EITECH ITRs	PROGRESS
-Pipe Bridge Underground Earthing →	0% [Linked to (3)]
-NPB-511 underground Earthing →	0% [Linked to (5)]
-ELA-01 roof trays →	50%
-NPB-511 MV, LV & Control Cables →	50%
-Temp Trafos to NPB-511 MV & Control Cables →	50%
PENDING GRK ITRs	PROGRESS
-Pipe rack foundations, Columns & groundworks →	0%
-NPB-511 groundworks →	0%
-Temporary transformers Groundworks & Lightning mast →	30%
PENDING FERRMIX ITRs	PROGRESS
-Priority 1 zones 3-4-5-6 Structural & Cable racks →	10% [Linked to (1)]

BOP-IDOM-Temporary Water Progress

W29

4

Milestone

3

High priority

W33

Target

Oct

NIWA on site

Status by Milestone

	Progress	Priority / target*
1 Permanent RW pipes around RW Chamber Approved commitment since 11 May by STEGRA PM; no action taken from GRK.	50%	High W33 1
2 Temporary spool + RW tank inlet CR-04387 raised 14 May. Commercial agreement still open. Since May, GRK only submitted price proposal on one occasion.	0%	High W32 2 3
3 Temporary lines TWTP → ASP CR-4359 raised 5 May for connection to ASP. Commercial agreement still open. Since May, GRK only submitted price proposal in 2occasions.	95%	High W31 2 3
4 RW tank watertightness test Test done W26. Test failed. C3C to come W32 to repair.	90%	Low W33

*Targets can be achieved only if blockers are resolved this week.

BLOCKERS / CONTRAINS

- 1

Commercial action to GRK

Apply pressure / penalty if no action is taken
- 2

CR Review resources


Add resources to reduce CR review time. Average review time in ACC 67 days
- 3

Strategic route GRK TEMP or NIWA

Strategic Decision Required: Proceed with the temporary water solution or transition to the permanent solution. NIWA to install → milestone 2 and 3. NIWA starts in October and finalize January as per contractual schedule

BOP | IDOM Level 1 Schedule

Progress

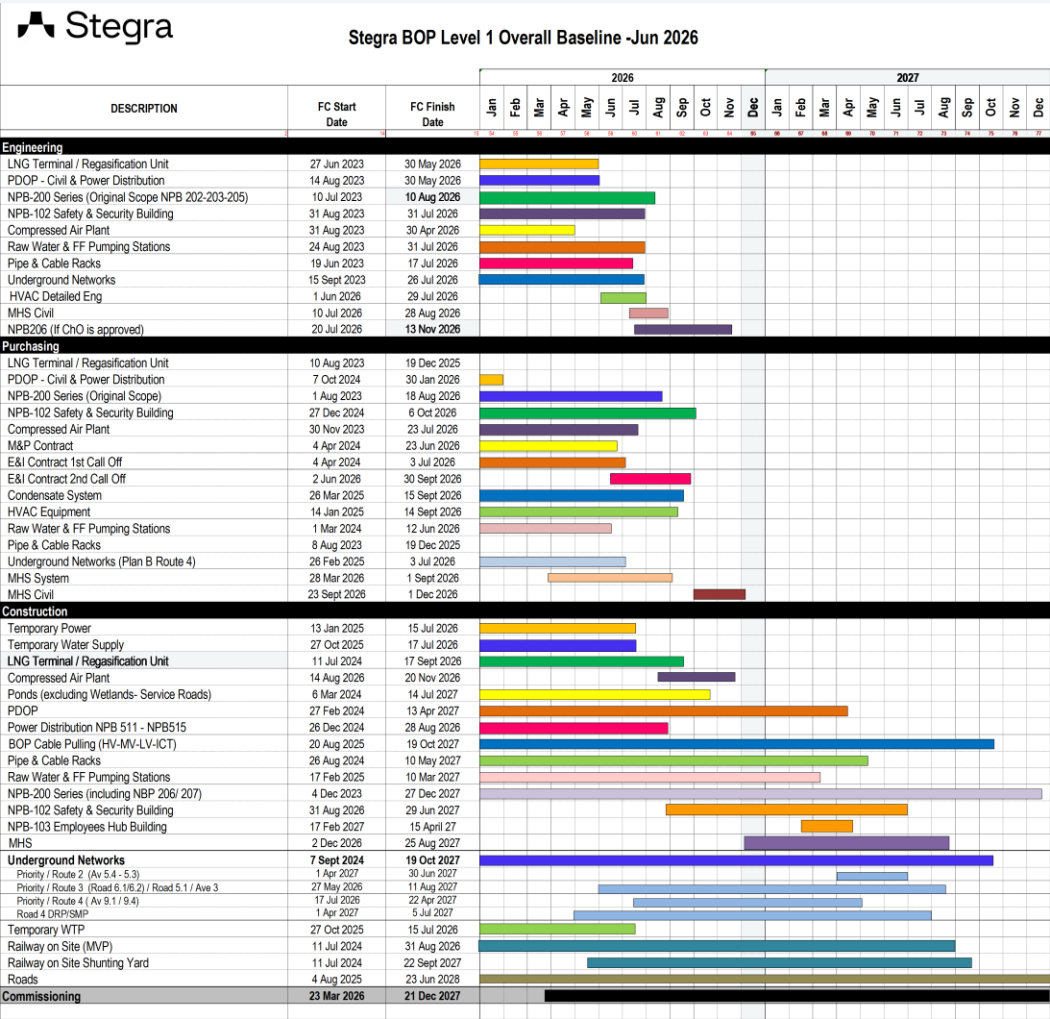

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue

Risk / Concern


Behind

BOP | IDOM Summary – Activities and Progress


Progress

Overall Progress		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering	Week	0,06%	0,19%	0,18%	31%	30%	0,18%
	Cumm.	97,12%	97,91%	97,34%	100%	99%	97,52%
Procurement (TG - Purchasing Process)	Week	0,18%	2,70%	1,33%	14%	7%	2,35%
	Cumm.	67,44%	73,95%	68,60%	98%	91%	70,95%
Manufacturing (On a Monthly Basis - Monthly Cut Off)	Week	0,00%	0,00%	0,00%	100%	100%	1,64%
	Cumm.	92,56%	92,56%	92,56%	100%	100%	94,20%
Construction	Week	0,71%	0,38%	1,07%	66%	188%	0,48%
	Cumm.	51,45%	52,70%	52,01%	99%	98%	52,49%
Overall	Week	0,43%	0,33%	0,70%	62%	129%	0,86%
	Cumm.	67,48%	68,51%	67,87%	99%	98%	68,73%

6-month key Waypoints		
Key Waypoints	Planned date	Forecast date
Temporary Water (Ready to Supply)	31 Jul 2026	30 Oct 2026
Temporary Power (Ready to Operate)	30 Jul 2026	30 Sep 2026
Power Supply from NPB-511 to ASP	31 Jul 2026	30 Sep 2026
Piping Connections - Priority 1 Finish	28 Aug 2026	28 Aug 2026
P2 – Pipebridge Installed + Piping Connections Finish	23 Oct 2026	23 Oct 2026
P5 – Pipebridge Installed + Piping Connections Finish	28 Aug 2026	28 Aug 2026
P4 – Pipebridge Installed + Piping Connections Finish	19 Nov 2026	27 Nov 2026
Priority 1 UG piping installation completion	17 Jul 2026	30 Sep 2026
Electrical Works by STS Start	06 Jul 2026	27 Jul 2026
Railway Groundworks Crossings Start	15 Jun 2026	17 Aug 2026

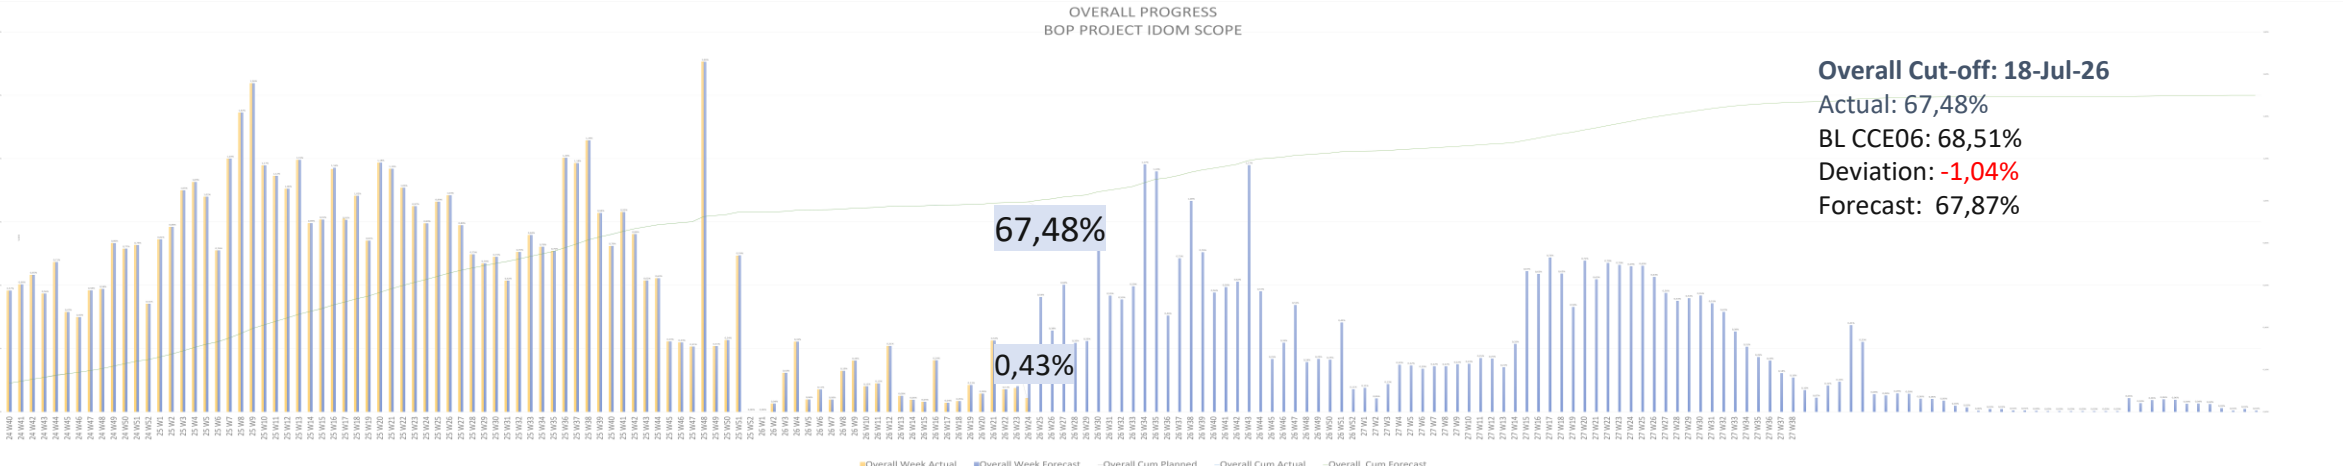

BOP - 6 Weeks Look Ahead

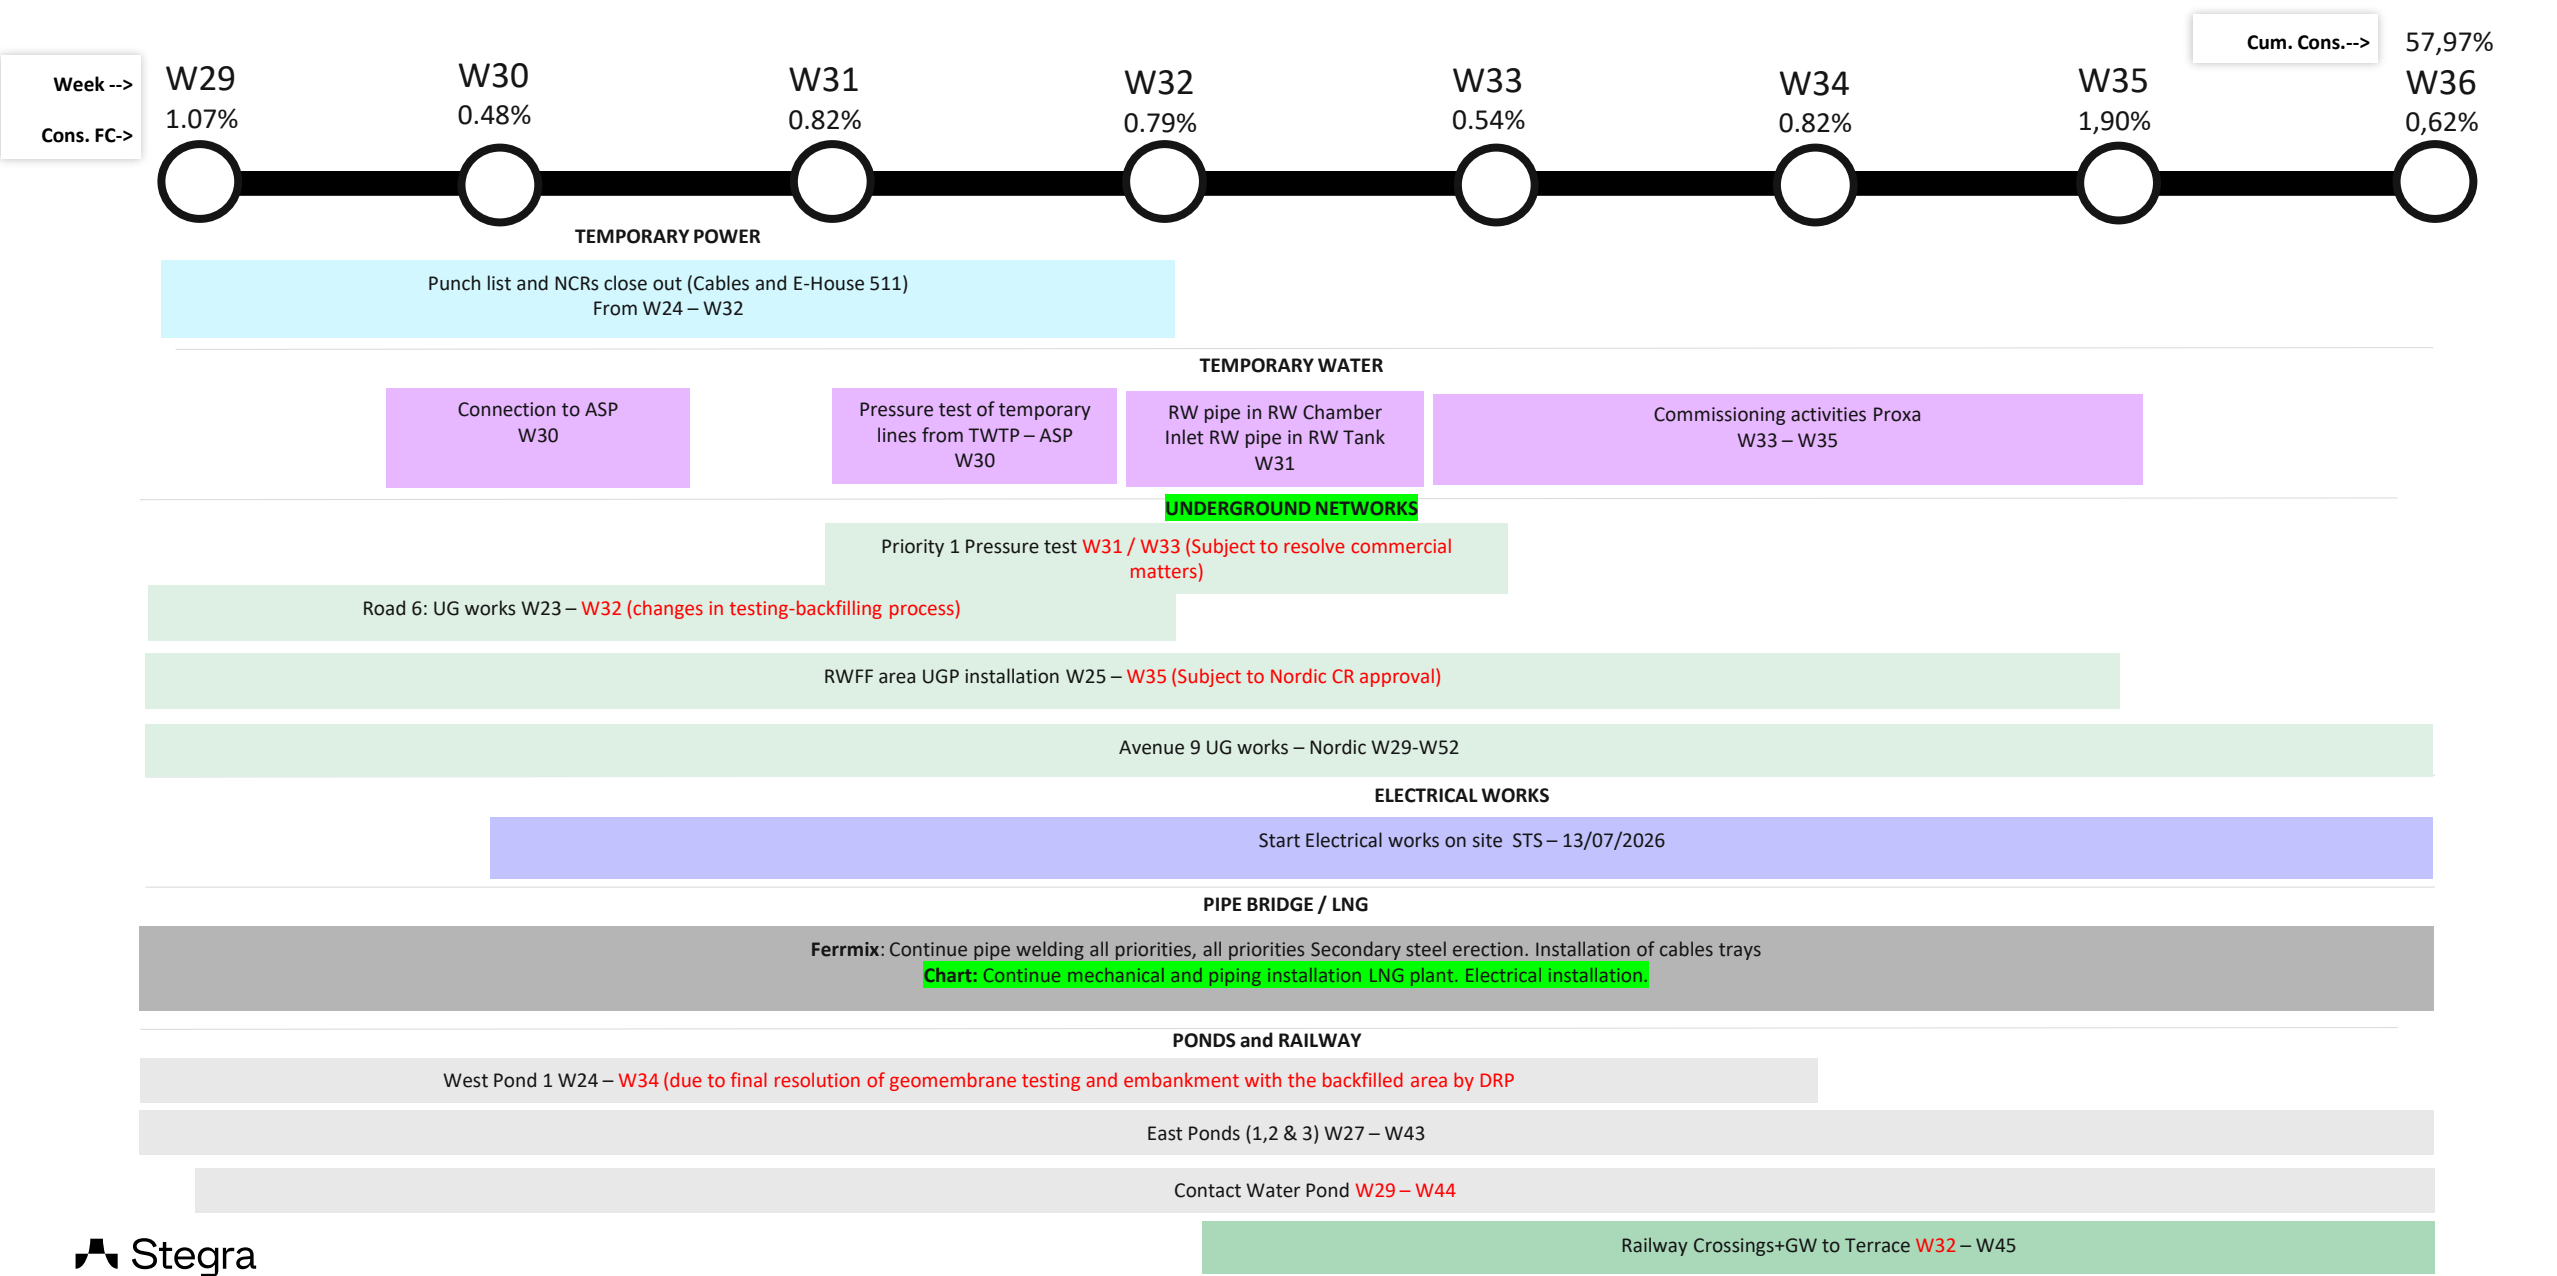

BOP | IDOM Summary – Activities and Progress -100 days look ahead

W29

Main deviations and mitigating actions

Discip	Red Activity	Due date	Mitigation Action
Proc	Chemical Dosing system for RW	W26	- Proxa: Final proposal and CRS responses expected by the end of Week 30 or early Week 31. - KURITA: RFQ for Basic design sent. they confirm that will present the proposal on week 31. .
Proc	NPB-102: Security Bldg	W27	Several companies involved in the procurement process: - Nordia: (€3.6 M offer under the clarification phase). - LC: quotation expected by 14/08/2026. - KSH: partial offer excluding interior distribution scope. - MKL BAU Sp.: quotation expected by 14/08/2026. Steel structure supply and erection only. - Plus 10 additional companies have been contacted. Waiting their responses.
Proc	PB & Air Compressor found. - Retender	W27	Call-off #3: PGB aproved, Commercial and contractual alignment is ongoing, and we are awaiting Nordic's updated BOQ to finalize the package.
Proc	E&I Call-Off 1	W27	STS contract documents totally agreed. Contract to be signed on W30.
Proc	GW commitments	W26	- East ponds, Contact water pond and GW+crossings railway are executed. Ponds KoM held in W25. GW workshop w31. - East ditch. Status: Acknowledge. Pending to be executed. Warning! This is a predecessor for ROS GW in sections 4 and 5.
Eng	Sweco	W30	- Road design packages expected before summer break will come after w36. No clear delivery dates available. - Rail Memo 20. Received only partially on 03/07. Missing service roads update and GW deliverables. Railway memo 21 will come after summer break. - Earthing. Ongoing discussions to clarify the scope. In parallel, Sweco is analyzing the existing information and preparing the team to start the production. - Fencing. Sweco will raise two CR: CR-4433 for BOP/Steel Mill and a new one for HMP. Stegra (&IDOM's) to provide feedback on the 4,250 hours for BOP.
Eng	Hydrogen pipeline crossing (Railway Section 4A)	W52	Hydrogen pipeline crossing. Alternative 3 is the chosen solution. Sweco raised CR-04439 for the Geotechnical investigations required for the Hydrogen pipebridge design, CR-04441 for the culvert under the railway (w38 expected the IFC if the CO is ready by w33) and they will raise a third CR for the design works for the civil work design on the pressure berm.
Con	Field Change Requests	W31	Stegra/IDOM to define the procedure on site for Filed Change Request and the Red-marked drawings, to establish how to include changes in the design due to construction reasons.
Con	PB Piping Connections + Pending Fittings	W35	WK29 2026- 19 welders working vs 20 forecast. 660 Forecast inches/week, Actual 517 inches/week
Con	GRK - Temporary power and WTP	W35	RW: temporary line in RW chamber CR discussion ongoing, RW tank filling pipe and overflow system Material delivery Week 28, temporary pipes to TWTP to ASP CR discussion ongoing. Temporary power punch list close out ongoing

Last Week Key Achievements


- ✓ **Significant progress:** 517 Inches welded and 4% progress achieved during this week. Total 13.645 inches out of 20.841 welded done **65% progress achieved.**
- ✓ Cable pulling: Total 9.851 out of 43.553 - 23% progress achieved
- ✓ East ponds excavated 4500 m3 out of 71000m3 – **6,3% progress achieved**



Distribution (Power) – Activities and Progress

Progress

PDOP Progress		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	99,25%	99,25%	99,25%	100%	100%	99,25%
Construction - PDOP	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	92,82%	92,68%	92,56%	100%	100%	92,56%
Construction - NPB 511	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	84,69%	84,69%	84,69%	100%	100%	84,69%
Temporary Power		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Construction - Temporary Power	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	99,00%	99,00%	99,00%	100%	100%	99,00%

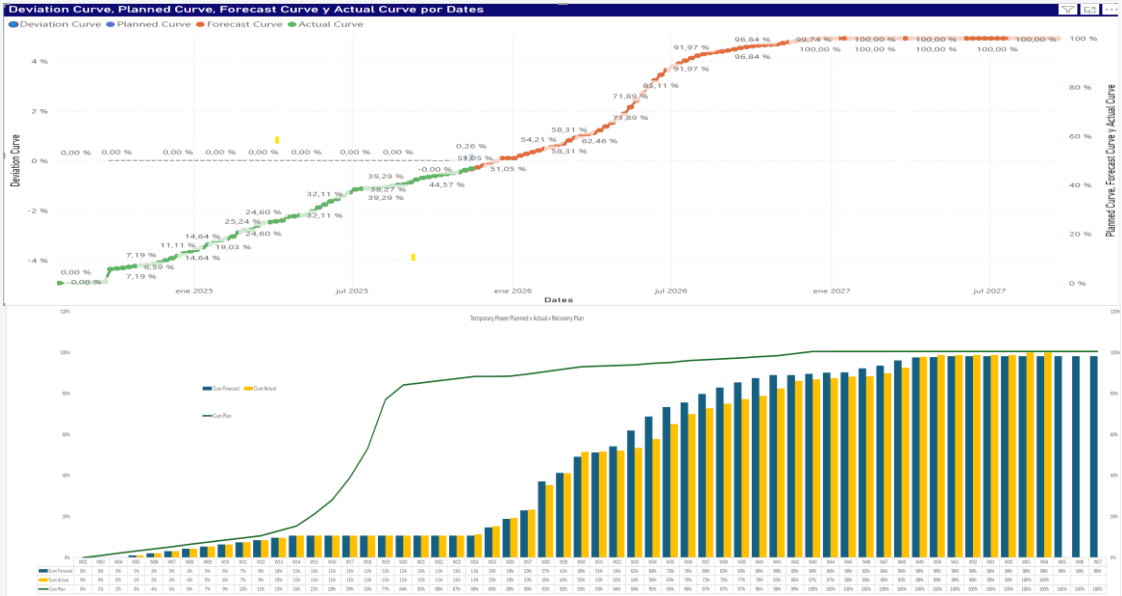


Main deviations and mitigating actions		
Discipline	RED Activity	Mitigating action
Con	Actemium: Delay PB and NPB511 UG earthing completion	Pending contractual agreement Stegra/Actemium
Con	SIEMENS: Delay to finalising NPB511 punch items	Siemens mobilization to site (expect WK33). 1 week is needed to close punches

6-month key Waypoints		
Key Waypoints	Planned date	Forecast date
Mechanical Completion Temp Power	30 Jul 2026	30 Sep 2026
Electrical Works by STS Start	06 Jul 2026	27 Jul 2026

BOP | Gas LNG – Activities and Progress

Progress

LNG Progress		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Construction -LNG	Week	1,63%	1,86%	3,73%	44%	87%	1,00%
	Cumm.	88,65%	91,99%	91,70%	97%	96%	92,70%

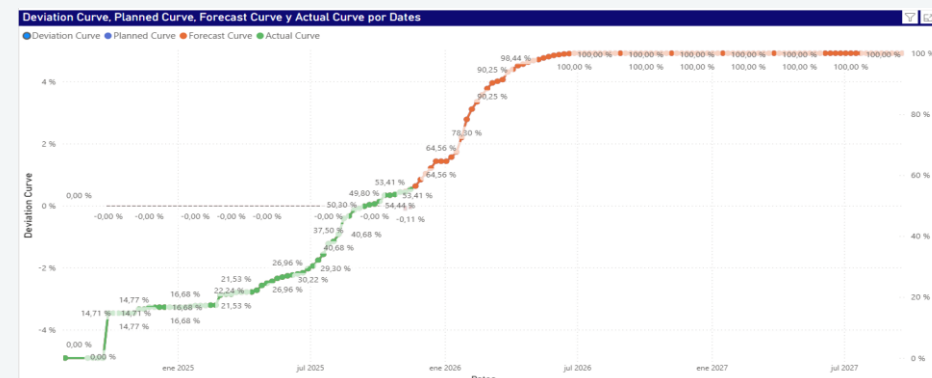

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Civil Works complete (remaining civil works)	17 July 2026	08 Oct 2026
Commence Control System Cabinet installation	08 Jul 2026	10 Aug 2026

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Ele	MV Transformer delivery date postponed (ETA 2 nd Oct 26)	Expediting action
Ele	Control Systems (2 containers) delivery date TBC	Expediting action
Ele	Odorization unit delivery to site end of July 26	Expediting action

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Distribution (Pipe Bridges) – Activities and Progress

Progress

PB & UGP Progress		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,18%	0,18%	0,18%	100%	100%	0,15%
	Cumm.	99,85%	99,85%	99,85%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Pipe Bridge (Foundation+Steel)	Week	0,31%	0,31%	0,44%	70%	100%	0,52%
	Cumm.	84,65%	83,99%	84,96%	100%	101%	85,48%



6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Piping Connections - Priority 1 Finish	28 Aug 2026	28 Aug 2026
Piping completion Priority 1 Finish	23 Oct 2026	23 Oct 2026
Pipe rack Modules - Priority 4 Finish	24 Aug 2026	01 Sep 2026
Pipe rack Modules - Priority 3 Finish	25 Sep 2026	09 Oct 2026
Pipe rack Columns - Priority 4 Finish	20 Aug 2026	27Aug 2026

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Con	PB- Piping connections + pending fittings	WK29 2026- 20 welders working vs 20 forecast. 660 Forecast inches/week, Actual 517 inches/week
Con	PB02. Foundation not possible due to works by Mc Dermott	McDermott piping pending. Focus on other areas/ Award civil works contractor to start works.
Con	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	Confirmation from Stegra to proceed with execution/ Award civil works contractor to start works.
Con	Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott.	Foundations can be start when McDermott release the area


Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue Risk / Concern
 Behind

BOP | Distribution (UG piping) – Activities and Progress

Progress

PB & UGP Progress		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,18%	0,18%	0,18%	100%	100%	0,15%
	Cumm.	99,85%	99,85%	99,85%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
UG Piping (Schedule)	Week	0,60%	0,61%	0,74%	81%	99%	1,26%
	Cumm.	18,15%	18,91%	18,66%	97%	96%	19,93%

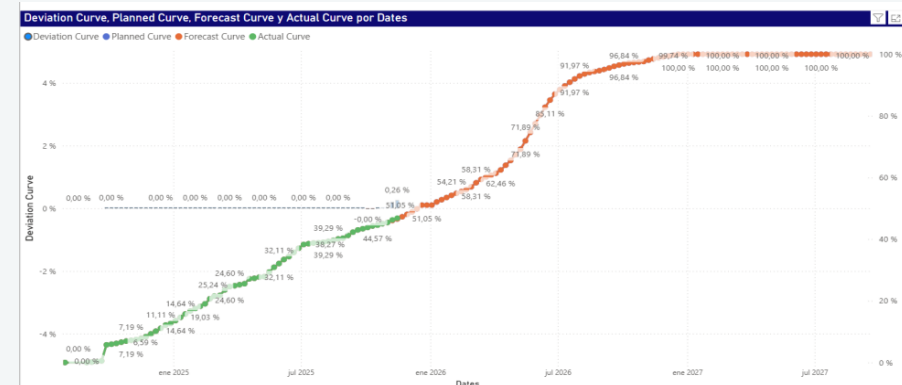

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
UGP – Route 0 testing complete	26 Jun 26	07 Aug 26
UGP – Route 1 Completion Av. 9.5	31 Jul 26	07 Aug 26
UGP – Route 2 Commencement	01 Apr 27	01 Apr 27
UGP – Route 5 Completion	11 Nov 26	11 Nov 26
UGP – RW & FW Completion	06 Oct 26	06 Oct 26

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Piping	Priority 0 (Potable water tank area) UG piping to be connected	Fire hydrant to be relocated by site services
QAQC/Proc	Pressure tests in Priority 1 to be done	Test pack approval and CO signature
QAQC/Eng	Road 6 - Backfilling	ITP to be approved

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue

Risk / Concern


Behind

BOP | Buildings & Other IDOM – Activities and Progress

Progress

Buildings & Others Progress

		W29-26 (Last W) 13/07-18/07					W30-26 (Current W) 20/07-25/07	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,04%	0,04%	0,04%	100%	100%	0,04%	
	Cumm.	97,27%	97,27%	97,27%	100%	100%	97,31%	
Procurement (TG)	Week	0,74%	0,46%	0,74%	100%	161%	2,15%	
	Cumm.	77,96%	81,82%	78,01%	100%	95%	80,11%	
Construction - RWPS & FF	Week	0,07%	0,07%	0,07%	102%	101%	0,00%	
	Cumm.	74,72%	74,72%	74,86%	100%	100%	74,72%	
Construction - NPB 200	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	55,95%	55,95%	55,95%	100%	100%	55,95%	

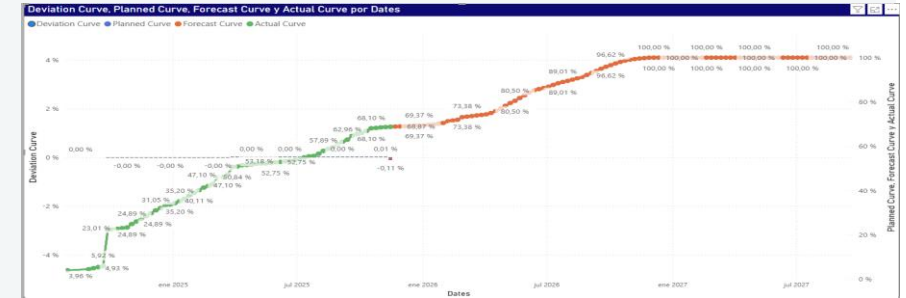

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Commence RW Pumping station building erection	10 Sep 2026	10 Sep 2026
Commence FF Pumping station civil works	14 Sep 2026	14 Sep 2026
Commence RW Pumping station equip. installation	30 Nov 2026	30 Nov 2026
Commence FF Pumping station building erection	19 Oct 2026	19 Oct 2026
Commence NPB205 civil work	19 Aug 2026	19 Aug 2026
Commence NPB102 civil work	31 Aug 2026	31 Aug 2026
Temporary WTP start operation	31 Jul 2026	30 Oct 2026

Main deviations and mitigating actions


Discipline	RED Activity	Mitigating action
Eng	NPB 207 – Crane Maintenance Workshop: Meeting conducted with STEGRA. Progress has been made but there are still open points.	Confirm whether building is required, define procurement strategy and utilities needs
	NPB 202 – Building on hold due to ongoing discussions concerning storage capacity and need for sprinkler system	Fire extinguishing system needed Pending building layout and rack distribution Chemical storage room layout, fire resistance requirements, containment method
	NPB 203 – Refractory Warehouse	Confirm design change insulated vs non-insulated building concept
	Chemical Container – oils and lubricants and Supplier container outside NPB 202: STEGRA engineering has retained three alternatives	Stegra to communicate power needed and any other utility depending on network under IDOM scope of design
	Review of fire detection and alarm and sprinkler system drawing by certified engineer - Pending to have a plan from certified engineer to complete the review of the BOP documentation. No review has been started yet.	Stegra to expedite this process to avoid major impacts to procurement, installation...
Con	RW Chamber temporary spool and RW Tank inlet pipe	CR to be approved

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
 ■ Behind

BOP | Engineering

Progress

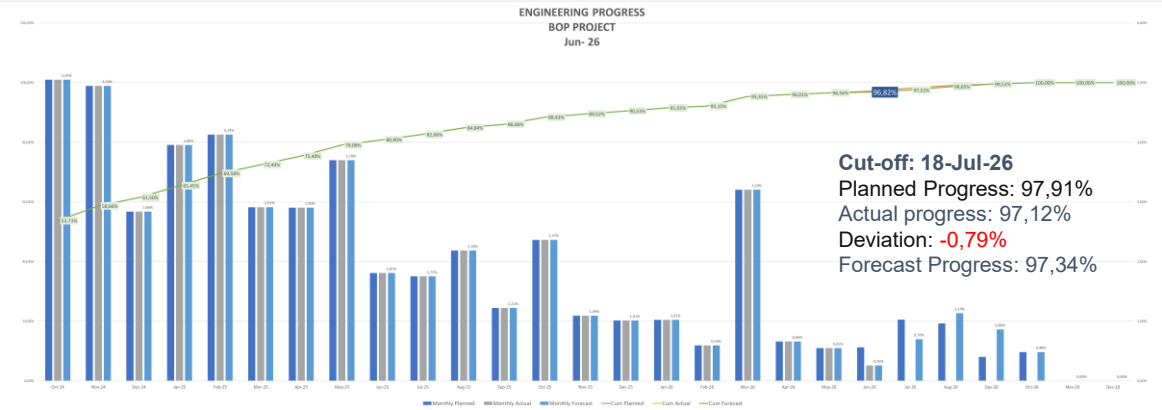

Plan deviations

RED Activity	Plan date	Fcst date	CP impact	Mitigating action	Who	When
UG system PB02 - PB05 and other areas excav. dwg.	Jun-26	Jun-26	Y	- Monitoring Sweco contractual commitments - Splitting UG works in several contractors	Sweco IDOM Stegra	


Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
IDOM Integration Drawings & Excavation models UGP	IDOM has communicated to Sweco the deadlines by which they must provide the inputs for UGP design of all areas pending combined drawings and excavation models. Upcoming deadlines for Sweco: - CSP-WTP2 Area (Av. 6.0-6.1): 08-05-2026 (Delivered) - Priority 4 (Av. 9.3-9.4): 13-05-2026 (Delivered) - Priority 3 zone D (Av. 2.0): 20-05-2026 (Delivered) - Priority 5 (Road 7.5): 20-05-2026 (Delivered) - Finishing Area: 29-05-2026 (Delivered) - DRP-SMP area (Road 4): 26-06-2026 → Sweco to deliver drawings in September. 2D and 3D models were provided in w27 - DRP-Scrap yard area (Av. 9.1-9.2): 17-06-2026 (Delivered)	IDOM/Stegra	Sep-26	Open	Ongoing
Underground Piping Priority 0 Underground Piping Priority 4 Underground Piping Road 5.1 and 5.2	- Prio 0: Final revision removing holds in the roundabout in Av. 1 is moved to September. Prio 4: IDOM is progressing with combined UGP IFC drawings. SWECO is analyzing the possibility of adjusting the design to reduce the meters of linear drainage/contact water gulleys to reduce overall material and installation costs. Pending response from Stegra. - Road 5.1 and 5.2: IDOM and Sweco UGP IFC drawings have holds from pipes going to NPB 207 – the design for this building is not developed. IDOM shall resubmit the IFC for combined drawings for Road 5. Sweco design is available.	IDOM/Stegra	Sep-26	Open	Ongoing

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Sweco Engineering Management (IDOM EPCM – SWECO)

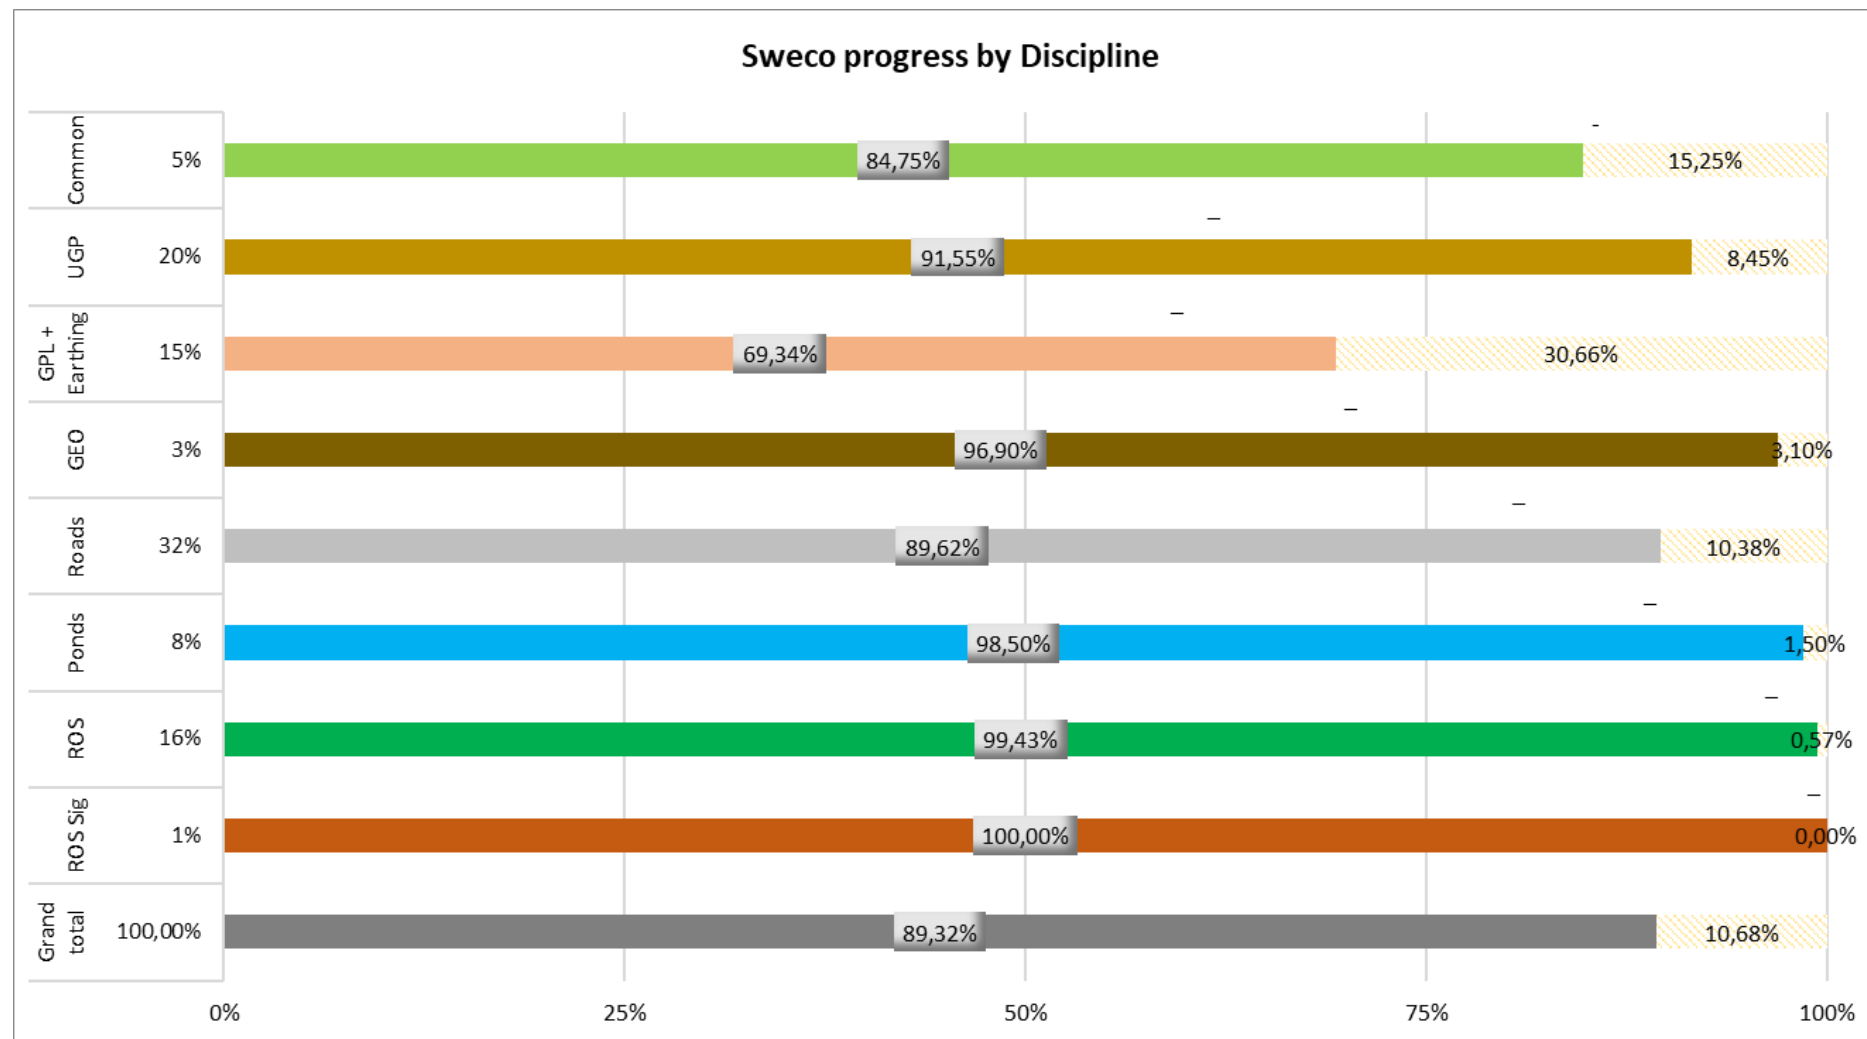

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
■ Behind


BOP | Sweco UGP Construction Readiness

Sweco UGP

Sweco							
Phase	Package	Construction Sta	Construction En	IFR	IFC	BoQ	Comments
1	Road 7.1 (Priority 1)	abr-26	ago-26	-	23/01/2026	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Av. 9.5 (Priority 1)	abr-26	jul-26	-	21/01/2025	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 7.5 + Road 9 (Priority 5)	abr-26	jul-26	-	10/12/2025	14/11/2025	- There is an area on-hold for the pipes going into STM cold mill and the railway area (BOD-SIN-UPB-CIV-DRWGA-00015) - Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 6.2	abr-26	jul-26	-	11/02/2026	17/04/2026	Package 2 BoQ is already available in IFC (Dedicated BoQ for Road 6 delivery date is indicated)
1	RW+FW tanks area + Road 8	abr-26	ago-26	-	23/01/2025	18/03/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Scrap road 1	abr-26	ago-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Av. 9.3-9.4 + Av. 6.0	may-26	-	21/01/2026	12/05/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due clashes with McDermott in Av. 9.3 (BOD-SIN-UPB-CIV-DRWGA-00023 + BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 (Av. 6 not included)
2	Road 5.1	jul-26	oct-26	-	05/12/2025	26/03/2026	- Area on-hold due to missing TOPs to NPB207 (BOD-SIN-UPB-CIV-DRWGA-00022) - Package 5.1 BoQ includes all of Road 5 (no dedicated BoQ for Road 5.1)
2	Av. 9.1-9.2	jul-26	mar-27	16/12/2026	08/07/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due to the slope designed in Av. 9.1 (east of DRP) (BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4
2	ELA01 & PDOP	jul-26	oct-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
2	Parking 1 area	jul-26	oct-26	23/01/2026	29/05/2026	08/07/2026	- IFC drawings in Omega are available, however there will be a new revision due to UGP being on-hold in this area (BOD-SIN-UPB-CIV-DRWGA-00017 + BOD-SIN-UPB-CIV-DRWGA-00013) - Package 0 (no dedicated BoQ for UGP in Parking 1). BoQ available is in IFR from 30/09/2025
4	Road 4 + Av. 2.0	abr-27	oct-27	11/07/2025	30/08/2026	30/08/2026	Drawings in Omega are IFC but there will be an additional revision due to multiple adjustments (TOP changes, etc.)
4	Av. 6	abr-27	oct-27	25/03/2026	12/05/2026	08/05/2026	
4	Av. 5	abr-27	oct-27	11/02/2025	01/04/2026	20/05/2026	Drawings are IFC in Omega, however there will be another revision due to TOP & design changes due to McD STM
4	Av. 4.1	abr-27	ago-27	-	11/02/2026	27/05/2026	
4	Av. 3.4	abr-27	ago-27	-	11/02/2026	03/06/2026	
4	Av. 3.2 + 3.3 + Road 5.3	abr-27	ago-27	-	11/02/2026	02/04/2026	

BOP | Procurement

Progress

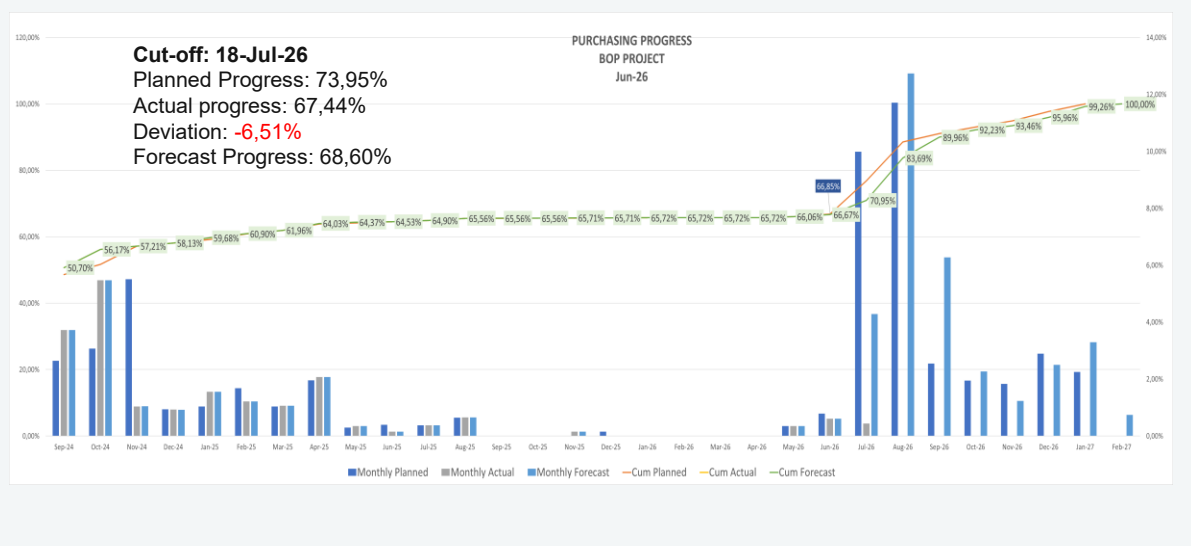

Plan deviations

RED Activity	Plan date	Fcst date	CP impact?	Mitigating action	Who	When
RW + FFPS steel struct. and cladding (ROS)	05/02/26	08/07/26	Y	LNTP: Confirmed by KSH Contract: Approved by both parties Approval of TG4 by PGB w19, contract to be signed w21.	Stegra	TBC
M&P Contractor (ROS)	19/12/25	13/09/26	Y	Awaiting NIWA's confirmation or comments on the proposed schedule. IDOM has also shared with NIWA the list of deliverables regarding pre-commissioning, cold and hot commissioning. TG4 PGB approval for w21.	Stegra IDOM	TBC
E&I Contractor (ROS)	19/12/25	28/08/26	Y	Initially, the plan was for the works to begin in June; however, since the approval process for TG4 may take approximately six weeks (GPB), it has been postponed to late June or early July. TG4 will be issued on W16. LOI approved(PGB) w19 and to be shared with STS w20.	Stegra	TBC

Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
Packages that will be proposed by Stegra-BOP as critical for ramp up (PGB):	- E&I - STS to submit the final version of A5 and A7, and IDOM final version of A1, all the contract documents to be shared in W26. - UG Piping Av. 9&6: Nordic to submit the last version of A7 and Nordic and Stegra to confirm all the contract documentation already shared by IDOM. - M&P Package – Contract signed. - RW&FF SS: Contract signed.				

BOP | Procurement (IDOM)

Main Packages Status

PACKAGE NUMBER	ITEMS	NEXT TG	TG FORECAST	Expected value MMEUR	TG4 forecast date	Contract signing forecast date	Forecast Arrival on Site
							(ROS forecast)
BOD-BOP-019EA	Underground Services & Roads Avenue 9.1, 2,3,4 Road 4	TG4	20/05/2026	35.9	20/05/2026	30/06/2026	01/07/2026
MISC	Remaining Civil Works	TG3	19/06/2026		10/07/2026	30/07/2026	30/08/2026
BOD-BOP-027C	HVAC engineering for BOP	TG5	22/05/2026	0.2	Approved 05/05/2026	15/05/2026	13/08/2026
	Engineering as priority						
BOD-BOP-020A	M&P Contractor	TG4	21/04/2026	4.3	21/04/2026	Signed 23/06/2026	30/08/2026 TBC
		(NIWA)					
BOD-BOP-020C	E&I Contractor	TG4	15/04/2026	32.7	15/04/2026	03/07/2026	06/07/2026
		(STS)					
BOD-BOP-051B	RW and FFPS Steel structure and Cladding	TG4	30/03/2026	0.9	Approved 11/05/2026	Signed 23/06/2026	15/08/2026
		(KSH)					
BOD-BOP-043	MHS for Slag and DRP by-products	TG3	29/05/2026	13.9	23/06/2026	14/07/2026 TBC	01/12/2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Pipe Bridge Manufacturing Progress - Ferrmix

Week 29 2026

PROJECT PHASE		Priority	P1		P2		P3		P4		P5	
			Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total
Steps												
Steel Structure	Assembled column		45	45	11	11	64	64	20	20	6	6
	Assembled modules		67	67	10	10	59	59	37	37	8	8
	Painted Columns		45	45	11	11	64	64	20	20	6	6
	Painted modules		67	67	10	10	59	59	37	37	8	8
Piping	Modules with pipe inside		45	45	10	10	59	59	18	20	8	8
Heat tracing	Modules with tracing		45	45	10	10	59	59	18	20	8	8


ERECTION STEEL STRUCTURE	TOTAL unit	ERECTED	REMAINING
Columns			
PB01	45	45	0
PB02	11	8	3
PB03	64	63	1
PB04	20	9	11
PB05	6	6	0
Modules			
PB01	67	67	0
PB02	10	9	1
PB03	59	57	2
PB04	37	16	21
PB05	8	8	0

BOP | Pipe Bridge General Comments - Ferrmix

Week 29 2026

Area	Description
General	FERRMIX manpower: number of critical resources remains unchanged (average of 19 welders) with a good performance.
General	FERRMIX is still underperforming in relation to Earthing. Only 97% progress have been achieved at P1. FERRMIX has announced mobilization of additional electricians for this Scope.


Weekly Welding by Welders

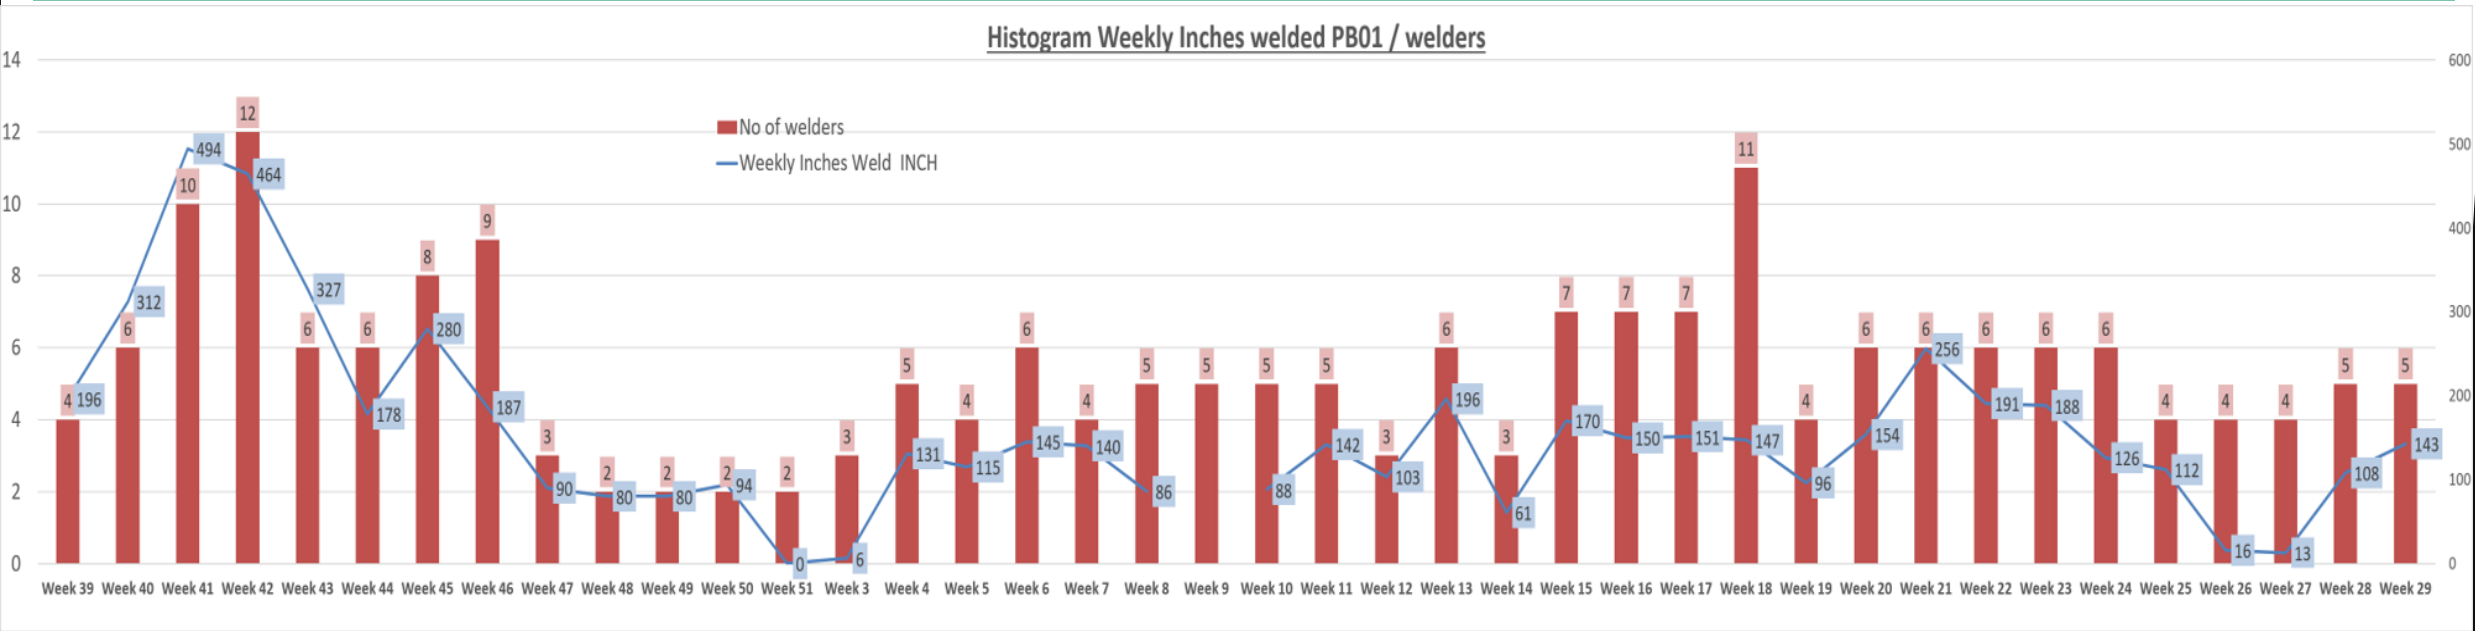

BOP | Pipe Bridge General Comments - Ferrmix

Weekly Welding by Welders

PB01 PRODUCTIVITY WELDING / WEEK

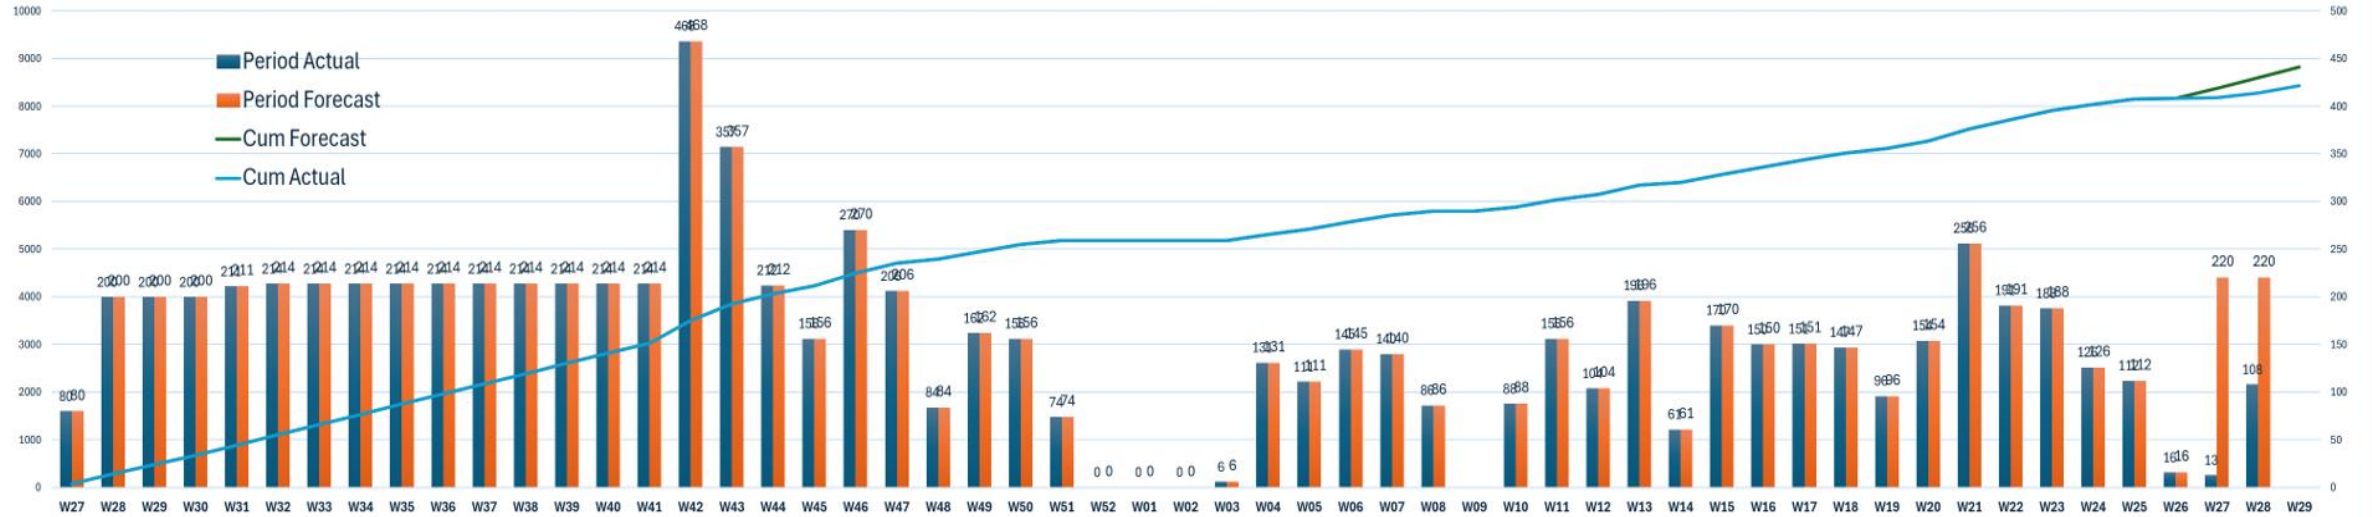


Status Piping Welding by Priorities

SUM % PROG.	Total Inch Field	Accum. Welded Field	% Prog. Welded Field	Total Inch Shop	Accum. Welded Shop	% Prog. Welded Shop	Total Inch F+S	Total Welded F+S	Total Weld %
P1	9.999	8.351	84%	12.696	12.696	100%	22.694	20.778	92%
P2	1.504	965	64%	3.851	3.783	98%	5.355	4.643	87%
P3	4.708	2.281	48%	13.198	13.158	100%	17.905	14.888	83%
P4	2.353	1.912	81%	3.528	3.528	100%	5.881	5.146	88%
P4.a	1.532	-	0%	4.021	3.991	99%	5.553	3.991	72%
P5	746	136	18%	1.596	1.473	92%	2.342	1.583	68%
	20.841	13.645	65%	38.888	38.627	99%	59.729	51.028	85%

BOP | Construction

Progress

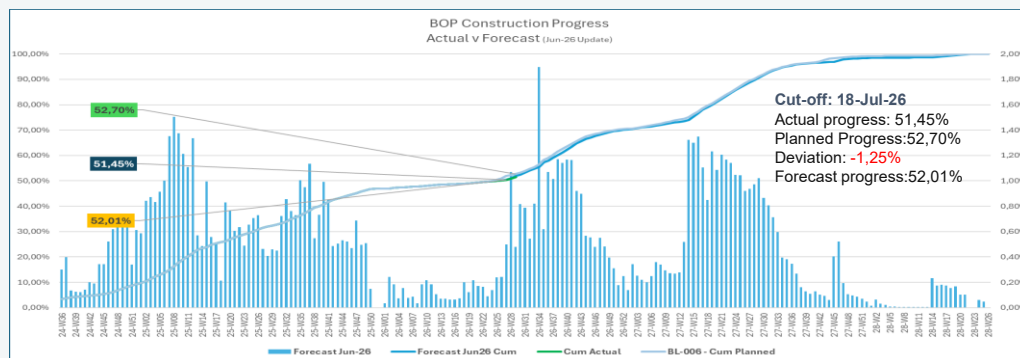

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Con	PB- Piping connections + pending fittings	- WK29 – Average 19 Welders, Ferrmix forecast 660 inches/week vs Actual 517 inches/week - PB01 Welding productivity: 220 inches /week - PB02 Welding productivity: 88 inches /week - PB03 Welding productivity: 264 inches /week - PB04 Welding productivity: 88 inches /week - PB05 Welding productivity: 0 inches /week
Con	PB05 foundation for support pipes	McDermott to execute the piping in that area asap/ Contract with the new civil contractor is to be signed.
Con	SIEMENS: Delay to finalising NPB511 punch items	Siemens mobilization to site (expect WK33). 1 week is needed to close punches
Con	PB02. Foundation not possible due to works by Mc Dermott	McDermott piping pending. Focus on other areas. / Contract with the new civil contractor is to be signed.
Con	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	Confirmation from Stegra to proceed with execution / Contract with the new civil contractor is to be signed.
Con	PB04. Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott.	Agreement reached to execute foundation. Steel structure installation pending for permission
Con	Actemium: Delay PB and NPB511 UG earthing completion.	Pending contractual agreement Stegra/Actemium

Plan

Activity	Plan date	Fcst date	CP impact?	Mitigating action	Who	When
LNG Civils works complete (remaining works)	W32 26	WK41 26	Y	Interface management	IDOM	WK32 26
Commence FF Pumping station civil works (after piping installation)	W38 26	WK38 26	Y	Interface management	IDOM	WK32 26
Commence RW Pumping station building erection	W37 26	WK37 26	Y	Interface management	IDOM	WK32 26
PB1 connections complete	W51	WK35 26	Y	Ferrmix confirms more welders: 20 welders	FER	WK35 26
UGP1 completion (incl. Ave. 9.5) (includ. Press test)	W31 26	WK28 26	Y	Piping works completed	GRK	WK32 26
Start Electrical Works (PDOP area)	WK 28 26	WK28 26	Y	Start electrical works PDOP	STS	WK 31 26

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Construction (IDOM)

Planned vs. Actual Week 29 2026


Weight	Activity	Cum Actual	Actual W29	Planned W29 (BL CCE06 TBA)	Forecast W29	Dev. Forecast Vs Actual	Dev. Planned Vs Actual	Forecast W30	Forecast W31	Forecast W32	Forecast W33	Forecast W34	Forecast W35	Deviation (Against Forecast)	Mitigation Actions
6,83%	Raw Water & FF Pumping Stations	74,65%	0,07%	0,07%	0,07%	0,00%	0,00%	0,00%	0,35%	0,00%	0,27%	0,27%	0,27%		
0,25%	Compressed Air Plant NPB-422	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
6,02%	LNG Terminal / Regasification Unit	87,02%	1,63%	1,86%	3,73%	-2,10%	-0,23%	1,00%	1,00%	1,00%	0,85%	2,62%	1,46%	1. Delay in electrical work for cable pulling 2. Delivery delay MV Transformer 3. Delivery delay Controll units 4. Completion of Civil works	1. Chart is recovering the delay 2. MV Transformer TBC (Pending Stegra Technical deviation approval) (+11 Week from response to delivery). 3. Controll units ETA W32/33 4. Completion of civil works
5,11%	PDOP Civil	92,82%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
1,76%	Power Distribution 51x	84,69%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	3,06%	3,06%	3,06%	3,06%	3,06%		
8,07%	NPB-200 Series	55,95%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,35%		
1,00%	NPB-102 Safety & Security Building	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
17,84%	Pipe & Cable Racks	84,34%	0,31%	0,31%	0,44%	-0,13%	0,00%	0,52%	0,50%	0,59%	0,81%	1,70%	2,07%		
21,06%	Underground Networks	17,55%	0,60%	0,61%	0,74%	-0,14%	-0,01%	1,26%	1,21%	1,05%	1,06%	1,04%	1,09%	1. RW/FF area: UG piping installation activities are underperforming 2. Prio 0 RW chamber not finish 3. Prio 1 Pressure test not yet performed 4. Electrical ducts PDOP	1. GRK will send a recovery schedule 2. GRK will finalize in the coming weeks 3. Test pack rejected to be re-submitted 4. Release area by Hitachi in Week 29
9,61%	RailWay Package	33,70%	0,00%	0,26%	0,02%	-0,02%	-0,26%	0,11%	2,84%	2,97%	0,27%	0,42%	0,26%	Pending approval of CO to proceed with the works	Expedite the approval of CO
22,45%	Overall Construction Sweco Scope: Ponds, Roads & Temporary Power - Water	34,18%	1,88%	0,23%	2,69%	-0,81%	1,65%	0,23%	0,27%	0,27%	0,12%	0,12%	4,82%	1. Completion of Mechanical completion of Temporary Power and TWTP 2. Completion of Mechanical completion of Temporary TWTP 3 UG network RWFF piping testing	1. Completion of Testing Cables, testing earthing works by Fermix and Actemium, Siemens needs to close the Punches opens B. 2. Close commercial/ contracting CR. 3 Expedite perform the RWFF piping testing.
100,00%	Total	50,74%	0,71%	0,38%	1,07%	-0,36%	0,33%	0,48%	0,82%	0,79%	0,54%	0,82%	1,90%		

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Railways Management (IDOM PCM – SWECO - GRK)

Progress Status

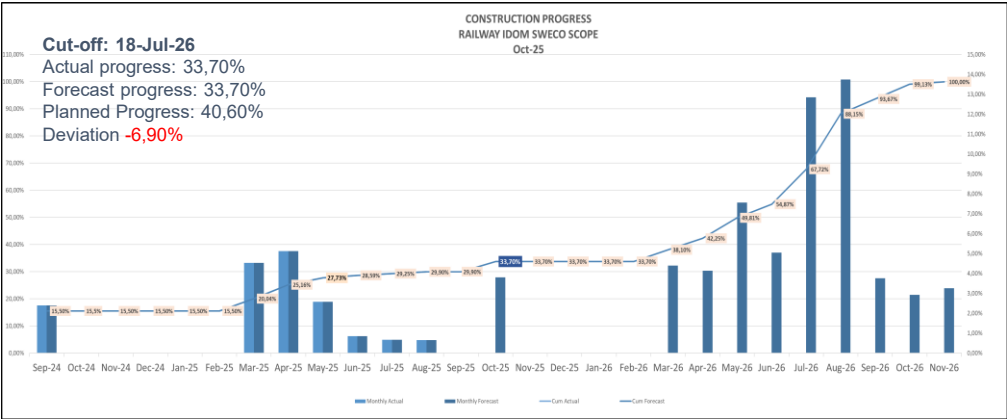

1+6 activities

- Week 31 – Mobilisation to site. Start drainage piping installation under the rail and UG piping crossing. DRP need to start removing pipe material of section 3
- Week 32 - Continue drainage piping installation under the rail and UG piping crossing
- Week 33 - Continue drainage piping installation under the rail and UG piping crossing
- Week 34 - Continue drainage piping installation under the rail and UG piping crossing
- Week 35 - Continue drainage piping installation under the rail and UG piping crossing
- Week 36 - Continue drainage piping installation under the rail and UG piping crossing

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
CON	Section 3 Interference with Hydrogen pipe	Expected IFC drawing for culvert end of September 26 (SWECO)
CON	New pile deck in Scope of McDermott not interfere with railway truck, but interfere with the pressure bern, east ditch and service road	Alternative 3 Hydrogen pipeline
CON	Scrap Yard micropilling Desing End of May (Done). Micropilling to be done by McDermott	Only for railway truck. East ditch and service road on the limit boundary can start
CON	Activities planned to restart in Week 30 (Drainage piping)	Pending CO for East ditch

TOTAL RAILWAY	Unit	Total	Weight %	Contractor	Actual Progress	Category	WK29	WK30	WK31	WK32	WK33	WK34	WK35
Underbelt Layer (Rein.) DCH. 15	m3	72973	20%	GRK	31%	Period Forecast	0	9177	2955	10542	10542	8669	0
						Period Actual	0	0	0	0	0	0	0
Underballest Layer (Frost) DCH. 16	m3	118902	20%	GRK	30%	Period Forecast	0	3609	5390	14408	5605	0	13428
						Period Actual	0	0	0	0	0	0	0
Catenary Poles/ Struts	ea	199	5%	GRK	33%	Period Forecast	0	12	0	20	12	16	0
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballast track	m	9602	15%	GRK	40%	Period Forecast	0	0	384	383	184	184	184
						Period Actual	0	0	0	0	0	0	0
Supplementation of ballast layer	m3	30296	15%	GRK	40%	Period Forecast	0	559	0	700	900	869	2250
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballasttles track	m	4403	5%	GRK	3%	Period Forecast	0	0	184	184	184	184	184
						Period Actual	0	0	0	0	0	0	0
Switches	ea	18	5%	GRK	39%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0
Hanging Works	ea	22	15%	GRK	27%	Period Forecast	0	0	0	3	0	0	1
						Period Actual	0	0	0	0	0	0	0
Concrete Channel Section 7 - Track 1	m	1000	1%	GRK	100%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Longitudinal drainage SSY (start)	10 Nov 2025	30 Aug 2026
Ballast & sub-ballast SSY (Start)	17 Nov 2025	17 Aug 2026
Trench excavation Track 1 – Section 6	28 Nov 2025	17 Aug 2026
North Railway - Section 7 – Ready for commissioning	29 May 2026	30 Sep 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Roads & Ditches Management (IDOM EPCM – SWECO – GRK)

Progress Status

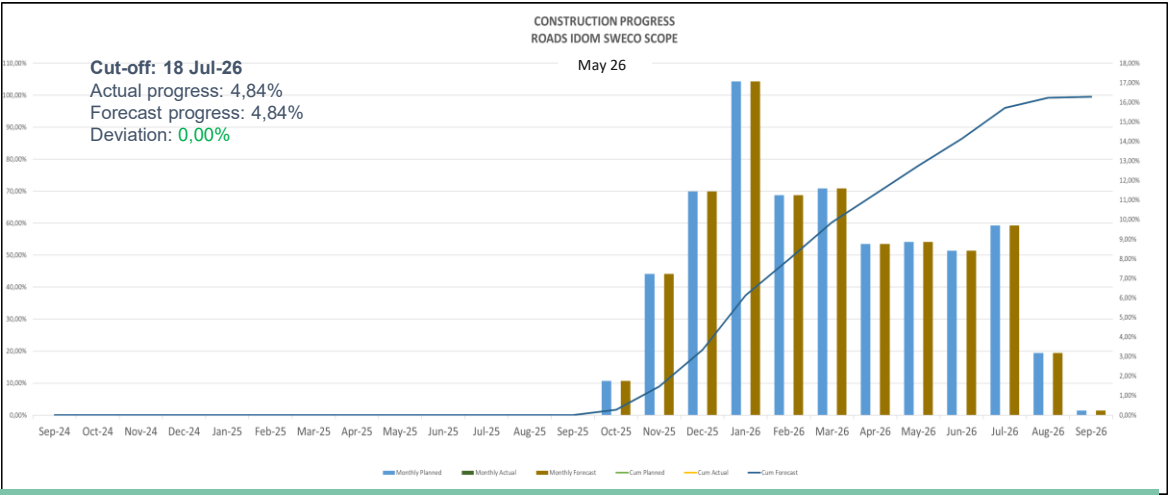

1+6 activities

- Week 30 - Expect to started permanents backfilling. CR for backfilling for road 6.1 and 6.2 to be issued
- Week 31 - Activities on hold.
- Week 32 - Activities on hold.
- Week 33 – Activities on hold.
- Week 34 – Start backfilling road 6 and ave. 9.5.
- Week 35 – Continued backfilling road 6 and ave. 9.5.

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action

Avenue/Roads	Activity name	Weight %	Weight % on Tot	Progress	Category	WK28	WK29	WK30	WK31	WK32	WK33	WK34
						11/07/26	18/07/26	25/07/26	01/08/26	08/08/26	15/08/26	22/08/26
Av 1	Avenue 1	100%	5%	34%	% Cum Planned	34%	34%	34%	34%	34%	34%	34%
					% Cum Forecast	34%	34%	34%	34%	34%	34%	34%
					% Cum Actual	34%	34%	34%	34%	34%	34%	34%
Av 1	Roads - Avenue 1 - Clearing and levelling ground	23%		100%	Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	1	1	1	1	1	1	1
					% Cum Forecast	100%	100%	100%	100%	100%	100%	100%
					Period Actual							
					Cum Actual	1	1	1	1	1	1	1
					% Cum Actual	100%	100%	100%	100%	100%	100%	100%

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Start sub-base laying Avenue 9.5	28 Sep 2026	19 Mar 2027
Start Road Ave 1 Laying subbase	20 Jul 2026	07 Aug 2026
Start sub-base laying Road 6	13 Jul 2026	14 Aug 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Ponds Management (IDOM EPCM – SWECO – GRK)

Progress Status

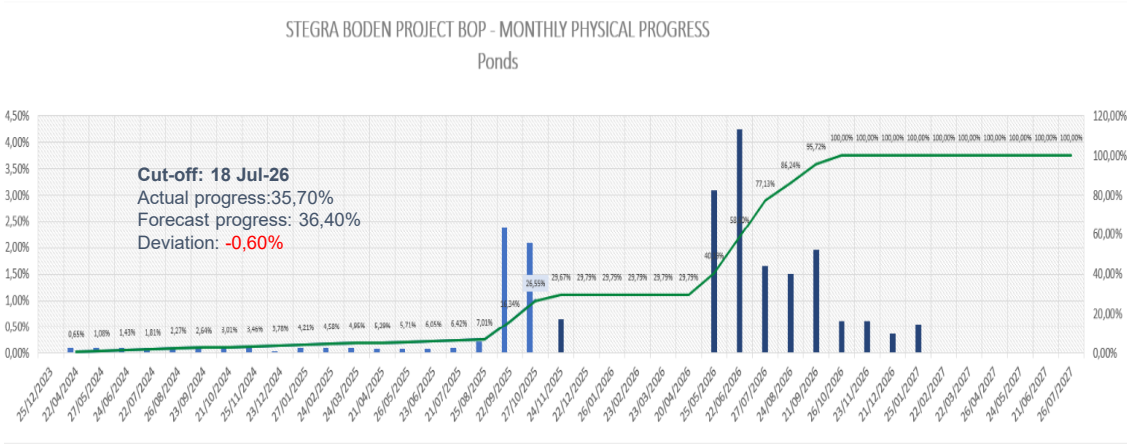

PONDS TOTAL	Unit	Total	Weight %	Contractor	Actual Progress	Category	WK29	WK30	WK31	WK32	WK33	WK34	WK35
Surcharge placement and removal	m3	74900	15%	GRK	98%	Period Forecast	9923	4500	3500	1000	0	0	0
						Period Actual	0	0	0	0	0	0	0
Groundworks	m3	436954	30%	GRK	89%	Period Forecast	5982	7606	5982	5982	5982	3508	3508
						Period Actual	4500	0	0	0	0	0	0
Pipes installation	m	1199	20%	GRK	50%	Period Forecast	0	10	47	382	0	0	0
						Period Actual	0	0	0	0	0	0	0
Geomembrane installation	m2	34280	15%	GRK	21%	Period Forecast	0	5000	5000	5511	7336	2336	0
						Period Actual	0	0	0	0	0	0	0
Erosion Protection (Riprap)	m3	94071	20%	GRK	36%	Period Forecast	3668	0	0	0	4115	13657	13854
						Period Actual	0	0	0	0	0	0	0

1+6 activities

Week 30 - East ponds excavated 4500 m3 out of 71000m3 – **6,3% progress achieved**. West pond 1 erosion protection cover installation.

Week 31 - Continue excavation East ponds. West pond 1 erosion protection cover installation

Week 32 - Continue excavation East ponds and Start excavation Contact water pond. West pond 1 erosion protection cover installation

Week 33 - Continue excavation East ponds and Contact water pond

Week 34- Continue excavation East ponds and Contact water pond

Week 35- Continue excavation East ponds and Contact water pond

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
PRC	Remaining works for West pond 3 completion (CR pending)	IDOM, GRK and Stegra to expedite process
QAQC	ITP for West ponds pending revision by IDOM/Stegra. Works on hold.	GRK to award sub-contractor for test
	Pending geomembrane testing sub-contractor award	

6-month key Waypoints



Key Waypoints	Planned date	Forecast date
Completion West Pond 1	30 Jun 2026	30 Jul 2026
Completion West Pond 3	30 Jun 2026	30 Jul 2026

Achievement — Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

Construction Manpower & Histogram for ongoing activities

Week 29 2026	GRK	ANFRA	ACTEMIUM	FERRMIX	CHART	SIEMENS	FORSSA	LBS	PROXA	KSH	STS	NORDIC
	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual
LNG	0				11					0		
RAIL												
PONDS	10											
RW AREA	0						0					9
UGP RW AREA	6											
UGP0 (Ave 1 & Ave 2)	0											
UGP1 (Road 7 Ave 9.5)	5											
UGP3 (Road 6)	8											
UGP4 (Ave 9)	0											
PDOP		6										
100 MW CABLE PULL (OFFSITE)			0									
100 MW CIVILS	0											
PB FOUNDATIONS	0											
PB ERECTION & FITUP				64								
TEMPORARY POWER ONSITE			0					0				
515	0					0						
511						0						
TEMPORARY PIPE BYPASS	0											
EARTHING WORKS	0											
Roads	0											
TWTP - Mechanical	0								1			
TWTP - Electrical											0	
TOTALS	29	6	0	64	11	0	0	0	1	0	0	9
BLTotal	60	0	0	65	30	0	0	0	0	0	29	100
Actual Week Average	120											
BL Week Average	285											
Forecast Average	285											

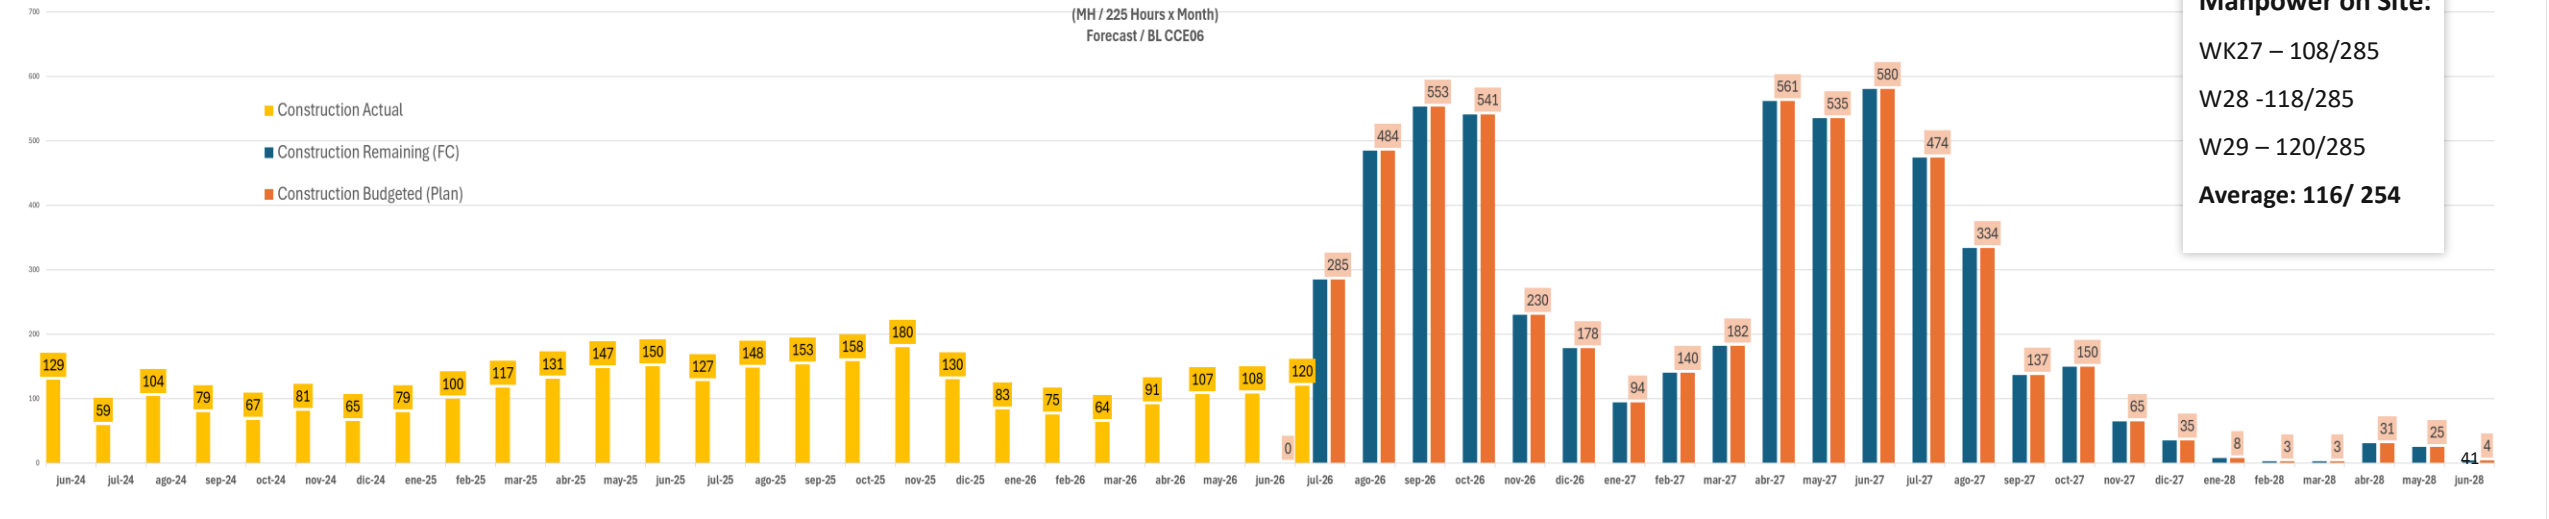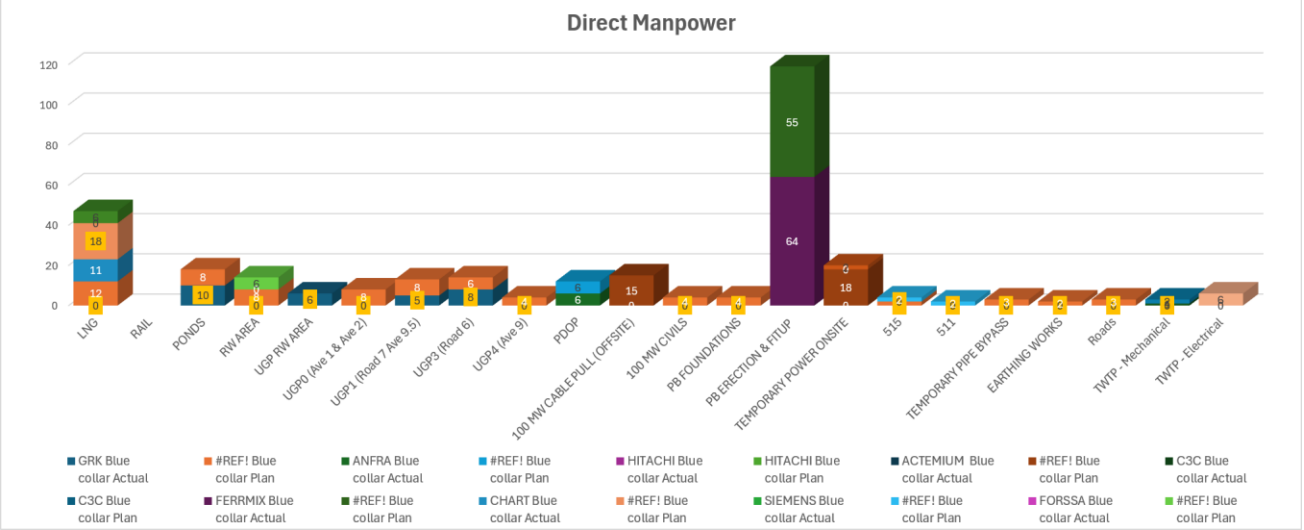

Actions

Sub-Area	Key issue / potential risk	Due Date	Owner	Description	Potential Impact	Mitigation
PB02	Erection of bridge & reinstall foundation PB02 to WTP1 blocked by Mc Dermott and Stegra	w42_25	STEGRA/ Mc Dermott	No access permission.	Delay to construction (pipes test)	Confirmation from stegra to proceed with erection
PB03	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	w45_25	STEGRA/ Mc Dermott	No access permission.	Delay to construction	Mc Dermott to be confirmed date to release the area
PB04	PB04: Foundation & Erection SS (columns and modules), due to constructability priorities of CAS/SMPT by Mc Dermott.	w36_25	STEGRA/ Mc Dermott	No access permission.	PB04 not ready as scheduled.	Agreement reached to execute foundation. Steel structure installation pending for permission.
Pipe Bridges	Pipebridge Piping Connections + Pending Fittings	w25_25	IDOM/STEGRA/FE RRMIX	Lack of welding Resources and low productivity	Delay in connections and pending fittings	WK27 – Average 19 Welders, Ferrmix actual 793 inches/week
Rail	Unloading Station Tunnel (Section 2)	w35_26	IDOM DRP	Track 1 execution restricted for Tunnel	Construction delay	Review status weekly to make sure Tunnel is delivered on schedule. DRP confirmed August 24, 2026 as the completion date.
Rail	Road 2 retaining wall (Section 2)	w30_26	IDOM BOP / GRK	Track 1 execution restricted for retaining wall	Construction delay	Review weekly status to ensure the retaining wall is delivered on time w29 - IDOM provided GRK preliminary documentation via email. The documentation will be provided officially once the BoQ for the Rail memo 19 has been priced and comments from IDOM will be included..
Roads/UGP	Road 6.0 as laydown area for UGP	w34_26	IDOM BOP	Road 6.0 to be used as laydown area for execution of Road 6.1 and Road 6.2 UGP	Construction delay	w22 - CR for filling of Road 6.0 to be issued this week for pricing. w23/w24/w25/w26/w28 - Stegra to review and approve the Road 6.0 CR. w29 - CR has been executed by Stegra but works will start in approx w33-w35
Rail	Transversal and longitudinal drainage interface with loading station	w30_26	IDOM BOP/DRP	Interface between the loading station and the transversal and longitudinal drainage.	Construction delay	w28 - Stegra identified potential issues with IDOM's proposed solution and will coordinate with IDOM site team to optimize the solution. w29 - Stegra requested elevations for the modifications implemented to the transversal and longitudinal drainge. IDOM is checking internally and will revert.
Rail/Roads	Clash with existing power supply at Section 5 Rail	w30_26	IDOM BOP / Stegra SS	Existing power supply to plant crosses eastern ditch and rail at Section 5. Until a solution if proposed, rail groundworks cannot start.	Construction delay , redesign may be required.	w28 - Stegra provided the theoretical levels and IDOM has reviewed them. IDOM construction team to establish a protocol to confirm they can proceed with the excavations. w29 - IDOM safety to coordinate with GRK such that a protocol is established to confirm they can proceed with the excavations in the RAMS. WK29 - Expedite agreement between STEGRA/GRK/IDOM
UGPiping	Work suspended - Preparation for Priority 1 piping tests Blocked	w30_26	IDOM BOP / Stegra	Work suspended - Preparation for Priority 1 piping tests	Construction delay	
Pipe Bridges	Piping test are blocked for commercial issues	w30_26	IDOM BOP / Stegra	Work suspended - PB01 piping tests	Construction delay	WK29 - Expedite agreement between STEGRA/Ferrmix/IDOM
Ponds	East pond groundworks execution is blocked.	w30_26	IDOM BOP	East pond groundworks execution is blocked. IDOM to provide GRK a plan drawing indicating the areas where sulphides are present as well as approximate depth.	Consutrction delay	w29 - IDOM to provide GRK with a plan drawing indicating the locations where sulphites are present, also indicating the depth. IDOM to collaborate with GRK to perform tests on-site to identify the information required to prepare the plan drawing.
Ponds	West Pond 2 cannot be finished until the northern area is handed back by DRP.	w33_26	IDOM BOP/DRP	In 2025, DRP took over the northern wall area to use it as a laydown area. This area must be handed back to BOP in order to allow the raising of the northern wall and the completion of West Pond 2.	Construction delay	w28 - IDOM BOP meeting with IDOM DRP has been postponed to w29 w29 - IDOM BOP and IDOM DRP are still coordinating on when the handover will take place.
Temp Power	Actemium: Delay PB and NPB511 UG earthing completion	WK25_26	IDOM/STEGRA	Actemium: Delay PB and NPB511 UG earthing completion	Delay to energization	Pending contractual aggrement STEGRA/ACTEMIUM
Roads	Boden Energy switch houses	w38_26	Stegra SS	Switch houses are located at the same location than the service road over the East ditch. It is necessary either to remove the houses or to divert the road	Construction delay , redesign may be required.	w28 - Current plan is to execute the service road until the switch houses. w29 - IDOM to review the constructability for the ditch in this area and revert with feedback.

BOP | Construction Pictures - Pipe Bridge

- Piping welding works (all priorities) 517 Inches welded



PB01 & PB05

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - UG piping

- Avenue 9.5 piping installation and backfilling completed
- Road 6 Piping installation and backfilling ongoing



Avenue 9.5 and ELA01 to Transformers T1 to T7



Scrap road 1



Road 6

BOP | Construction Pictures - LNG Terminal

- Pipe welding ongoing
- Cable pulling and connection ongoing



Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - RW+FF Area

✓ UG piping installation ongoing




Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - PDOP

- Area between ELA01 and Transformers backfilling completed WK29

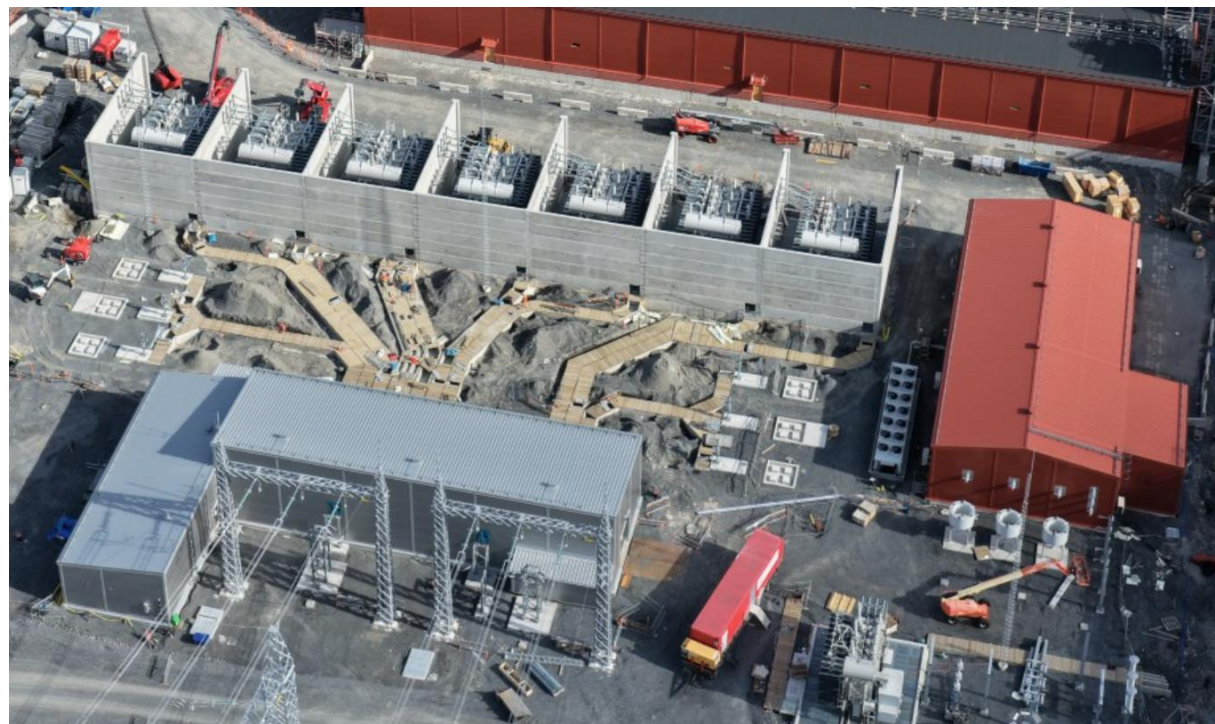

PDOP

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue
 Risk / Concern
 Behind

BOP | Construction Pictures – Railways



Section 2 Unloading station



Section 3 Wet land view and
Terrace of Tracks 10, 11 and
12



Section 4A Scrap Yard Area for Track 1 (exterior) and Tracks
101 and 102 (internal)

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures – Ponds

East ponds excavation



East ponds

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish	2026										
					W25	W26	W27	W28	W29	W30	W31	W32	W33	W34	W35
Pipe & Cable Racks	11-Dec-24 A	13-Nov-26	11-Dec-24	11-Dec-26											
PR Civil, Structural and Architectural (CSA)	11-Dec-24 A	13-Nov-26	11-Dec-24	11-Dec-26											
Construction - Pipe Rack Modules Priority 1	09-Sep-25 A	28-Aug-26	09-Sep-25	28-Aug-26											
Construction - PCR - Piping Connections - Priority 1	09-Sep-25 A	28-Aug-26	09-Sep-25	28-Aug-26											
Construction - Pipe Rack Modules Priority 2	11-Dec-24 A	23-Oct-26	11-Dec-24	23-Oct-26											
Construction - PCR - Pipe rack Foundation - Priority 2 - backfilling	11-Dec-24 A	31-Jul-26	11-Dec-24	31-Jul-26											
Construction - PCR - Modules Erection - Priority 2	03-Nov-25 A	20-Jul-26	03-Nov-25	22-Jun-26											
Construction - PCR - Loose Items Installation (Cable Trays) - Priority 2	01-Dec-25 A	23-Jul-26	01-Dec-25	25-Jun-26											
Construction - PCR - Piping Connections - Priority 2	02-Mar-26 A	23-Oct-26	02-Mar-26	23-Oct-26											
Construction - Pipe Rack Modules Priority 3	04-Feb-25 A	13-Nov-26	04-Feb-25	11-Dec-26											
Construction - PCR - Pipe rack Foundation - Priority 3 - excavation	04-Feb-25 A	10-Jul-26	04-Feb-25	17-Jul-26											
Construction - PCR - Pipe rack Foundation - Priority 3 - concrete	04-Feb-25 A	24-Jul-26	04-Feb-25	07-Aug-26											
Construction - PCR - Pipe rack Foundation - Priority 3 - backfilling	04-Feb-25 A	31-Jul-26	04-Feb-25	14-Aug-26											
Construction - PCR - Columns Erection - Priority 3	15-Oct-25 A	14-Aug-26	15-Oct-25	28-Aug-26											
Construction - PCR - Modules Erection - Priority 3	24-Nov-25 A	11-Sep-26	24-Nov-25	25-Sep-26											
Construction - PCR - Loose Items Installation (Cable Trays) - Priority 3	02-Mar-26 A	25-Sep-26	02-Mar-26	09-Oct-26											
Construction - PCR - Secondary Steel - Priority 3	02-Mar-26 A	02-Oct-26	02-Mar-26	16-Oct-26											
Construction - PCR - Piping Connections - Priority 3	12-May-26 A	13-Nov-26	12-May-26	11-Dec-26											
Construction - Pipe Rack Modules Priority 4	12-Nov-25 A	01-Sep-26	12-Nov-25	24-Aug-26											
Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - excavation	12-Nov-25 A	10-Jul-26	12-Nov-25	31-Jul-26											
Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - concrete	13-Nov-25 A	04-Aug-26	13-Nov-25	04-Aug-26											
Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - backfilling	17-Nov-25 A	05-Aug-26	17-Nov-25	05-Aug-26											
Construction - PCR - Remaining Columns Erection - Priority 4	06-Aug-26	20-Aug-26	06-Aug-26	20-Aug-26											
Construction - PCR - Remaining Modules Erection - Priority 4	19-Aug-26	01-Sep-26	11-Aug-26	24-Aug-26											
Construction - Pipe Rack Modules Priority 5	02-Mar-26 A	06-Oct-26	02-Mar-26	08-Sep-26											
Construction - PCR - Pipe drops and Loose Items - Priority 5	02-Mar-26 A	06-Oct-26	02-Mar-26	08-Sep-26											
Construction - PCR - Piping Connections - Priority 5	02-Mar-26 A	28-Aug-26	02-Mar-26	28-Aug-26											

Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish		2026	July 2026					August		
						W25	W26	W27	W28	W29	W30	W31	W32	W33
Temporary Water Supply	29-Jun-26	11-Jan-27	29-Jun-26	11-Jan-27										
Construction - Underground Networks - Route 0 - RW Chamber - Piping Arrang	29-Jun-26	17-Jul-26	29-Jun-26	17-Jul-26										
Construction - Excavation - Inst Contact Water pipe CW - Test backfilling (RW	29-Jun-26	17-Jul-26	29-Jun-26	17-Jul-26										
Construction - Temporary Water Supply - TWTP Plant Operative	03-Aug-26	11-Jan-27	03-Aug-26	11-Jan-27										


Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish		2026	July 2026					August		
						W25	W26	W27	W28	W29	W30	W31	W32	W33
Temporary Power Transformers 2x63 MVA / 100 MW	01-Oct-25 A	09-Jul-26	01-Oct-25	09-Jul-26										
33 kV distribution from ELA to NPB511 and ASP - ON SITE	01-Oct-25 A	03-Jul-26	01-Oct-25	26-Jun-26										
ELA to NPB511 and ASP - Earthing Works - Installation & Connection by Ferrn	01-Oct-25 A	03-Jul-26	01-Oct-25	26-Jun-26										
Mechanical Completion & PreCom	06-Jul-26	09-Jul-26	29-Jun-26	09-Jul-26										
Pre Commissioning - E-House NPB511 (Temporary Set) for WTP1, ASP, WPS, M	06-Jul-26	09-Jul-26	29-Jun-26	09-Jul-26										

Actions

BOP – 6 Week Look Ahead

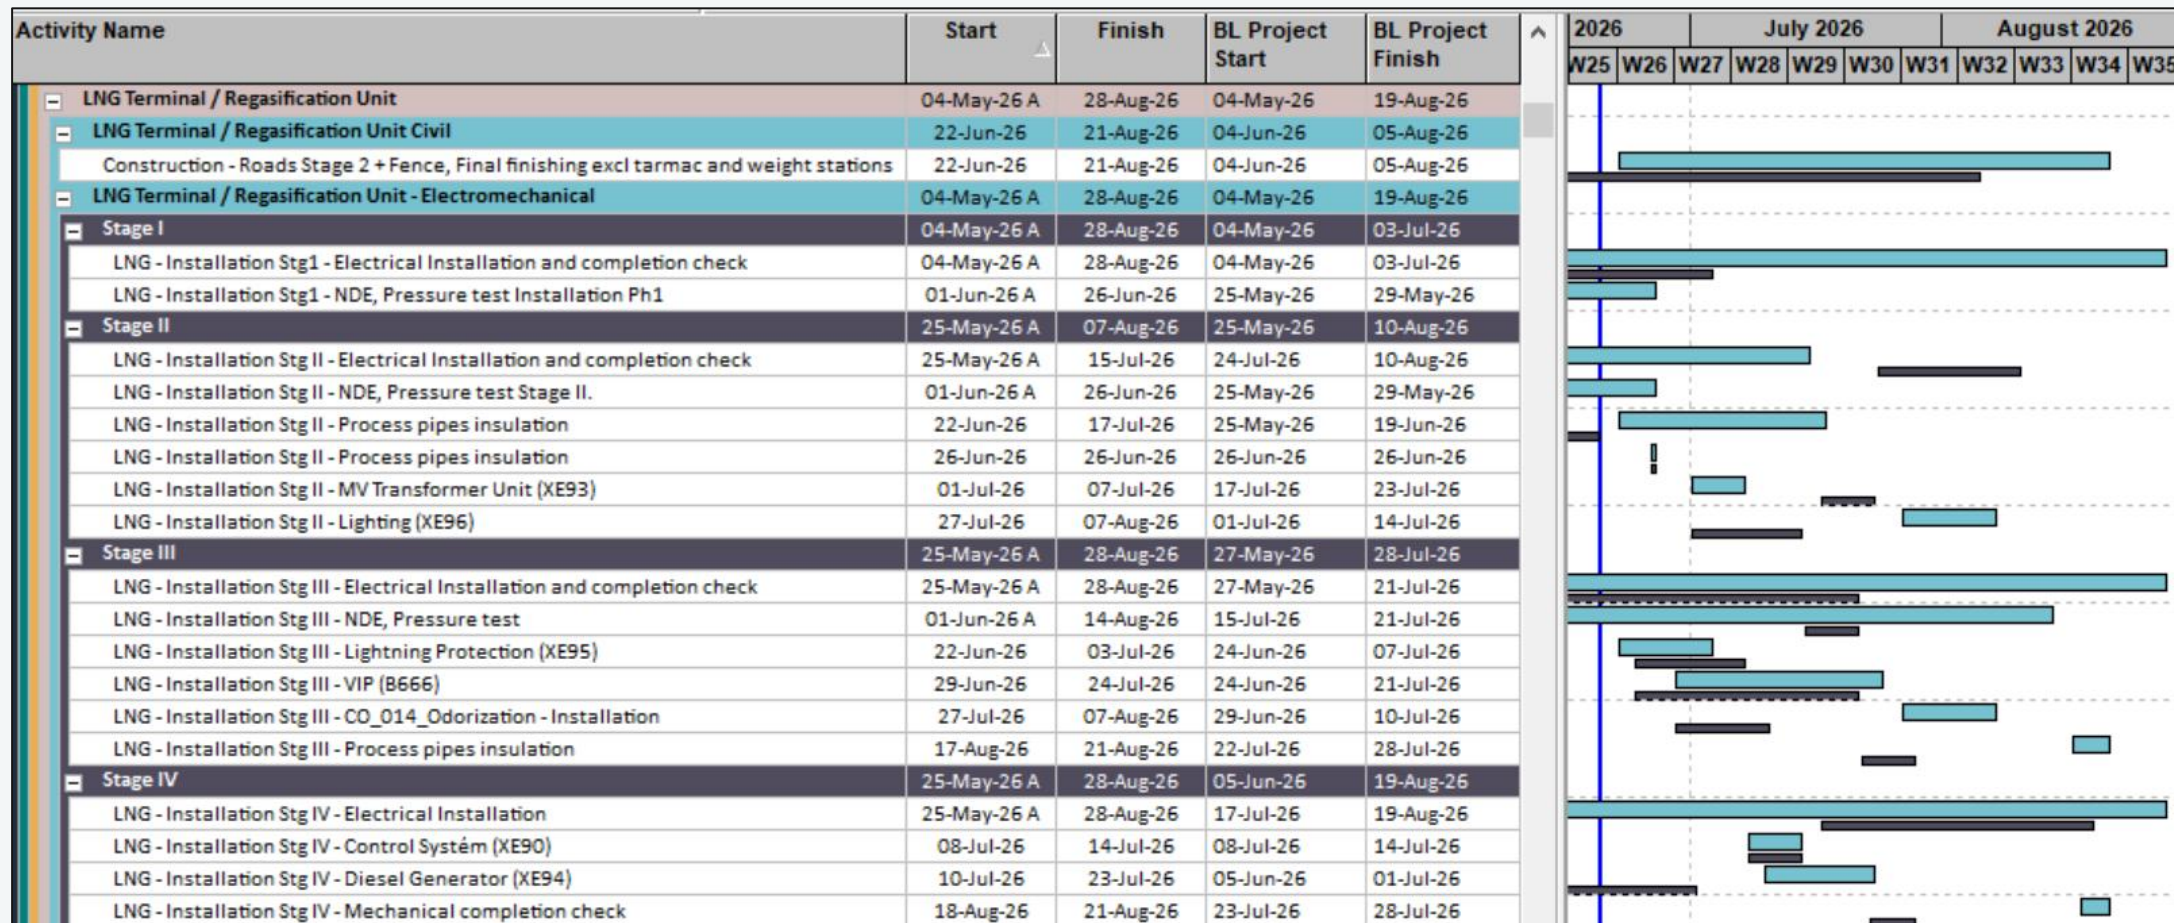

Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish											
					2026		July 2026					August 2026			
					W25	W26	W27	W28	W29	W30	W31	W32	W33	W34	W35
Underground Networks	07-Aug-25 A	23-Oct-26	07-Aug-25	30-Aug-27											
Piping Route 0 to Route 5 & Others Areas UG Networks	07-Aug-25 A	23-Oct-26	07-Aug-25	23-Oct-26											
Underground Piping Route 0 (Av 1.1 - 2.1 to 2.5)	03-Oct-25 A	24-Jul-26	03-Oct-25	26-Jun-26											
Underground Piping Route 0 - Process & SW & CW	03-Oct-25 A	24-Jul-26	03-Oct-25	26-Jun-26											
Underground Networks - Route 0 - Testing (PT,HT,LT etc.)	03-Oct-25 A	24-Jul-26	03-Oct-25	26-Jun-26											
Underground Piping Route 1 (Road 7 + Av 9.5)	07-Aug-25 A	07-Aug-26	07-Aug-25	31-Jul-26											
Underground Piping Route 1 - Process & SW & CW	07-Aug-25 A	07-Aug-26	07-Aug-25	31-Jul-26											
Underground Networks - Route 1 - trench excavation (BoP and SIN) E, F, G (Av. 9.5)	07-Aug-25 A	22-Jun-26	07-Aug-25	19-Jun-26											
Underground Networks - Route 1 - Piping Install & Welding and Weld Test E, F, G (Av. 9.5)	20-Aug-25 A	06-Jul-26	20-Aug-25	10-Jul-26											
Underground Networks - Route 1 - Backfilling in trenches for underground piping E, F, G (Av. 9.5)	26-Aug-25 A	09-Jul-26	26-Aug-25	17-Jul-26											
Underground Networks - Route 1 - Backfilling in trenches for underground piping A (Road 7)	25-Sep-25 A	03-Jul-26	25-Sep-25	19-Jun-26											
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) A (Road 7)	06-Jul-26	17-Jul-26	22-Jun-26	03-Jul-26											
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) E, F, G (Av. 9.5)	10-Jul-26	23-Jul-26	20-Jul-26	31-Jul-26											
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) B, C, D (Road 7)	27-Jul-26	07-Aug-26	29-Jun-26	10-Jul-26											
Underground Piping Route 5 (Road 7.5)	17-Nov-25 A	23-Oct-26	17-Nov-25	23-Oct-26											
Underground Piping Route 5 - Process & SW & CW	17-Nov-25 A	23-Oct-26	17-Nov-25	23-Oct-26											
Underground Networks - Route 5 - trench excavation (BoP and SIN)	17-Nov-25 A	25-Sep-26	17-Nov-25	25-Sep-26											
Underground Networks - Route 5 - Backfilling in trenches for underground piping	24-Nov-25 A	23-Oct-26	24-Nov-25	23-Oct-26											
Underground Networks - Route 5 - Piping Installation & Welding (WFI from P1 to Others Areas - 90 ml)	24-Nov-25 A	09-Oct-26	24-Nov-25	09-Oct-26											
Underground Piping Route 4 (Av 9.4 -9.3 -9.2)	20-Jul-26	02-Oct-26	20-Jul-26	02-Oct-26											
Underground Piping Route 4 - Process & SW & CW	20-Jul-26	02-Oct-26	20-Jul-26	02-Oct-26											
Underground Networks - Route 4 (A-B) (Av. 9.4 -9.3 - Av 6) - trench excavation	20-Jul-26	11-Sep-26	20-Jul-26	11-Sep-26											
Underground Networks - Route 4 (A-B) (Av.9.4 -9.3 - Av 6) - Piping Install & Weld (WFI P1 / around 15 lines)	24-Aug-26	02-Oct-26	24-Aug-26	02-Oct-26											
Underground Piping Route 3	25-May-26 A	04-Sep-26	13-Jul-26	04-Sep-26											
Underground Piping Route 3 - Process & SW & CW	25-May-26 A	04-Sep-26	13-Jul-26	04-Sep-26											
Underground Networks - Route 3 (A Road 6.1/6.2) - excavation & trench	25-May-26 A	31-Jul-26	13-Jul-26	31-Jul-26											
Underground Networks - Route 3 (A Road 6.1/6.2) Piping Installation & Welding (WFI / WBD / WSI)	08-Jun-26 A	21-Aug-26	03-Aug-26	21-Aug-26											
Underground Networks - Route 3 (A Road 6.1/6.2) - Backfilling in trenches for underground piping	15-Jun-26 A	04-Sep-26	24-Aug-26	04-Sep-26											
Underground Piping Other Areas	22-Jun-26	04-Sep-26	08-Jun-26	06-Oct-26											
Other Areas - RW + FFW UGP area	22-Jun-26	04-Sep-26	08-Jun-26	06-Oct-26											
Other Areas - RW + FFW UGP area - Process (IDOM)	22-Jun-26	04-Sep-26	08-Jun-26	06-Oct-26											
UG Networks - Others Areas - RW + FF (A) - Testing (PT,HT,LT etc.)	22-Jun-26	03-Jul-26	08-Jun-26	19-Jun-26											
UG Networks - Others Areas - RW + FF (E) - trench excavation (BoP and SIN)	06-Jul-26	17-Jul-26	13-Jul-26	24-Jul-26											
UG Networks - Others Areas - RW + FF (D) - Piping Installation & Welding (WFI / WRA)	06-Jul-26	24-Jul-26	10-Aug-26	28-Aug-26											
UG Networks - Others Areas - RW + FF (C) - Testing (PT,HT,LT etc.)	06-Jul-26	17-Jul-26	17-Aug-26	28-Aug-26											
UG Networks - Others Areas - RW + FF (B) - Testing (PT,HT,LT etc.)	06-Jul-26	17-Jul-26	27-Jul-26	07-Aug-26											
UG Networks - Others Areas - RW + FF (E) - Piping Installation & Welding (WFI / WRA)	20-Jul-26	07-Aug-26	19-Aug-26	08-Sep-26											
UG Networks - Others Areas - RW + FF (D) - Testing (PT,HT,LT etc.)	27-Jul-26	07-Aug-26	31-Aug-26	11-Sep-26											
UG Networks - Others Areas - RW + FF (E) - Backfilling in trenches for underground piping	10-Aug-26	21-Aug-26	09-Sep-26	22-Sep-26											
UG Networks - Others Areas - RW + FF (E) - Testing (PT,HT,LT etc.)	24-Aug-26	04-Sep-26	23-Sep-26	06-Oct-26											
