

Weekly Report W30



BOP-IDOM-EHSS – SAFETY MOMENT-Lifting operations W30

SAFETY MOMENT

LIFTING OPERATIONS

CONTROL THE LOAD • CONTROL THE RISK



01 PLAN
Approved lift plan, verified weight and safe crane setup

02 CHECK
Inspect crane, rigging, hook, ground and weather conditions

03 CONTROL
Barricade the zone; one banksman; use tag lines safely

04 PROTECT
Never stand beneath or enter the path of a suspended load

STOP THE LIFT
if communication is lost or conditions change

1


BOP-IDOM-EHSS – DASHBOARD Summary (Week 30)

For information


Lagging Performance Indicators

408 Days LTI Free!!!!

All Incidents & Risks

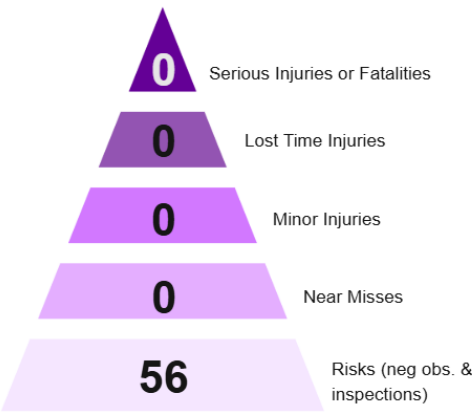

SIF Potential Classification

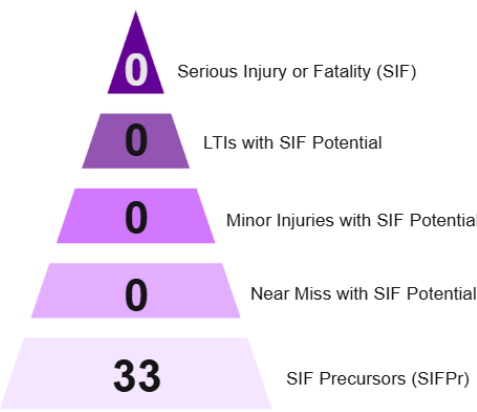

	Project to date	UE Construction	Benchmarking sector
LTIFR	1,55	5	2
TRIFR	5,15	N/A	N/A

Highlights/Downlights of the week:


- 22.07.2026 LNG 3RD Test pack-Pneumatic pressure test completed safe.
- IDOM Construction management stand up 23.07.2026.
- Schedule Emergency Drills of contractors.




Leading Performance Indicators

	Week	Last week	Project to date
SITE WALKS	11	14	991
OBSERVATIONS	66	77	9694
BBS INSPECTIONS	8	16	649
TARGET INSPECTIONS	18	18	346
NEAR-MISS	0	0	48
ENVIRONMENTAL IN	0	0	18
Environmental Corrective Actions Closed on Time	0	0	18
PERMITS TO WORK	53	48	832
RAMS APPROVED	2	4	93
REWARDS	4	2	41
SENDING OFFS	0	0	0


Observations by Reporting Company



Observations by Type

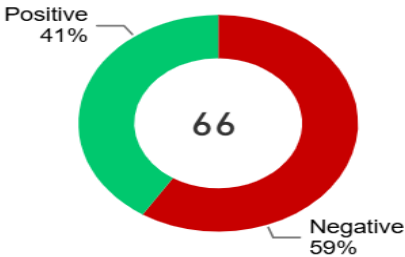


Observations by Resp. Main Contractor




Total Actions Reported	Open Actions (Clickable)	Closed Actions	Closed Past Due	Open/Closed Overdue Actions (Clickable)
326	38	288	68	27

Observations by Category



Site Walks by Reporting Company



CONFIDENTIAL

3

Type of information: General (CUSTOM)

BOP-IDOM-EHSS – Highlights(Week 30)

- **LNG Terminal 3rd test pack safely done.**



- **3rd time Fire brigade familiarization/survey LNG Terminal.**
- **Safety stand up by IDOM Construction management team.**




BOP-IDOM-EHSS – BBS Dashboard (Week 30)

Behaviour Based Safety Assessments

Last Update:
27 iul. 2026 03:30

Checklist Name: Toate
Related to Main Contractor: Toate
Major Area: BOP
From Week: 26W10
To Week: Toate

Safety Performance With TRIF

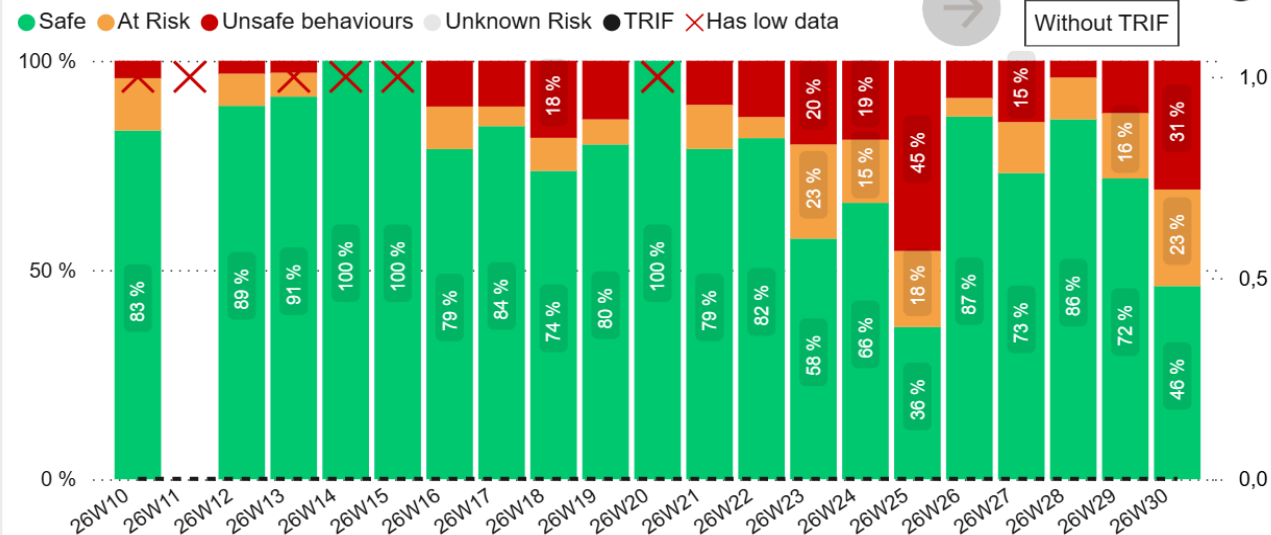

46,2%

Safety Performance (Last week)
▼ -34.2%
vs Previous period


30,8%

Unsafe behaviours (Last week)
▲ +21.2%
vs Previous period


70

Total assessments (Selected period)
▲ +17
vs Previous period


Safety Performance by Category

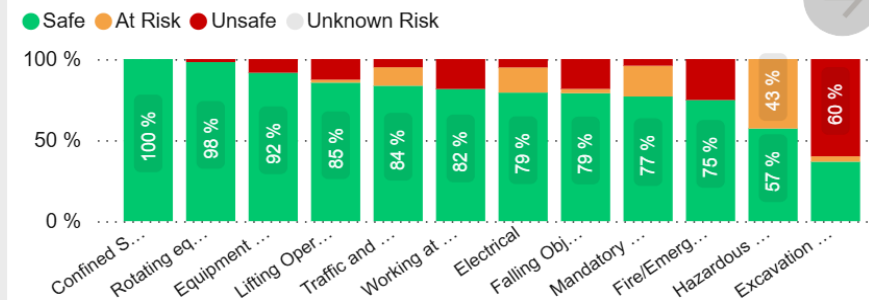


Assessment Timeline

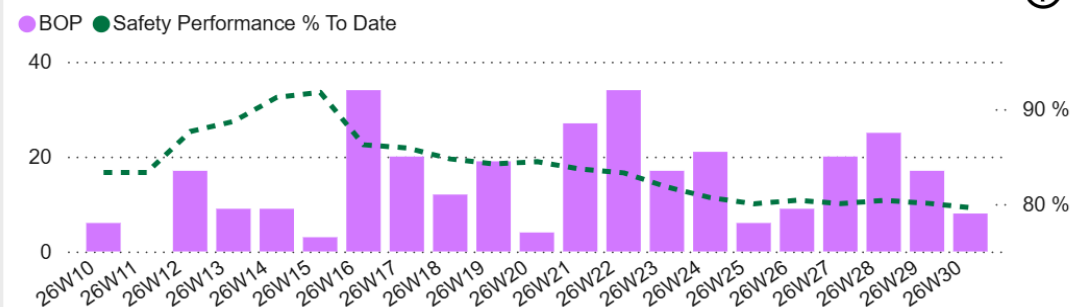

Assessments related to Main Contractor



Feedback distribution

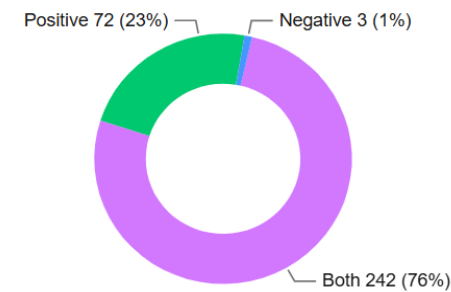

• PROJECT P-103475 · EPCM BODEN BOP

BOP Quality.

Centralized quality control workspace for the **Balance of Plant** scope of **STEGRA's** green steel facility in Boden — the world's first large-scale fossil-free steel plant. Inspection records, ITPs, audits, NCRs and procedures, governed by the IDOM site team.

QUICK LINKS

Team members

EXTERNAL TOOLS

 Airtable · QOC

 Airtable · NCR

 Airtable · NOI

 Omega 365 · EDMS

CLIENT	STAGE	QUALITY LEAD	LAST SYNC
--------	-------	--------------	-----------

QA/QC — Weekly Summary

REPORT WEEK
W30

● KEY ACHIEVEMENTS

- 1 Chart Ferox Pressure Test completed. Awaiting the As Built Dossier.
- 2 TPs GRK UG has been reviewed and rejected . IDOM QC requested GRK to participate in a workshop to guide the contractors on the applicable requirements and ensure a consistent understanding and implementation of the process.
- 3 ITPs for GRK-Ponds, Roads,UG,Rails has been expedited.
- 4 STS -Quality Plan, ITPs has been expedited. ITRs workshop to be organize.
- 5 EPCM QC will coordinate with EPCM Construction on Test Packs and Golden Weld Joint requirements to ensure consistent understanding and implementation by all contractors.
- 6 Follow-up is ongoing regarding the partial handover. The Pipe Bridge partial handover is still pending .

● LOOK-AHEAD · W31

- 1 Review Chart Ferox Test Packs 15 ,16,17,18 and participate in the associated walkdown activities to verify system readiness, completion status, and outstanding punch items prior to handover.
- 2 EPCM QC to continue the Site Surveillance, focus on the Contractor Construction supervision availability, Design Revision availability on site, Contractor Supervision acknowledgment of project specification, sequence of construction, inspection and test requirements.
- 3 Fermix shall submit an updated TP Register. EPCM QC and EPCM Construction shall review the register for compliance with project requirements
- 4 Geomembrane Air Test is schedule for this week in the West Pond. NOIs has been raised by GRK Ponds, EPCM QC will be present during the test.
- 5 Follow-up the Closure of Supply Chain PLs and CMS PLs.

QA/QC — Major Risks

MAJOR RISKS

- 1 NCRs 801 has been issued by Stegra against EPCM Contractor Management, Ponds Geomembrane Installations. Stegra has raised concerns that the current execution of the geomembrane installation works does not provide sufficient evidence of compliance with the contractual requirements, the geomembrane manufacturer's installation procedures, and the applicable Swedish standards referenced in the project specifications.
- 2 The concrete pads are required for the FF underground piping system, including hydrant valves, sectioning valves, and the thrust blocks associated with the hydrants. However, these concrete pads have not yet been installed. According to EPCM Engineering, these works were not included within the GRK underground piping scope. The intention last year was for the works to be executed under a separate contract by another contractor, which ultimately did not materialize. It should also be noted that the Priority 0 Test Packs were pressure tested last year and subsequently backfilled. Therefore, in order to install the required concrete pads and thrust blocks, excavation activities will now be necessary to expose the affected areas. This situation may have an impact on the completion sequence and should be addressed as soon as possible to avoid further delays.

QA/QC Site Quality


REPORT WEEK
W30


1
NEW NCR · W30
EPCM 0 · STEGRA 1


12
NCR OPEN
OF 107 TO DATE


63
QOC OPEN
OF 1007 TO DATE


89%
NCR CLOSED
95 OF 107 TO DATE

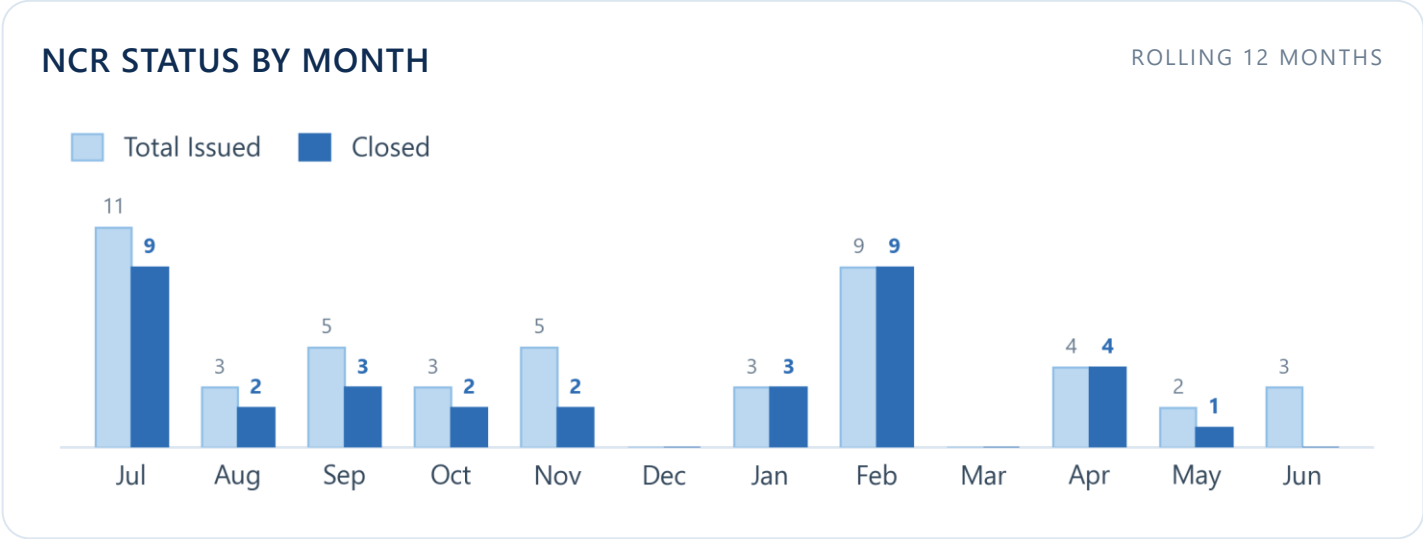

QUALITY OBSERVATIONS & NCR

OWNER	NEW	TO DATE	OPEN	>30D	>60D
QUALITY OBSERVATIONS · QOC					
EPCM	9	257	31	16	7
Stegra	0	750	32	14	16
TOTAL	9	1007	63	30	23
NON-CONFORMANCE · NCR					
EPCM	0	23	3	1	2
Stegra	1	84	9	2	6
TOTAL	1	107	12	3	8

TEST PACK STATUS

Ferrmix

CHART Ferro

GRK

Nordic Concrete

PLAN 0

SUB 2

REV 1

APR 1

CMP 1

AB 1

PLAN 18

SUB 9

REV 7

APR 7

CMP 7

AB 0

PLAN 0

SUB 9

REV 9

APR 0

CMP 0

AB 0

PLAN 0

SUB 0

REV 0

APR 0

CMP 0

AB 0

PLANNED → SUBMITTED → REVIEWED → APPROVED → COMPLETED → AS-BUILT

0%

39%

0%

0%

QA/QC — NOI & Site Activity


QUALITY PYRAMID



Site activities = NOIs + QOCs + site surveillance

WEEKLY NOI ISSUANCE BY CONTRACTORS

ROLLING 12 WEEKS

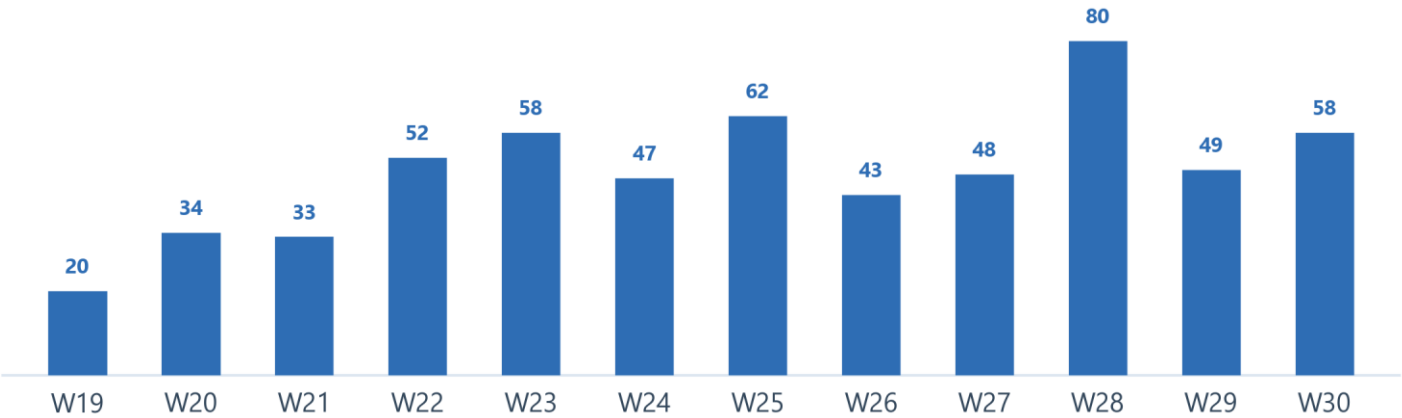

INSPECTION STATUS · W19–W30

Rejection rate 0% · KPI threshold ≤ 5%

METRIC	W19	W20	W21	W22	W23	W24	W25	W26	W27	W28	W29	W30
Accepted	20	34	33	52	58	47	62	43	48	80	49	58
Rejected	0	0	0	0	0	0	0	0	0	0	0	0
Postponed	0	0	0	0	0	0	0	0	0	0	0	0
Rejection Rate	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%

QA/QC — Partial Handover

6 partial handovers between contractors in progress · 1 completed

6 IN PROGRESS

1 COMPLETED

PARTIAL HANDOVER BETWEEN CONTRACTORS

6 RECORDS

DEFINITION	SYSTEM	SUBSYSTEM	TAG NO	ITRS	TCCC	WALKDOWNS	PUNCH LIST	COMPLETED
GRK-Stegra-Municipality Piping	SIN-800-TEMP	SIN-800-01-TEMP	TEMP-BOP-1001-WRW-0800-10P1-NI	P-02A	TCCC	Done	None	Completed
GRK-Stegra-Municipality Civil	SIN-800-TEMP	TBD	TEMP-BOP-Civil_Works_ Temporary Line	C-25A	TCCC	—	—	—
GRK-Nordic RW Area	SIN-907A	SIN-907-01,02	RW Receiving &Pumping Station	TCCC	TCCC	Done	Yes	—
GRK -Nordic LNG Area	SIN-909A	SIN-909A-101	LNG-TCCC from GRK to NOR	TCCC	TCCC	Done	Yes	—
GRK-Ferrmix PB Area	SIN-980	SIN/980/01,02	Pipe Racks, Columns,Foundations 1-5	TCCC	TCCC	—	—	—
ANFRA/STS PDOP Area	SIN-987	SIN/987-02	PDOP Capacitor Bank Trenches	TCCC	TCCC	Done	Yes	—

Project Risk Update – Balance of Plant

- 41 total BOP Type 2 risks identified – 20 active, 1 draft, 0 parked, 0 submitted, 16 retired, 3 expired, 1 Canceled
- Out of 20 active risk – 0 critical, 5 major, 11 moderate, 4 minor risks assessed
- 60 total mitigation actions planned for all active risks – 4 overdue, 24 open, 30 closed, 2 canceled

Data Date: 17 July 2026

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R22	Construction & Site Execution	GNRL - Misaligned area schedules and complex multi-contractor interfaces lead to blocked BOP Workfront and delayed equipment deliveries resulting in schedule and cost impacts	30	- Sequence UGP and piping to avoid SMS install clashes; await SMS schedule (31/07/2026 - Open) @Marten Sonnerup - Interface Meeting with STM and BOP Construction team to align UGP works and SMS equipment deliveries. (31/07/2026 - Open) @Marten Sonnerup - Prepare reforecast schedule for BOP and Interface dates with STM and other areas (27/07/2026 - Open) @Reghardt Heunes / Comment: It is under discussion and waiting for the STM-McDermott rebaseline, which currently they are working on - Align and finalize with WTP1 and WTP2 for access dates (31/07/26 - Open) @Marten Sonnerup / Comment: Ongoing discussion, as there is interference with Eiffage due to road works in front of WTP2, where Eiffage is scheduled to carry out works; an alternative northern access is also under discussion.	19
B1.BOP.R10	Construction & Site Execution	RAIL - Late Handover of STM Construction Areas (Scrapyard, CLP) – Impacting Rail	25	- Follow up on Micropiling progress in Scrapyard area (15/08/2026 – Open) @Roger Campbell / Comment : Work must be completed by mid-August to allow follow-on activities. Delays beyond early September will impact rail works and may place them on the critical path, with potential multi-month delays due to winter. The micro-piling contract has not yet been awarded by STM-McDermott, there might not be a short list in place; since execution takes ~8 weeks, award is required within the next few days to enable rail works to start in September as planned. Stegra have instructed STM-McDermott to provide an acceptable rebaseline.	23
B1.BOP.R548	Construction & Site Execution	Pipe Bridge (21) Modules Install blockage by STM and may need to be paused	21	- Finalize decision on BOP continuation of 19 modules and confirm if need by dates of utilities will still be met (31/07/2026 – Open) @Chris Van Der Berg	14
B1.BOP.R387	Construction & Site Execution	PDOP - Uncoordinated Installation of HV and Control Cables leading to blocked handover by HESE resulting in delay of permanent power	19	- HESE to review IFC prior to Production & Construction (31/08/2026 - Open) @Tomas Winter - HESE to define required documentation prior to Handover (31/08/2026 - Open) @Tomas Winter - [Stegra to] review and possibly revise [its] handover procedure to include electrical installation works (31/08/2026 - Open) @Tomas Winter	11
B1.BOP.R565	Project Delivery General	UGNW - Av 9 Underground piping installation may not be completed by end of 2026	19	- Award Avenue 9 scope to another contractor who is already working on site (to avoid loss of time due to running a tender and subsequent mobilisation) (31/07/2026 – Closed) @Tuncay Ozel	19

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.

Project Risk Update – Balance of Plant (2/2)

(Reviewed by Stegra and Idom Risk Management)


Status and summary comments as per *previous* week.

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R323	Construction & Site Execution	PDNW - Resource shortfall for Power Distribution Network (Single Source E&I) may impact construction progress	14	- Engage additional E&I resources or contractors to meet required manpower levels (31/07/26 – Open) @Tuncay Ozel / Comment: The Call-Off package was shared with STS on 13 July, while the OMEGA workflow was launched to support Stegra’s internal approval. STS confirmation and the ongoing signature process remain pending. - Closely monitor workforce allocation between STM and BOP to avoid bottlenecks (30/04/27 – Open) @Guillaume Camerini	9
B1.BOP.R436	Supply Chain Management	TEMP - Availability of emergency Diesel Generator TG4	5	- TG4 is scheduled for late May, and the contract signing for mid-June. (14/08/26 – Open) @Tuncay Ozel / Comment: The bidder has confirmed updated proposal submission in W30. Subject to receipt and review of the revised proposal, TG4 is scheduled to be issued in W31.	5
B1.BOP.R484	Construction & Site Execution	PCRU - Pipe Bridge – Hydrotesting activities may get pushed into 2026–2027 winter period due to delayed prerequisites. (QLT)	15	- Develop an overall hydrotesting program, which final completion of last hydrotesting activity is before the start of the 2026–2027 winter.(30/09/26 – Open) @Javier Cervera / Comment: It is confirmed that glycol will not be used; therefore, no hydraulic piping tests will be conducted during winter.	11

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.



PIPE BRIDGE (Target W35)



NPB-511 (Target W37)



PROGRESS W30

- CR approved for Siemens repair works. Siemens confirmed start of repairs W32
- Inspections ongoing for Pipe Bridge earthing. ITP for testing released

BLOCKERS	RESPONSIBLE
----------	-------------

- | | |
|--|-------------|
| <div></div> PB EARTHING DELAYS ON INSTALLATION, INSPECTION & TESTING → | FERRMIX |
| <div></div> ACTEMIUM ITR APPROVAL → | STEGRA |
| <div></div> GRK/FERRMIX ITR APPROVAL → | IDOM/STEGRA |

PENDING ACTEMIUM/EITECH ITRs	PROGRESS
-Pipe Bridge Underground Earthing →	0% [Linked to (3)]
-NPB-511 underground Earthing →	0% [Linked to (5)]
-ELA-01 roof trays →	50%
-NPB-511 MV, LV & Control Cables →	50%
-Temp Trafos to NPB-511 MV & Control Cables →	50%
PENDING GRK ITRs	PROGRESS
-Pipe rack foundations, Columns & groundworks →	0%
-NPB-511 groundworks →	0%
-Temporary transformers Groundworks & Lightning mast →	30%
PENDING FERRMIX ITRs	PROGRESS
-Priority 1 zones 3-4-5-6 Structural & Cable racks →	20%

BOP-IDOM-Temporary Water Progress

W30

4

Milestone

3

High priority

W33

Target

Status by Milestone

	Progress	Priority / target*
1 Permanent RW pipes around RW Chamber Approved commitment since 11 May by STEGRA PM; no action taken from GRK.	50%	High W33 1
2 Temporary spool + RW tank inlet CR-04387 raised 14 May. Commercial agreement still open. Since May, GRK only submitted price proposal on one occasion.	20%	High W32 2 3
3 Temporary lines TWTP → ASP CR-4359 raised 5 May for connection to ASP. Commercial agreement still open. Since May, GRK only submitted price proposal in 2occasions.	25%	High W31 2 3
4 RW tank watertightness test Test done W26. Test failed. C3C to come W32 to repair.	50%	Low W33

*Targets can be achieved only if blockers are resolved W31.

BLOCKERS / CONTRAINS

- 1

Commercial action to GRK

GRK/Stegra to reach commercial agreement
- 2

CR Review resources


Add resources to reduce CR review time. Average review time in ACC 67 days
- 3

Strategic route GRK TEMP or NIWA

Strategic Decision Required: Proceed with the temporary water solution or transition to the permanent solution. NIWA to install → milestone 2 and 3. NIWA starts in October and finalize January as per contractual schedule

BOP | IDOM Level 1 Schedule

Progress

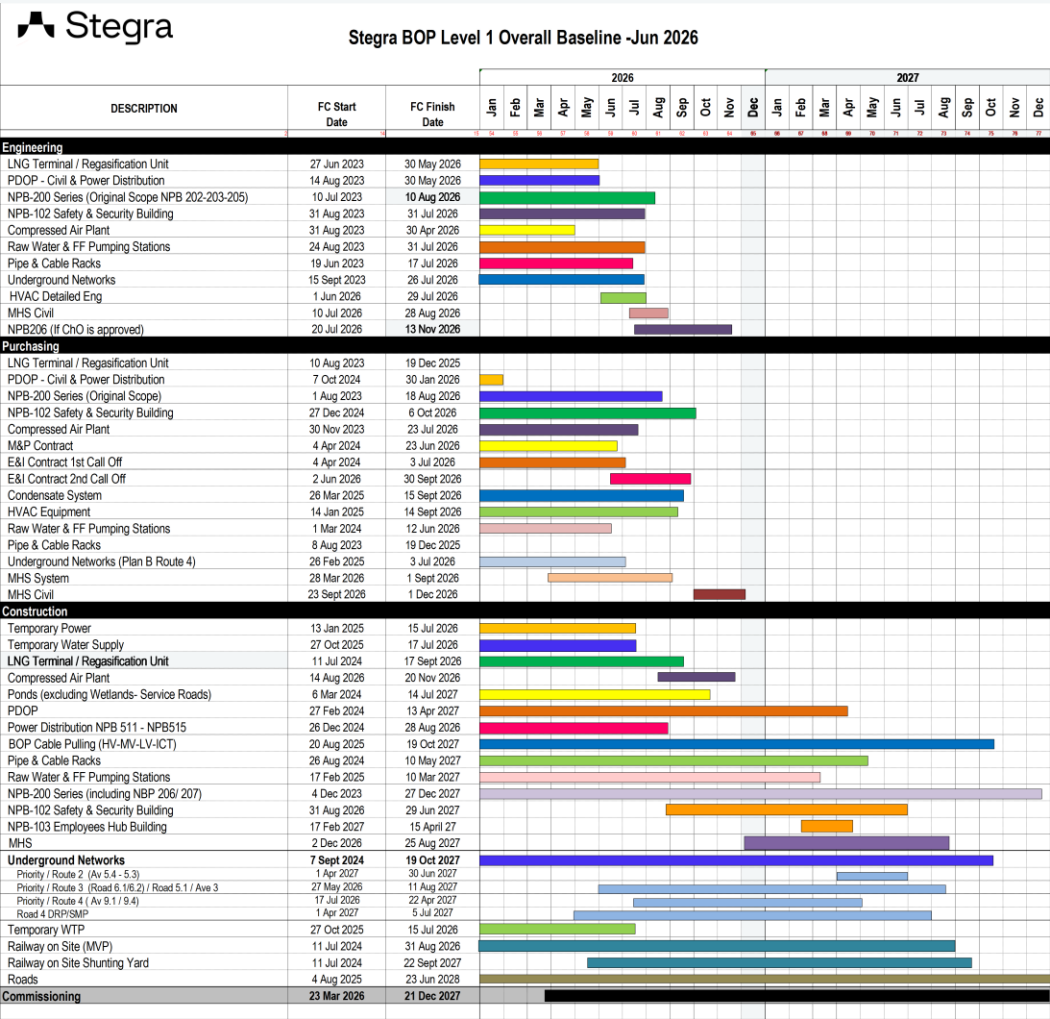

June 2026 Will be updated W33 (Cut off W30)

Achievement

Actual / Plan OR Forecast / Plan as percentage

On track / no issue


Risk / Concern

Behind


BOP | IDOM Summary – Activities and Progress

Progress

Overall Progress		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08	6-month key Waypoints		
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	Key Waypoints	Planned date	Forecast date
Engineering	Week	0,05%	0,24%	0,16%	31%	21%	0,28%	Temporary Water (Ready to Supply)	31 Jul 2026	30 Oct 2026
	Cumm.	97,17%	98,15%	97,50%	100%	99%	97,78%	Temporary Power (Ready to Operate)	30 Jul 2026	30 Sep 2026
Procurement (TG - Purchasing Process)	Week	0,53%	2,88%	2,35%	23%	18%	2,89%	Power Supply from NPB-511 to ASP	31 Jul 2026	30 Sep 2026
	Cumm.	67,97%	76,84%	70,95%	96%	88%	73,84%	Piping Connections - Priority 1 Finish	28 Aug 2026	28 Aug 2026
Manufacturing (On a Monthly Basis - Monthly Cut Off)	Week	1,64%	1,64%	1,64%	100%	100%	0,00%	P2 – Pipebridge Installed + Piping Connections Finish	23 Oct 2026	23 Oct 2026
	Cumm.	94,20%	94,20%	94,20%	100%	100%	94,20%	P5 – Pipebridge Installed + Piping Connections Finish	28 Aug 2026	28 Aug 2026
Construction	Week	0,42%	0,60%	0,48%	87%	69%	0,82%	P4 – Pipebridge Installed + Piping Connections Finish	19 Nov 2026	27 Nov 2026
	Cumm.	51,86%	53,30%	52,49%	99%	97%	53,31%	Priority 1 UG piping installation completion	17 Jul 2026	30 Sep 2026
Overall	Week	0,74%	0,95%	0,85%	87%	78%	0,61%	Railway Groundworks Crossings Start	15 Jun 2026	17 Aug 2026
	Cumm.	68,22%	69,46%	68,72%	99%	98%	69,34%	Construction –slide 37-		

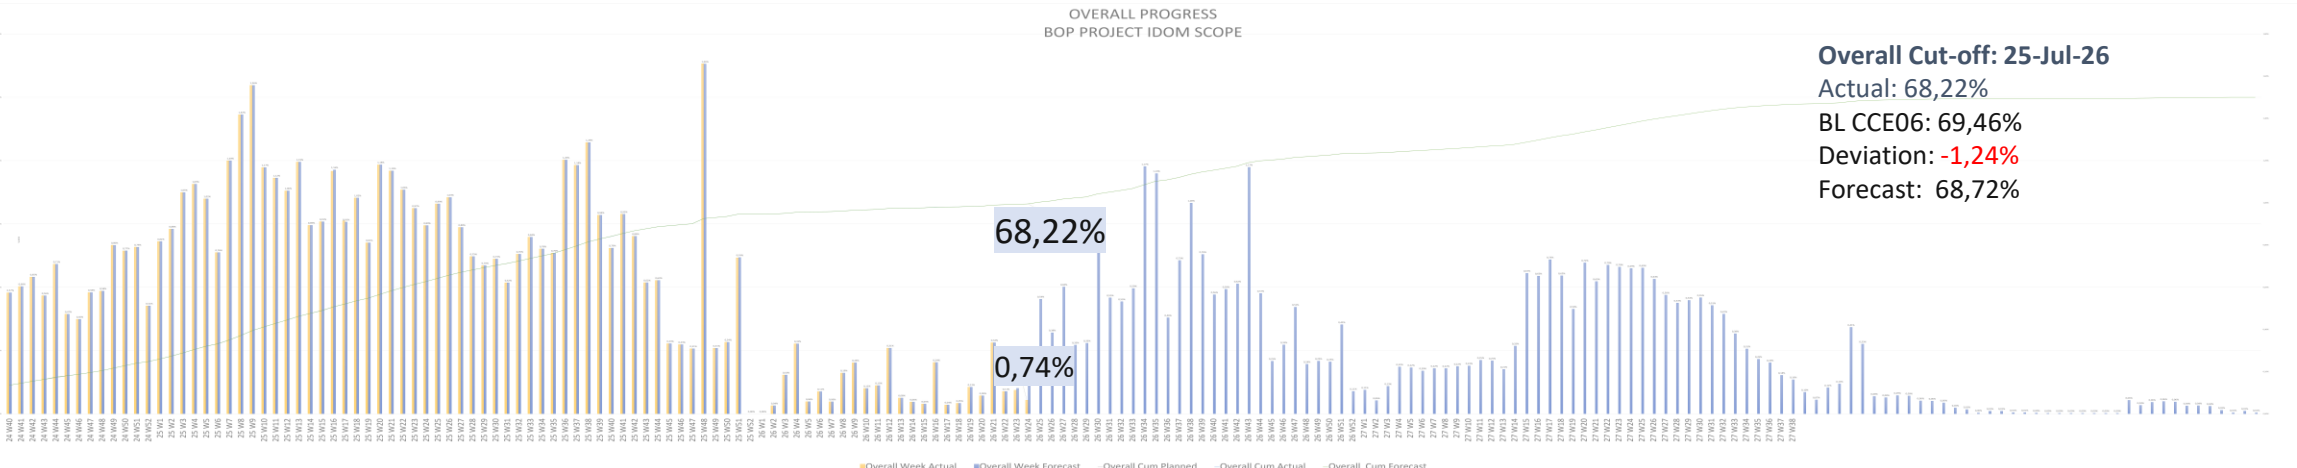

BOP - 6 Weeks Look Ahead

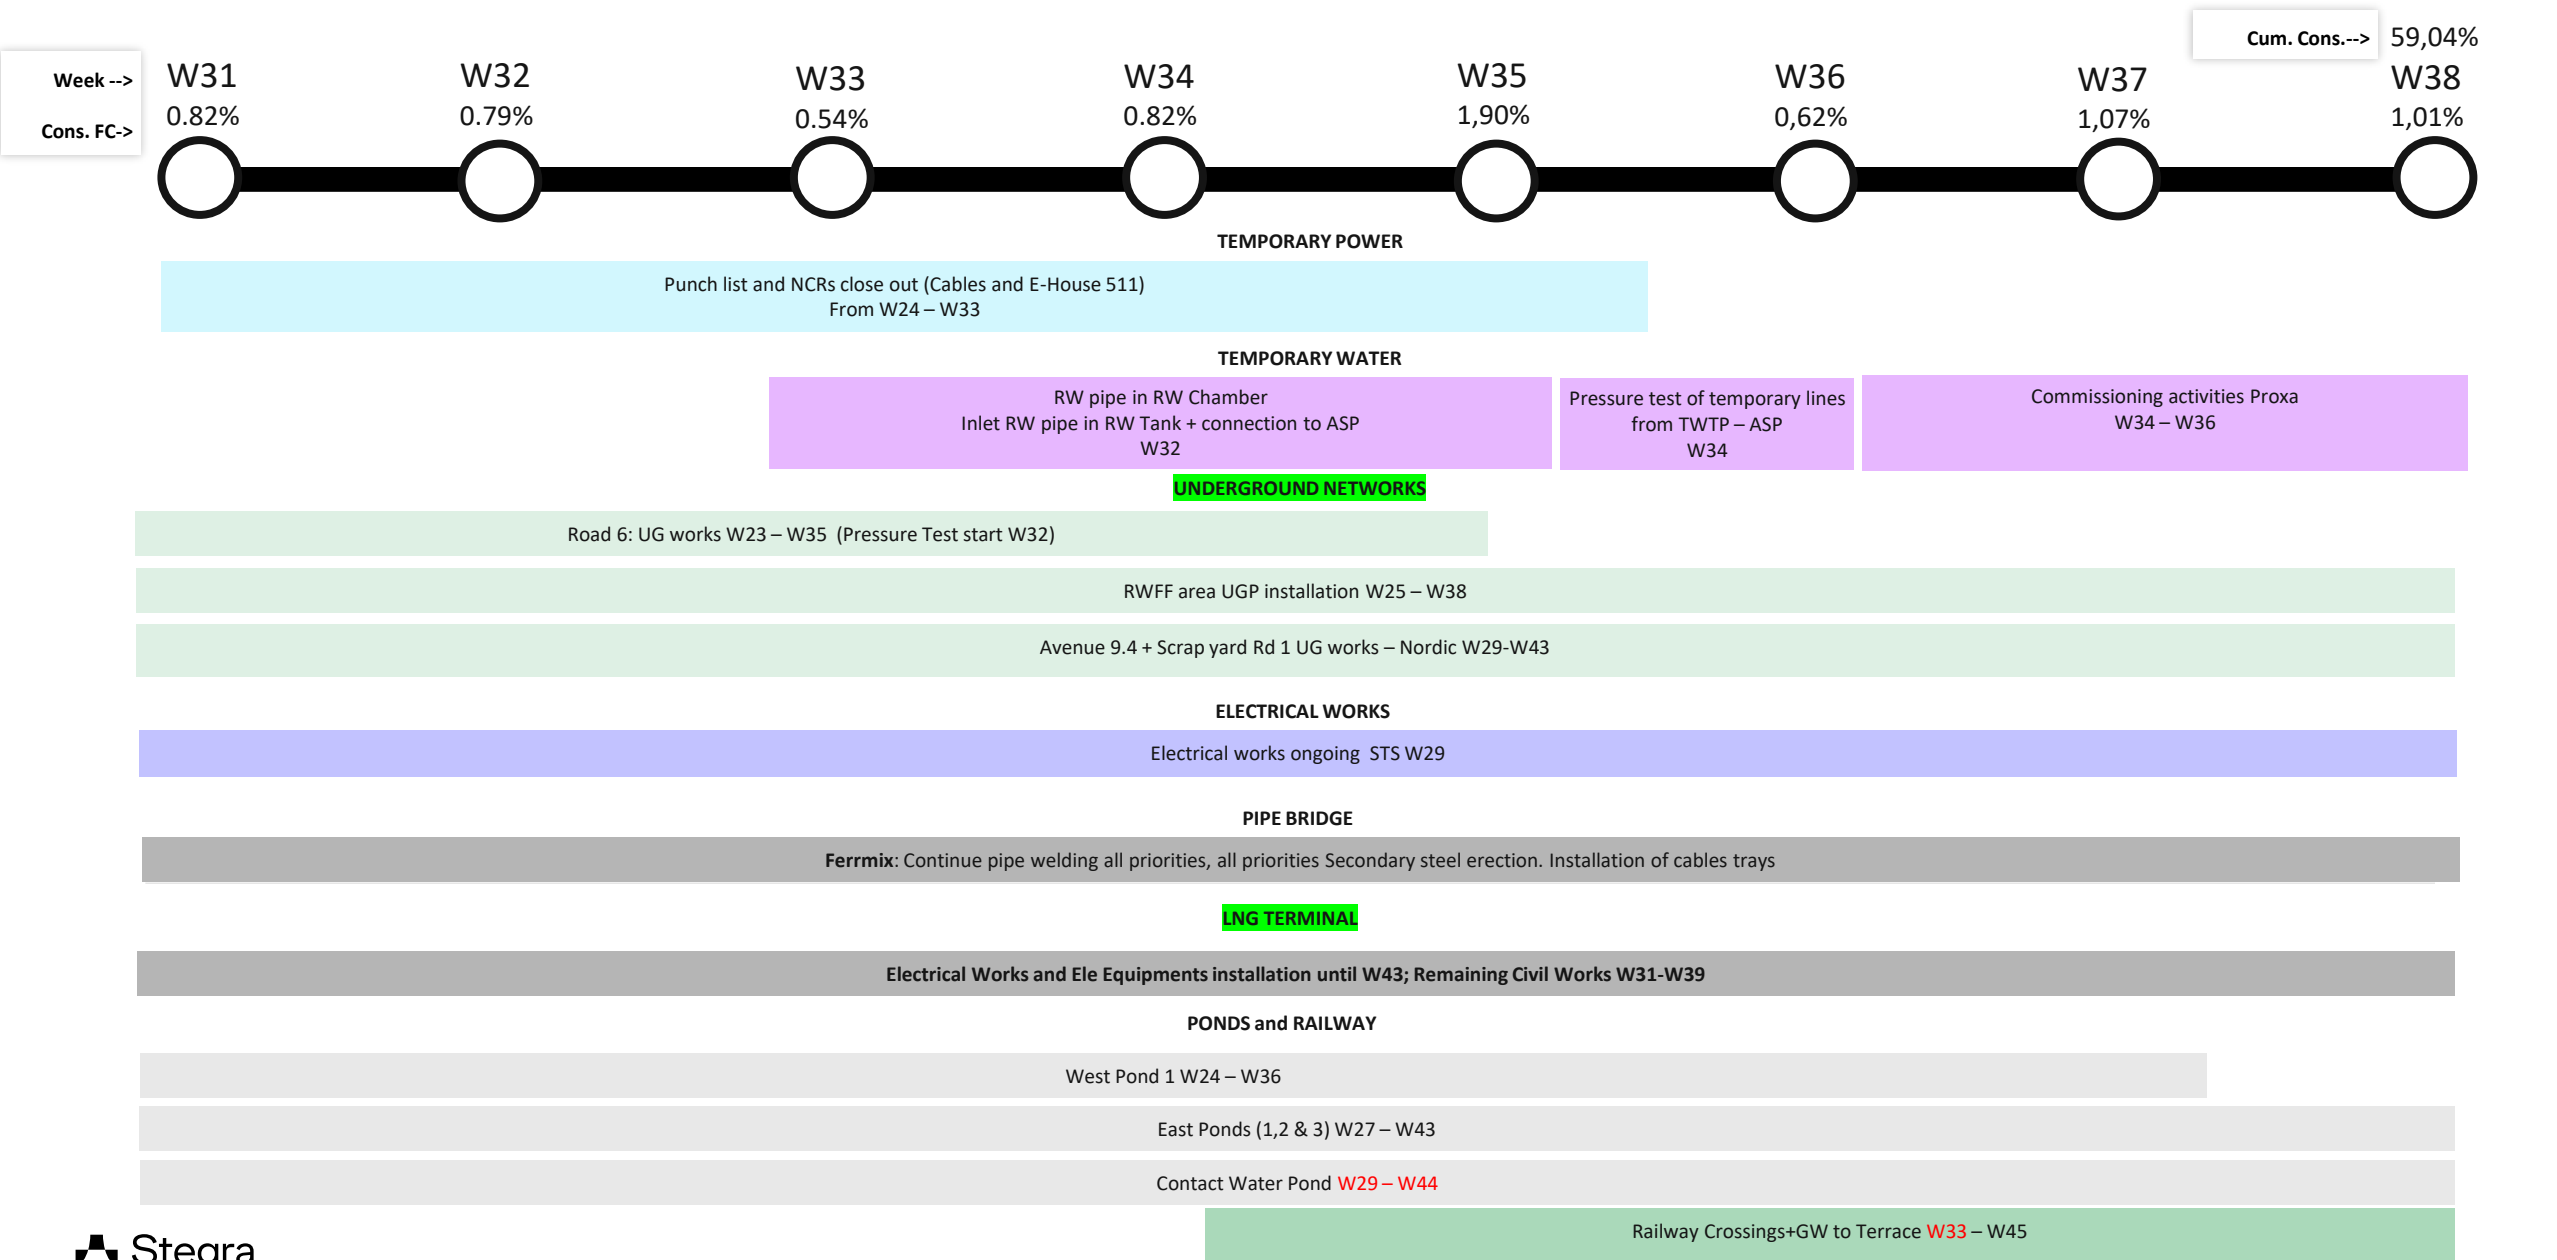

BOP | IDOM Summary – Activities and Progress -100 days look ahead




W30

Main deviations and mitigating actions

Discip	Red Activity	Due date	Mitigation Action
Proc	Chemical Dosing system for RW	W31	- Proxa: Updated proposal and CRS received, under review. - KURITA: RFQ for Basic design sent. they confirm that will present the proposal on week 31.
Proc	NPB-102: Security Bldg	W31	Several companies involved in the procurement process: - Nordia: (€3.6 M offer under the clarification phase). - LC: quotation expected by 14/08/2026. - KSH: partial offer excluding interior distribution scope. - MKL BAU Sp.: quotation expected by 14/08/2026. Steel structure supply and erection only. - Plus 10 additional companies have been contacted. Waiting their responses.
Proc	PB & Air Compressor found. - Retender	W31	Call-off #3: PGB approved, Commercial and contractual alignment is ongoing. Nordic's proposal with updated BOQ, received. Commercial negotiation to follow.
Proc	E&I Call-Off 1	W31	STS contract documents totally agreed. Contract to be signed on W30.
Proc	GW commitments	W31	- East ponds, Contact water pond and GW+crossings railway are executed. Ponds KoM held in W25. GW workshop w31. - East ditch. Status: Acknowledge. Pending to be executed. Warning! This is a predecessor for ROS GW in sections 4 and 5.
Eng	Sweco	W30	- Road design packages expected before summer break will come after w36. No clear delivery dates available. - Rail Memo 20. Received only partially on 03/07. Missing service roads update and GW deliverables. Railway memo 21 will come after summer break. - Earthing. Ongoing discussions to clarify the scope. In parallel, Sweco is analyzing the existing information and preparing the team to start the production. - Fencing. Sweco raised two CR: CR-4433 for BOP/Steel Mill and a new one for HMP. Stegra eng will request alternative quotation. Hours provided by Sweco was too high: 4,250 hours for BOP.
Eng	Hydrogen pipeline crossing (Railway Section 4A)	W33	Sweco raised CR-04439 for the Geotechnical investigations, for CR-04441 for the culvert design and CR-04444 for the rest of the civil works. Stegra to execute the CO for Sweco to start the works when they are back from holidays. CRITICAL execution CR-04441 (culvert), design works shall start w33, including final number of pipes.
Con	Field Change Requests	W31	Stegra/IDOM to define the procedure on site for Filed Change Request and the Red-marked drawings, to establish how to include changes in the design due to construction reasons.
Con	PB Piping Connections + Pending Fittings	W35	WK30 2026- 15 welders working vs 20 forecast. 660 Forecast inches/week, Actual 535 inches/week
Con	GRK - Temporary power and WTP	W35	RW: temporary line in RW chamber CR discussion ongoing, RW tank filling pipe and overflow system Material delivery TBC, temporary pipes to TWTP to ASP CR discussion ongoing. Temporary power punch list close out ongoing

Last Week Key Achievements


- ✓ **Significant progress:** 535 Inches welded and 3% progress achieved during this week. Total 14.180 inches out of 20.841 welded done 68% progress achieved.
- ✓ Cable pulling: Total 12.629 out of 43.553 - **29% progress achieved**
- ✓ East ponds: Completed excavation east ponds. **100% progress achieved. 31.000m3**

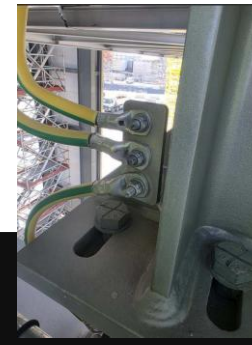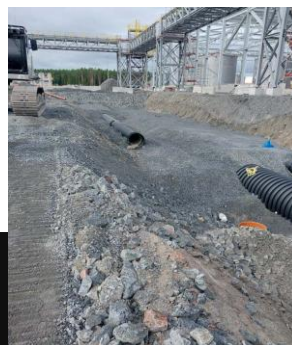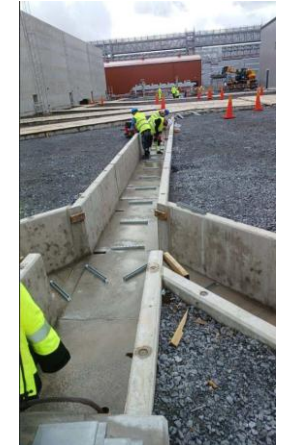

Distribution (Power) – Activities and Progress

Progress

PDOP Progress		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,75%	0,00%	100%	0%	0,00%
	Cumm.	99,25%	100,00%	99,25%	100%	99%	99,25%
Construction - PDOP	Week	0,09%	0,96%	0,00%	100%	9%	0,00%
	Cumm.	92,91%	93,64%	92,56%	100%	99%	92,56%
Construction - NPB 511	Week	0,00%	0,00%	0,00%	100%	100%	3,06%
	Cumm.	84,69%	84,69%	84,69%	100%	100%	87,75%
Temporary Power		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Construction - Temporary Power	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	99,00%	99,00%	99,00%	100%	100%	99,00%

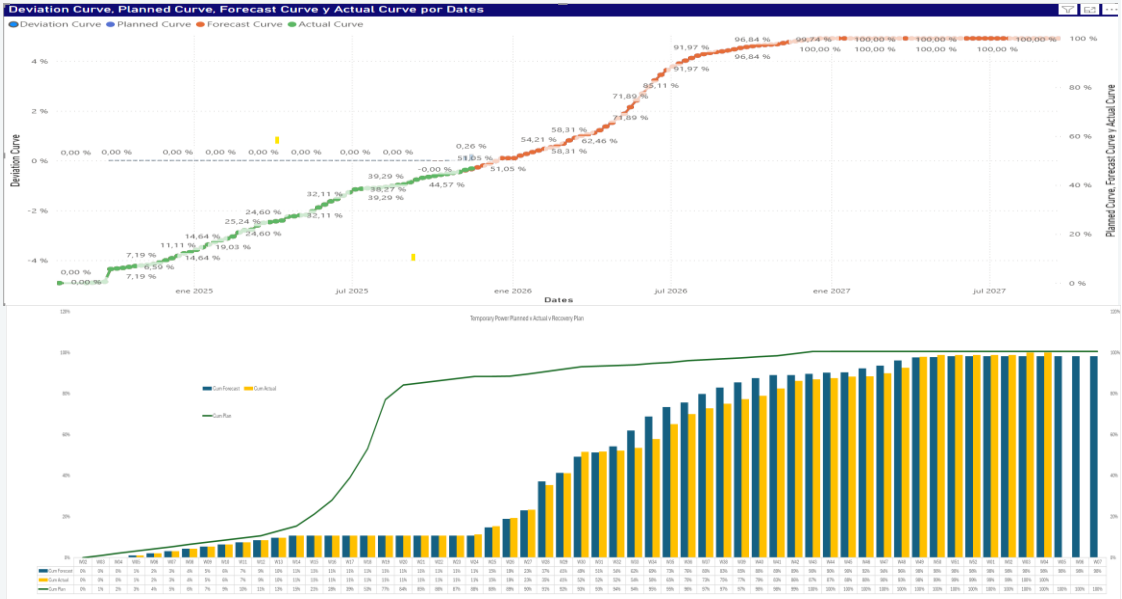


Main deviations and mitigating actions		
Discipline	RED Activity	Mitigating action
Con	Actemium: Delay PB and NPB511 UG earthing completion	Pending contractual agreement Stegra/Actemium
Con	SIEMENS: Delay to finalising NPB511 punch items	Siemens mobilization to site (expect WK33). 1 week is needed to close punches

6-month key Waypoints		
Key Waypoints	Planned date	Forecast date
Mechanical Completion Temp Power	30 Jul 2026	30 Sep 2026
Electrical Works by STS Start	06 Jul 2026	27 Jul 2026

BOP | Gas LNG – Activities and Progress

Progress

LNG Progress		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Construction -LNG	Week	0,60%	1,97%	1,00%	60%	30%	1,00%
	Cumm.	89,25%	93,96%	92,70%	96%	95%	93,71%

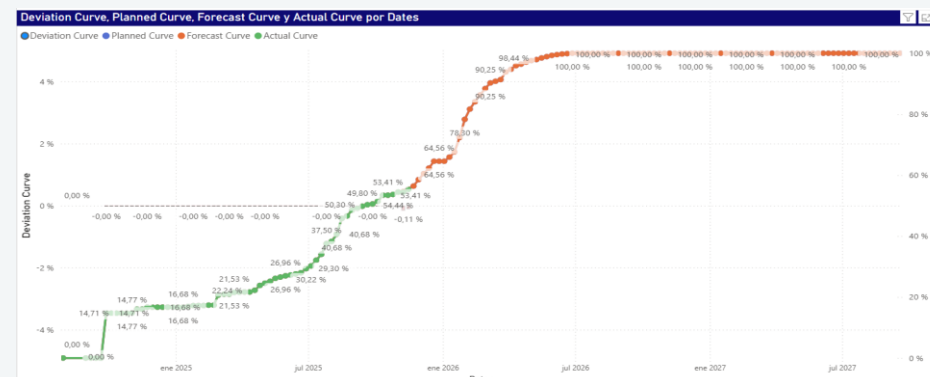

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Civil Works complete (remaining civil works)	17 July 2026	08 Oct 2026
Commence Control System Cabinet installation	08 Jul 2026	22 Aug 2026

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Mec	MV Transformer delivery date postponed to October – 10 weeks from Stegra final decision regarding the insulation	Vendor expediting
Mec	Pending 11 Pressure test to be performed	Expedite Test pack submission, review and approval
Civ	Risk of interference between Nordic (civil works and UG network starting in week 31) and CHART (Mech and electrical works)	Interface management
Civ	Control unit basement to be levelled before installation (W34)	High priority – expedite survey (IDOM) and execution (Nordic)

Achievement Actual / Plan OR Forecast / Plan as percentage


On track / no issue
 Risk / Concern
 Behind

BOP | Distribution (Pipe Bridges) – Activities and Progress

Progress

PB & UGP Progress

		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,15%	0,15%	0,05%	291%	100%	0,00%	
	Cumm.	100,00%	100,00%	99,90%	100%	100%	100,00%	
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%	
Pipe Bridge (Foundation+Steel)	Week	0,51%	0,42%	0,52%	99%	122%	0,50%	
	Cumm.	85,16%	84,40%	85,48%	100%	101%	85,98%	

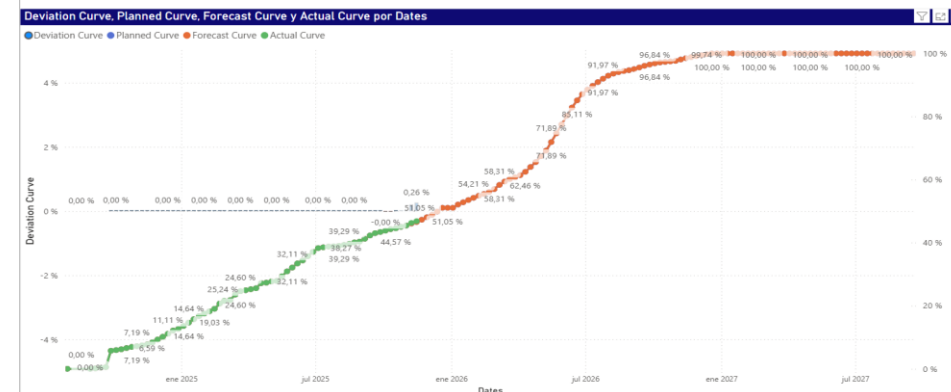

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Piping Connections - Priority 1 Finish	28 Aug 2026	28 Aug 2026
Piping completion Priority 1 Finish	23 Oct 2026	23 Oct 2026
Pipe rack Modules - Priority 4 Finish	24 Aug 2026	01 Sep 2026
Pipe rack Modules - Priority 3 Finish	25 Sep 2026	09 Oct 2026
Pipe rack Columns - Priority 4 Finish	20 Aug 2026	27Aug 2026

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Con	PB- Piping connections + pending fittings	WK30 2026- 15 welders working vs 20 forecast. 660 Forecast inches/week, Actual 535 inches/week
Con	PB02. Foundation not possible due to works by Mc Dermott	McDermott piping pending. Focus on other areas/ Award civil works contractor to start works.
Con	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	Confirmation from Stegra to proceed with execution/ Award civil works contractor to start works.
Con	Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott.	Foundations can be start when McDermott release the area


Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue Risk / Concern
 Behind

BOP | Distribution (UG piping) – Activities and Progress

Progress

PB & UGP Progress		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,15%	0,15%	0,05%	291%	100%	0,00%
	Cumm.	100,00%	100,00%	99,90%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
UG Piping (Schedule)	Week	0,24%	1,36%	1,26%	19%	18%	1,21%
	Cumm.	18,39%	20,26%	19,93%	92%	91%	21,14%

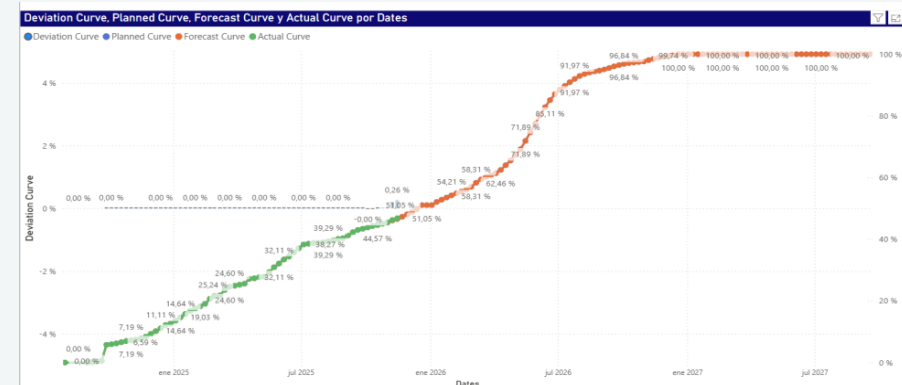

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
UGP – Route 0 testing complete	26 Jun 26	07 Sep 26
UGP – Route 2 Commencement	01 Apr 27	01 Apr 27
UGP – RW & FW Completion	06 Oct 26	06 Oct 26
UGP – Priority 4 and Scrap Yard Completion	10/ Feb 27	10 Feb 27

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Piping	Priority 0 (Potable water tank area) UG piping to be connected	Emergency center access to be modified by Site service
QAQC/Proc	Pressure tests in Priority 1 to be done	Test pack approval and CO signature

Achievement Actual / Plan OR Forecast / Plan as percentage


■ On track / no issue
 ■ Risk / Concern
 ■ Behind

BOP | Buildings & Other IDOM – Activities and Progress

Progress

Buildings & Others Progress

		W30-26 (Last W) 20/07-25/07					W31-26 (Current W) 27/07-01/08	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,04%	0,04%	0,04%	100%	100%	0,21%	
	Cumm.	97,31%	97,31%	97,31%	100%	100%	97,52%	
Procurement (TG)	Week	2,15%	0,20%	2,15%	100%	1075%	1,20%	
	Cumm.	80,11%	82,02%	80,16%	100%	98%	81,31%	
Construction - RWPS & FF	Week	0,01%	0,00%	0,00%	100%	100%	0,35%	
	Cumm.	74,73%	74,72%	74,86%	100%	100%	75,08%	
Construction - NPB 200	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	55,95%	55,95%	55,95%	100%	100%	55,95%	

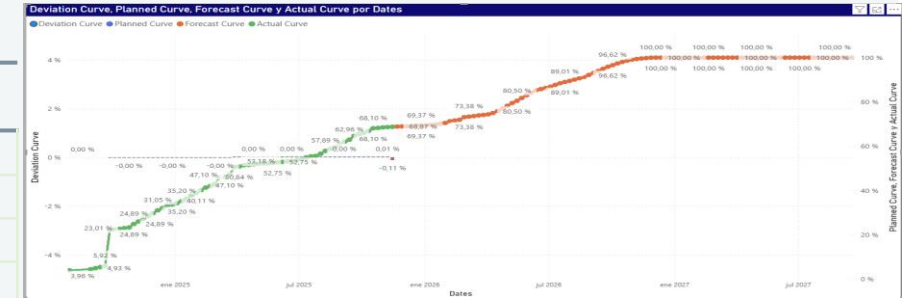

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Commence RW Pumping station structure erection	10 Sep 2026	10 Sep 2026
Commence FF Pumping station civil works	14 Sep 2026	14 Sep 2026
Commence RW Pumping station equip. installation	30 Nov 2026	30 Nov 2026
Commence FF Pumping station structure erection	19 Oct 2026	19 Oct 2026
Commence NPB205 civil work	19 Aug 2026	19 Aug 2026
Commence NPB102 civil work	31 Aug 2026	31 Aug 2026
Temporary WTP start operation	31 Jul 2026	30 Oct 2026

Main deviations and mitigating actions


Discipline	RED Activity	Mitigating action
Eng	NPB 207 – Crane Maintenance Workshop: Meeting conducted with STEGRA. Progress has been made but there are still open points.	Confirm whether building is required, define procurement strategy and utilities needs
	NPB 202 – Building on hold due to ongoing discussions concerning storage capacity and need for sprinkler system	Fire extinguishing system needed Pending building layout and rack distribution Chemical storage room layout, fire resistance requirements, containment method
	NPB 203 – Refractory Warehouse	Confirm design change insulated vs non-insulated building concept
	Chemical Container – oils and lubricants and Supplier container outside NPB 202: STEGRA engineering has retained three alternatives	Stegra to communicate power needed and any other utility depending on network under IDOM scope of design
	Review of fire detection and alarm and sprinkler system drawing by certified engineer - Pending to have a plan from certified engineer to complete the review of the BOP documentation. No review has been started yet.	Stegra to expedite this process to avoid major impacts to procurement, installation...
Con	RW Chamber temporary spool and RW Tank inlet pipe	CR to be approved

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue ■ Risk / Concern
■ Behind

BOP | Engineering

Progress

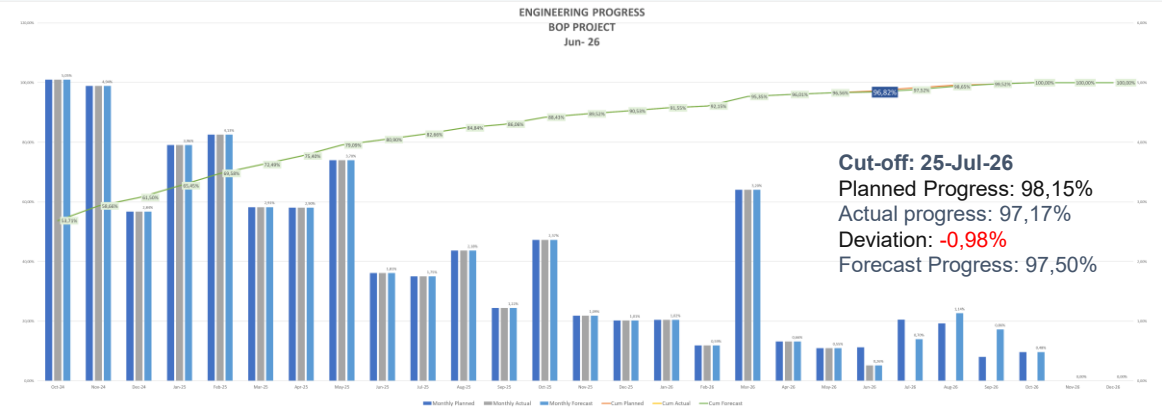

Plan deviations

RED Activity	Plan date	Fcst date	CP impact	Mitigating action	Who	When
UG system PB02 and other areas excav. dwg.	Sep-26	Sep-26	Y	- Monitoring Sweco contractual commitments - Splitting UG works in several contractors	Sweco IDOM Stegra	


Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
IDOM Integration Drawings & Excavation models UGP	IDOM has communicated to Sweco the deadlines by which they must provide the inputs for UGP design of all areas pending combined drawings and excavation models. Upcoming deadlines for Sweco: - CSP-WTP2 Area (Av. 6.0-6.1): 08-05-2026 (Delivered) - Priority 4 (Av. 9.3-9.4): 13-05-2026 (Delivered) - Priority 3 zone D (Av. 2.0): 20-05-2026 (Delivered) - Priority 5 (Road 7.5): 20-05-2026 (Delivered) - Finishing Area: 29-05-2026 (Delivered) - DRP-SMP area (Road 4): 26-06-2026 → Sweco to deliver drawings in September. 2D and 3D models were provided in w27 - DRP-Scrap yard area (Av. 9.1-9.2): 17-06-2026 (Delivered)	IDOM/Stegra	Sep-26	Open	Ongoing
Underground Piping Priority 0 Underground Piping Priority 4 Underground Piping Road 5.1 and 5.2	- Prio 0: Final revision removing holds in the roundabout in Av. 1 is moved to September. - Prio 4: IDOM is progressing with combined UGP IFC drawings. SWECO analyzed the possibility of reducing overall material and installation costs by modifying the design to reduce the meters of linear drainage/contact water gulleys. Stegra has approved the proposal and has instructed Sweco to proceed with the cheapest option. - Road 5.1 and 5.2: IDOM and Sweco UGP IFC drawings have holds from pipes going to NPB 207 – the design for this building is not developed. IDOM shall resubmit the IFC for combined drawings for Road 5. Sweco design is available.	IDOM/Stegra	Sep-26	Open	Ongoing

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Sweco Engineering Management (IDOM EPCM – SWECO)

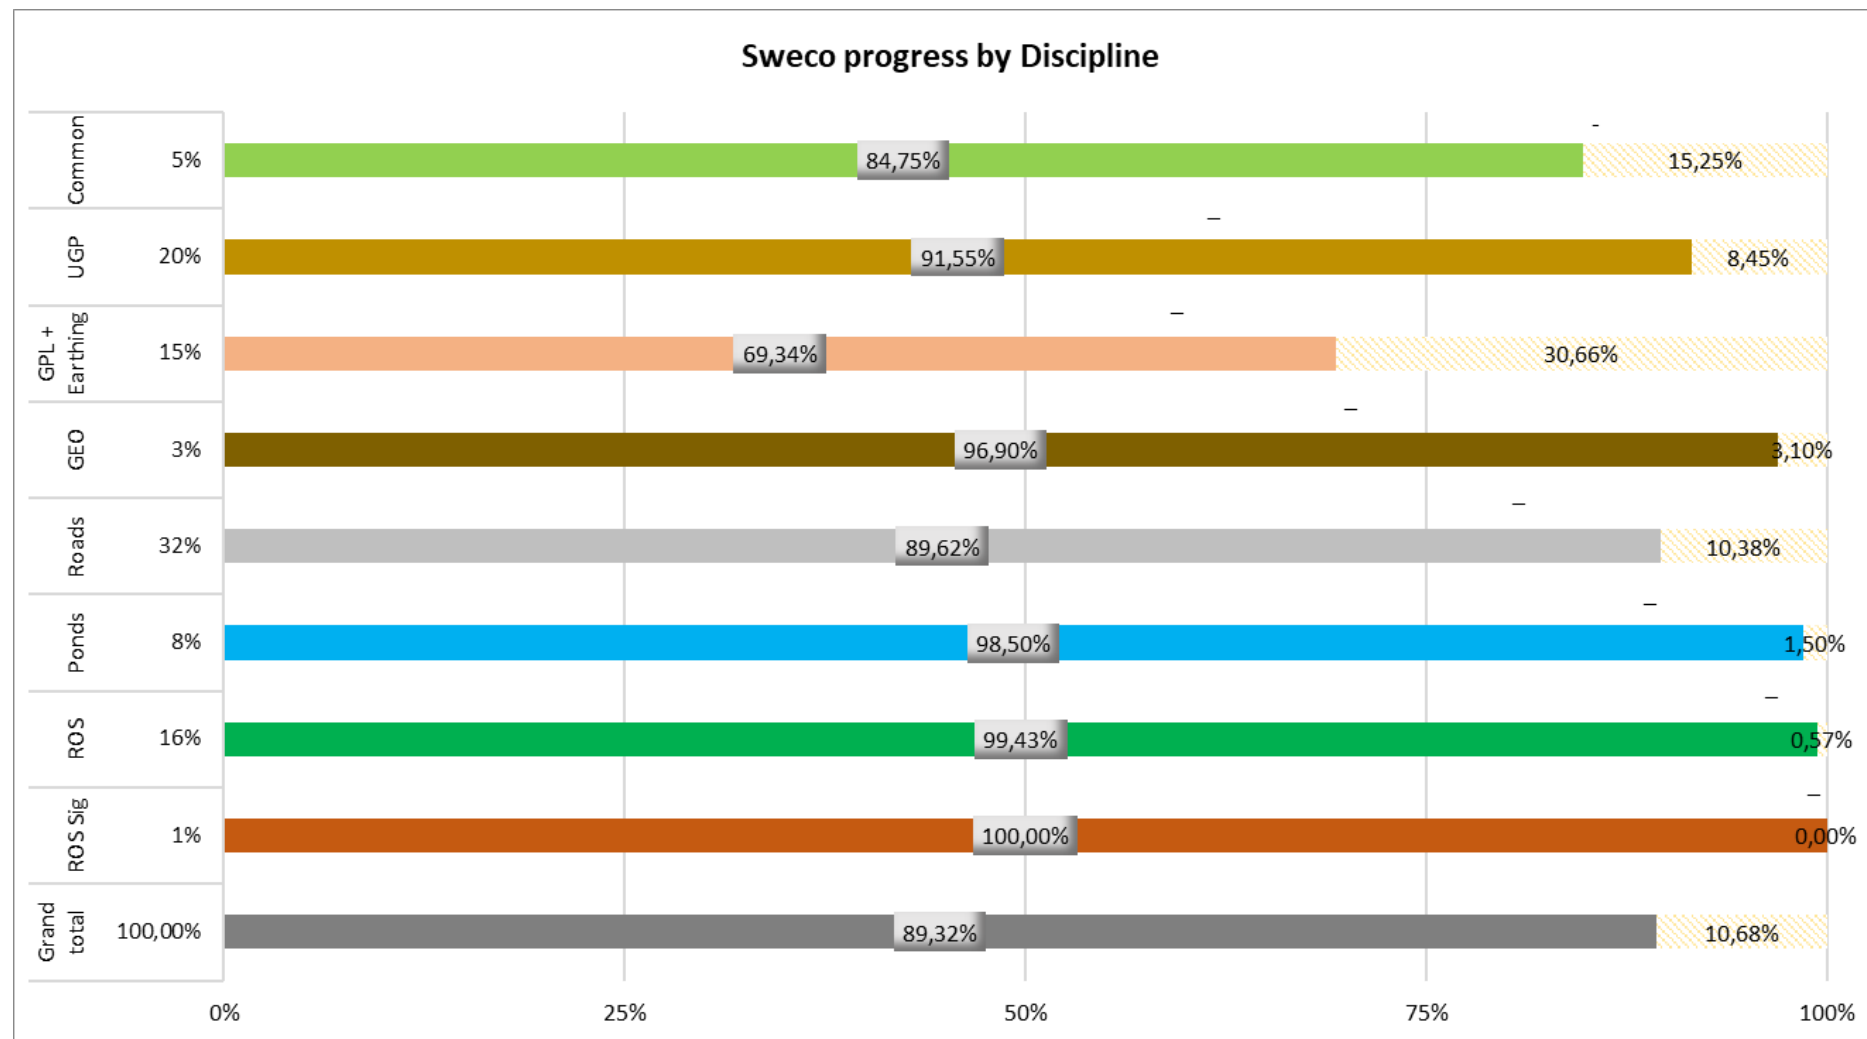

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
 ■ Behind


BOP | Sweco UGP Construction Readiness

Sweco UGP

Sweco							
Phase	Package	Construction Sta	Construction En	IFR	IFC	BoQ	Comments
1	Road 7.1 (Priority 1)	abr-26	ago-26	-	23/01/2026	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Av. 9.5 (Priority 1)	abr-26	jul-26	-	21/01/2025	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 7.5 + Road 9 (Priority 5)	abr-26	jul-26	-	10/12/2025	14/11/2025	- There is an area on-hold for the pipes going into STM cold mill and the railway area (BOD-SIN-UPB-CIV-DRWGA-00015) - Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 6.2	abr-26	jul-26	-	11/02/2026	17/04/2026	Package 2 BoQ is already available in IFC (Dedicated BoQ for Road 6 delivery date is indicated)
1	RW+FW tanks area + Road 8	abr-26	ago-26	-	23/01/2025	18/03/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Scrap road 1	abr-26	ago-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Av. 9.3-9.4 + Av. 6.0	may-26	-	21/01/2026	12/05/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due clashes with McDermott in Av. 9.3 (BOD-SIN-UPB-CIV-DRWGA-00023 + BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 (Av. 6 not included)
2	Road 5.1	jul-26	oct-26	-	05/12/2025	26/03/2026	- Area on-hold due to missing TOPs to NPB207 (BOD-SIN-UPB-CIV-DRWGA-00022) - Package 5.1 BoQ includes all of Road 5 (no dedicated BoQ for Road 5.1)
2	Av. 9.1-9.2	jul-26	mar-27	16/12/2026	08/07/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due to the slope designed in Av. 9.1 (east of DRP) (BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4
2	ELA01 & PDOP	jul-26	oct-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
2	Parking 1 area	jul-26	oct-26	23/01/2026	29/05/2026	08/07/2026	- IFC drawings in Omega are available, however there will be a new revision due to UGP being on-hold in this area (BOD-SIN-UPB-CIV-DRWGA-00017 + BOD-SIN-UPB-CIV-DRWGA-00013) - Package 0 (no dedicated BoQ for UGP in Parking 1). BoQ available is in IFR from 30/09/2025
4	Road 4 + Av. 2.0	abr-27	oct-27	11/07/2025	30/08/2026	30/08/2026	Drawings in Omega are IFC but there will be an additional revision due to multiple adjustments (TOP changes, etc.)
4	Av. 6	abr-27	oct-27	25/03/2026	12/05/2026	08/05/2026	
4	Av. 5	abr-27	oct-27	11/02/2025	01/04/2026	20/05/2026	Drawings are IFC in Omega, however there will be another revision due to TOP & design changes due to McD STM
4	Av. 4.1	abr-27	ago-27	-	11/02/2026	27/05/2026	
4	Av. 3.4	abr-27	ago-27	-	11/02/2026	03/06/2026	
4	Av. 3.2 + 3.3 + Road 5.3	abr-27	ago-27	-	11/02/2026	02/04/2026	

BOP | Procurement

Progress

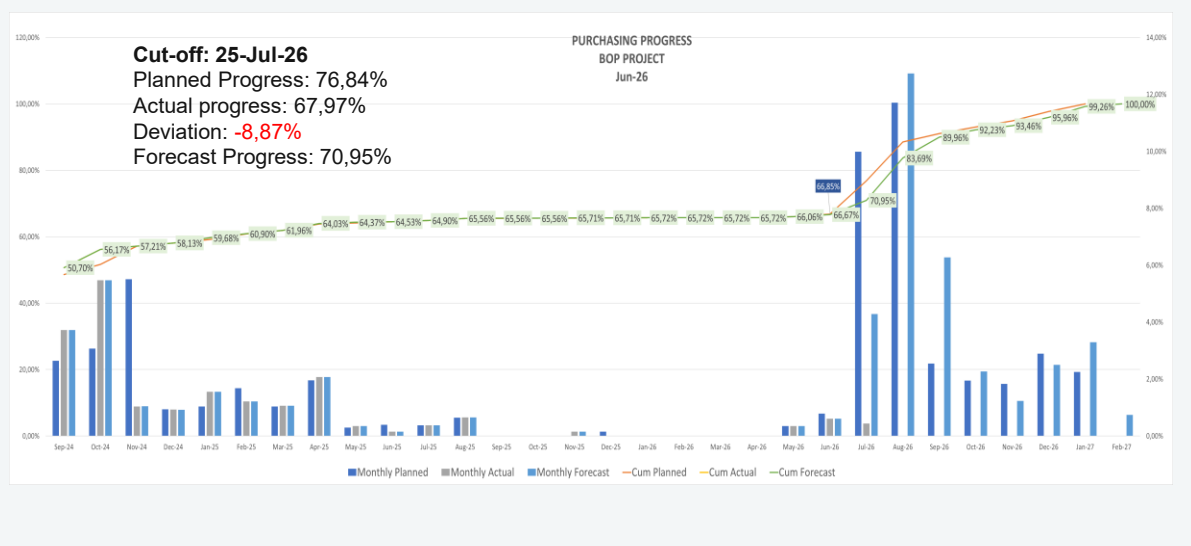

Plan deviations

RED Activity	Plan date	Fcst date	CP impact?	Mitigating action	Who	When
RW + FFPS steel struct. and cladding (ROS)	05/02/26	08/07/26	Y	LNTP: Confirmed by KSH Contract: Approved by both parties Approval of TG4 by PGB w19, contract to be signed w21.	Stegra	TBC
M&P Contractor (ROS)	19/12/25	13/09/26	Y	Awaiting NIWA's confirmation or comments on the proposed schedule. IDOM has also shared with NIWA the list of deliverables regarding pre-commissioning, cold and hot commissioning. TG4 PGB approval for w21.	Stegra IDOM	TBC
E&I Contractor (ROS)	19/12/25	28/08/26	Y	Initially, the plan was for the works to begin in June; however, since the approval process for TG4 may take approximately six weeks (GPB), it has been postponed to late June or early July. TG4 will be issued on W16. LOI approved(PGB) w19 and to be shared with STS w20.	Stegra	TBC

Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
Packages that will be proposed by Stegra-BOP as critical for ramp up (PGB):	- E&I - STS to submit the final version of A5 and A7, and IDOM final version of A1, all the contract documents to be shared in W26. - UG Piping Av. 9&6: Nordic to submit the last version of A7 and Nordic and Stegra to confirm all the contract documentation already shared by IDOM. - M&P Package – Contract signed. - RW&FF SS: Contract signed.				

BOP | Procurement (IDOM)

Main Packages Status

PACKAGE NUMBER	ITEMS	NEXT TG	TG FORECAST	Expected value MMEUR	TG4 forecast date	Contract signing forecast date	Forecast Arrival on Site
							(ROS forecast)
BOD-BOP-019EA	Underground Services & Roads Avenue 9.1, 2,3,4 Road 4	TG4	20/05/2026	35.9	20/05/2026	30/06/2026	01/07/2026
MISC	Remaining Civil Works	TG3	19/06/2026		10/07/2026	30/07/2026	30/08/2026
BOD-BOP-027C	HVAC engineering for BOP	TG5	22/05/2026	0.2	Approved 05/05/2026	15/05/2026	13/08/2026
	Engineering as priority						
BOD-BOP-020A	M&P Contractor	TG4	21/04/2026	4.3	21/04/2026	Signed 23/06/2026	30/08/2026 TBC
		(NIWA)					
BOD-BOP-020C	E&I Contractor	TG4	15/04/2026	32.7	15/04/2026	03/07/2026	06/07/2026
		(STS)					
BOD-BOP-051B	RW and FFPS Steel structure and Cladding	TG4	30/03/2026	0.9	Approved 11/05/2026	Signed 23/06/2026	15/08/2026
		(KSH)					
BOD-BOP-043	MHS for Slag and DRP by-products	TG3	29/05/2026	13.9	23/06/2026	14/07/2026 TBC	01/12/2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Pipe Bridge Manufacturing Progress - Ferrmix


Week 30 2026

PROJECT PHASE		Priority	P1		P2		P3		P4		P5	
			Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total	Completed Cummulative	Total
Steps												
Steel Structure	Assembled column		45	45	11	11	64	64	20	20	6	6
	Assembled modules		67	67	10	10	59	59	37	37	8	8
	Painted Columns		45	45	11	11	64	64	20	20	6	6
	Painted modules		67	67	10	10	59	59	37	37	8	8
Piping	Modules with pipe inside		45	45	10	10	59	59	18	20	8	8
Heat tracing	Modules with tracing		45	45	10	10	59	59	18	20	8	8

ERECTION STEEL STRUCTURE	TOTAL unit	ERECTED	REMAINING
Columns			
PB01	45	45	0
PB02	11	8	3
PB03	64	63	1
PB04	20	9	11
PB05	6	6	0
Modules			
PB01	67	67	0
PB02	10	9	1
PB03	59	57	2
PB04	37	16	21
PB05	8	8	0

BOP | Pipe Bridge General Comments - Ferrmix

Weekly Welding by Welders

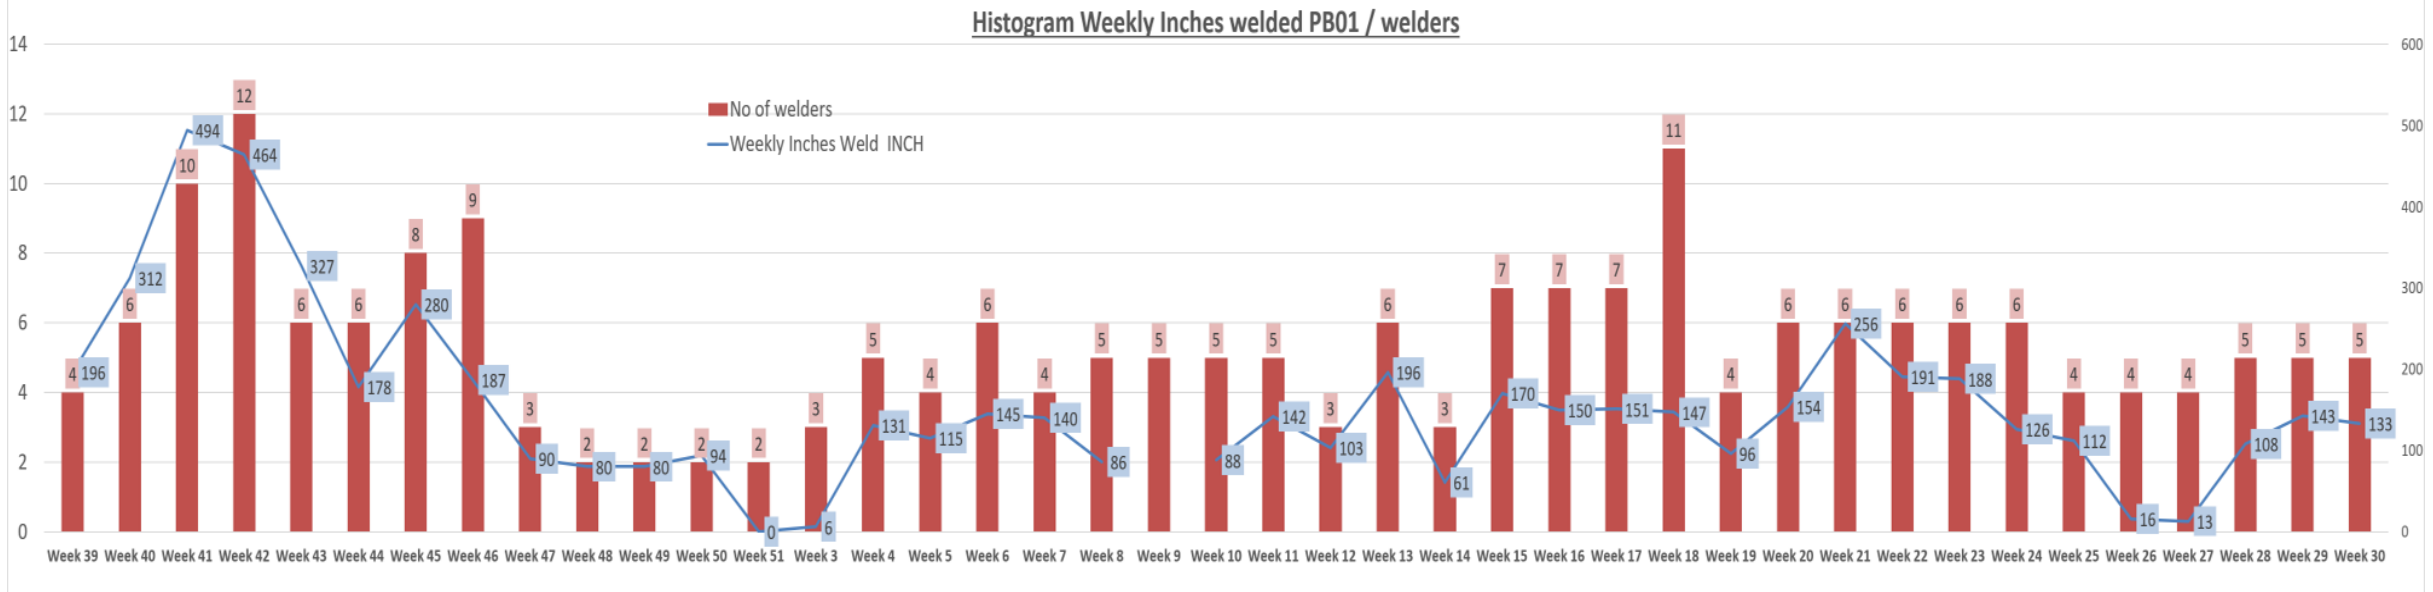


Status Piping Welding by Priorities

SUM % PROG.	Total Inch Field	Accum. Welded Field	% Prog. Welded Field	Total Inch Shop	Accum. Welded Shop	% Prog. Welded Shop	Total Inch F+S	Total Welded F+S	Total Weld %
P1	9.999	8.484	85%	12.696	12.696	100%	22.694	20.778	92%
P2	1.504	1.087	72%	3.851	3.783	98%	5.355	4.643	87%
P3	4.708	2.539	54%	13.198	13.158	100%	17.905	14.888	83%
P4	2.353	1.928	82%	3.528	3.528	100%	5.881	5.146	88%
P4.a	1.532	-	0%	4.021	3.991	99%	5.553	3.991	72%
P5	746	142	19%	1.596	1.473	92%	2.342	1.583	68%
	20.841	14.180	68%	38.888	38.627	99%	59.729	51.028	85%

BOP | Construction

Progress

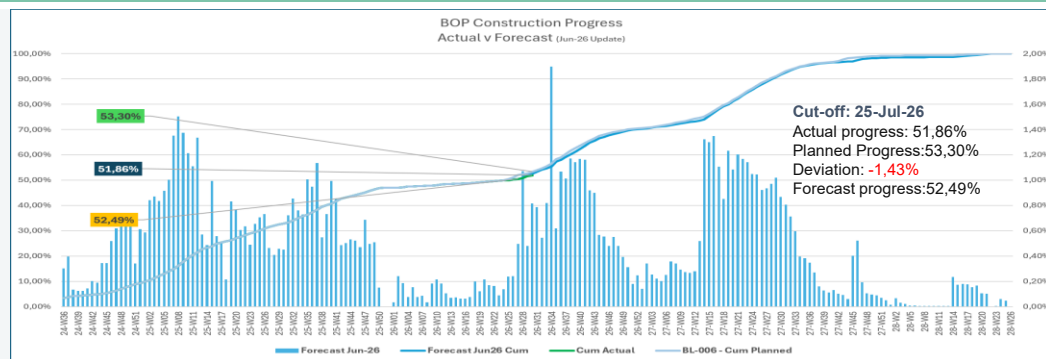

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Con	PB- Piping connections + pending fittings	- WK30 – Average 15 Welders, Ferrmix forecast 660 inches/week vs Actual 535 inches/week - PB01 Welding productivity: 220 inches /week - PB02 Welding productivity: 88 inches /week - PB03 Welding productivity: 264 inches /week - PB04 Welding productivity: 88 inches /week - PB05 Welding productivity: 0 inches /week
Con	PB05 foundation for support pipes	McDermott to execute the piping in that area asap/ Contract with the new civil contractor is to be signed.
Con	SIEMENS: Delay to finalising NPB511 punch items	Siemens mobilization to site (expect WK33). 1 week is needed to close punches
Con	PB02. Foundation not possible due to works by Mc Dermott	McDermott piping pending. Focus on other areas. / Contract with the new civil contractor is to be signed.
Con	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	Confirmation from Stegra to proceed with execution / Contract with the new civil contractor is to be signed.
Con	PB04. Foundation & Erection SS (columns and modules) PB-04, due to constructability priorities of CAS/SMPT by Mc Dermott.	Agreement reached to execute foundation. Steel structure installation pending for permission
Con	Actemium: Delay PB and NPB511 UG earthing completion.	Pending contractual agreement Stegra/Actemium

Plan

Activity	Plan date	Fcst date	CP impact?	Mitigating action	Who	When
LNG Civils works complete (remaining works)	W32 26	WK41 26	Y	Interface management	IDOM	WK32 26
Commence FF Pumping station civil works (after piping installation)	W38 26	WK38 26	Y	Interface management	IDOM	WK32 26
Commence RW Pumping station building erection	W37 26	WK37 26	Y	Interface management	IDOM	WK32 26
PB1 connections complete	W51	WK35 26	Y	Ferrmix confirms more welders: 20 welders	FER	WK35 26
Start Electrical Works (PDOP area)	WK 28 26	WK28 26	Y	Start electrical works PDOP	STS	WK 31 26

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue Risk / Concern
 Behind

Planned vs. Actual Week 30 2026


Weight	Activity	Cum Actual	Actual W30	Planned W30 (BL CCE06 TBA)	Forecast W30	Dev. Forecast Vs Actual	Dev. Planned Vs Actual	Forecast W31	Forecast W32	Forecast W33	Forecast W34	Forecast W35	Forecast W36	Deviation (Against Forecast)	Mitigation Actions
6,83%	Raw Water & FF Pumping Stations	74,65%	0,01%	0,00%	0,00%	0,01%	0,01%	0,35%	0,00%	0,27%	0,27%	0,27%	0,39%		
0,25%	Compressed Air Plant NPB-422	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
6,02%	LNG Terminal / Regasification Unit	87,02%	0,60%	1,97%	1,00%	-0,40%	-1,37%	1,00%	1,00%	0,85%	2,62%	1,46%	0,36%	1. Delay in electrical work for cable pulling 2. Delivery delay MV Transformer 3. Delivery delay Control units	1. Chart is recovering the delay 2. MV Transformer Expected delivery 02 Oct 2026. 3. Control units ETA W35
5,11%	PDOP Civil	92,82%	0,09%	0,96%	0,00%	0,09%	-0,87%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
1,76%	Power Distribution 51x	84,69%	0,00%	0,00%	0,00%	0,00%	0,00%	3,06%	3,06%	3,06%	3,06%	3,06%	0,00%		
8,07%	NPB-200 Series	55,95%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,35%	0,58%		
1,00%	NPB-102 Safety & Security Building	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
17,84%	Pipe & Cable Racks	84,34%	0,51%	0,42%	0,52%	-0,01%	0,09%	0,50%	0,59%	0,81%	1,70%	2,07%	0,89%		
21,06%	Underground Networks	17,55%	0,24%	1,36%	1,26%	-1,02%	-1,12%	1,21%	1,05%	1,06%	1,04%	1,09%	1,00%	1. RW/FF area: UG piping installation activities are underperforming 2. Completion of the Priority 0 RW chamber remains outstanding 3. Pressure testing for Priority 1 and Priority 3 systems has not yet commenced 4. The start of AV9.4 activities is delayed by two weeks	1. GRK will send a recovery schedule 2. GRK will finalize in the coming weeks 3. Test pack to be submitted 4. Av9.4 Excavation will start in week 32
9,61%	RailWay Package	33,70%	0,00%	0,37%	0,11%	-0,11%	-0,37%	2,84%	2,97%	0,27%	0,42%	0,26%	1,41%	Delay to start the works civil contractor	Expedite to start works
22,45%	Overall Construction Sweco Scope: Ponds, Roads & Temporary Power - Water	34,18%	1,04%	0,16%	0,23%	0,81%	0,87%	0,27%	0,27%	0,12%	0,12%	4,82%	0,09%	1. Completion of Mechanical completion of Temporary Power and TWTP 2. Completion of Mechanical completion of Temporary TWTP 3 UG network RWFF piping testing	1. Completion of Testing Cables, testing earthing works by Ferrmix and Actemium, Siemens needs to close the Punches opens B. 2. Close commercial/ contracting CR. 3 Expedite perform the RWFF piping testing.
100,00%	Total	50,74%	0,42%	0,60%	0,48%	-0,06%	-0,18%	0,82%	0,79%	0,54%	0,82%	1,90%	0,62%		

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP | Railways Management (IDOM PCM – SWECO - GRK)

Progress Status

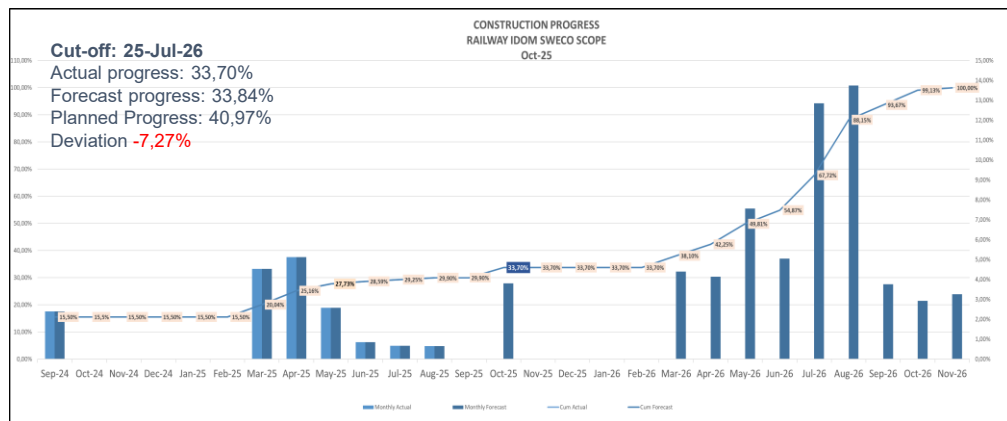

1+6 activities

Week 31 – Mobilisation to site. Start drainage piping installation under the rail and UG piping crossing. DRP need to start removing pipe material of section 3

Week 32 - Continue drainage piping installation under the rail and UG piping crossing

Week 33 - Continue drainage piping installation under the rail and UG piping crossing

Week 34 - Continue drainage piping installation under the rail and UG piping crossing

Week 35 - Continue drainage piping installation under the rail and UG piping crossing

Week 36 - Continue drainage piping installation under the rail and UG piping crossing

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
CON	Section 3 Interference with Hydrogen pipe	Expected IFC drawing for culvert end of September 26 (SWECO)
CON	New pile deck in Scope of McDermott not interfere with railway truck, but interfere with the pressure bern, east ditch and service road	Alternative 3 Hydrogen pipeline
CON	Scrap Yard micropilling Desing End of May (Done). Micropilling to be done by McDermott	Only for railway truck. East ditch and service road on the limit boundary can start
CON	Activities planned to restart in Week 30 (Drainage piping)	Pending CO for East ditch

TOTAL RAILWAY	Unit	Total	Weight %	Contractor	Actual Progress	Category	WK30	WK31	WK32	WK33	WK34	WK35	WK36
Underbelt Layer (Rein.) DCH. 15	m3	72973	20%	GRK	31%	Period Forecast	9177	2955	10542	10542	8669	0	0
						Period Actual	0	0	0	0	0	0	0
Underballest Layer (Frost) DCH. 16	m3	118902	20%	GRK	30%	Period Forecast	3609	5390	14408	5605	0	13428	13428
						Period Actual	0	0	0	0	0	0	0
Catenary Poles/ Struts	ea	199	5%	GRK	33%	Period Forecast	12	0	20	12	16	0	0
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballast track	m	9602	15%	GRK	40%	Period Forecast	0	384	383	184	184	184	184
						Period Actual	0	0	0	0	0	0	0
Supplementation of ballast layer	m3	30296	15%	GRK	40%	Period Forecast	559	0	700	900	869	2250	2912
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballasttles track	m	4403	5%	GRK	3%	Period Forecast	0	184	184	184	184	184	184
						Period Actual	0	0	0	0	0	0	0
Switches	ea	18	5%	GRK	39%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0
Hanging Works	ea	22	15%	GRK	27%	Period Forecast	0	0	3	0	0	1	1
						Period Actual	0	0	0	0	0	0	0
Concrete Channel Section 7 - Track 1	m	1000	1%	GRK	100%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Longitudinal drainage SSY (start)	10 Nov 2025	30 Aug 2026
Ballast & sub-ballast SSY (Start)	17 Nov 2025	17 Aug 2026
Trench excavation Track 1 – Section 6	28 Nov 2025	17 Aug 2026
North Railway - Section 7 – Ready for commissioning	29 May 2026	30 Sep 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Roads & Ditches Management (IDOM EPCM – SWECO – GRK)

Progress Status

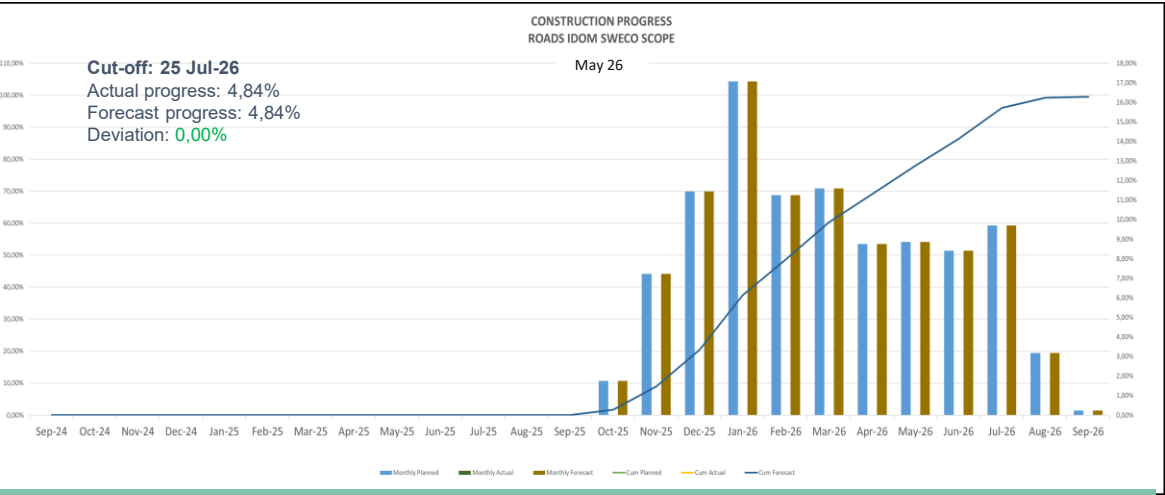

1+6 activities

- Week 31 - Activities on hold.
- Week 32 - Activities on hold.
- Week 33 – Activities on hold.
- Week 34 – Start backfilling road 6 and ave. 9.5.
- Week 35 – Continued backfilling road 6 and ave. 9.5.
- Week 36 – Continued backfilling road 6 and ave. 9.5

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action

Avenue/Roads	Activity name	Weight %	Weight % on Total	Progress	Category	WK30	WK31	WK32	WK33	WK34	WK35	WK36
						25/07/26	01/08/26	08/08/26	15/08/26	22/08/26	29/08/26	05/09/26
Av 1	Avenue 1	100%	5%	34%	% Cum Planned	34%	34%	34%	34%	34%	34%	34%
					% Cum Forecast	34%	34%	34%	34%	34%	34%	34%
					% Cum Actual	34%	34%	34%	34%	34%	34%	34%
Av 1	Roads - Avenue 1 - Clearing and levelling ground	23%		100%	Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	1	1	1	1	1	1	1
					% Cum Forecast	100%	100%	100%	100%	100%	100%	100%
					Period Actual							
					Cum Actual	1	1	1	1	1	1	1
Av 1	Roads - Avenue 1 - Laying of sub-base and base layers 1.1 & 1.2	10%		100%	% Cum Actual	100%	100%	100%	100%	100%	100%	100%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	18279	18279	18279	18279	18279	18279	18279
					% Cum Forecast	100%	100%	100%	100%	100%	100%	100%
					Period Actual							
Av 1	Roads - Avenue 1 - Laying of sub-base and base layers 1.3	6%		0%	Cum Actual	18279	18279	18279	18279	18279	18279	18279
					% Cum Actual	100%	100%	100%	100%	100%	100%	100%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	0	0	0	0	0	0	0
					% Cum Forecast	0%	0%	0%	0%	0%	0%	0%
Av 1	Roads - Avenue 1 - Application of wearing course (asphalt)	15%		0%	Period Actual							
					Cum Actual	0	0	0	0	0	0	0
					% Cum Actual	0%	0%	0%	0%	0%	0%	0%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	0	0	0	0	0	0	0

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Start sub-base laying Avenue 9.5	28 Sep 2026	19 Mar 2027
Start Road Ave 1 Laying subbase	20 Jul 2026	07 Aug 2026
Start sub-base laying Road 6	13 Jul 2026	14 Aug 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
Behind

BOP | Ponds Management (IDOM EPCM – SWECO – GRK)

Progress Status

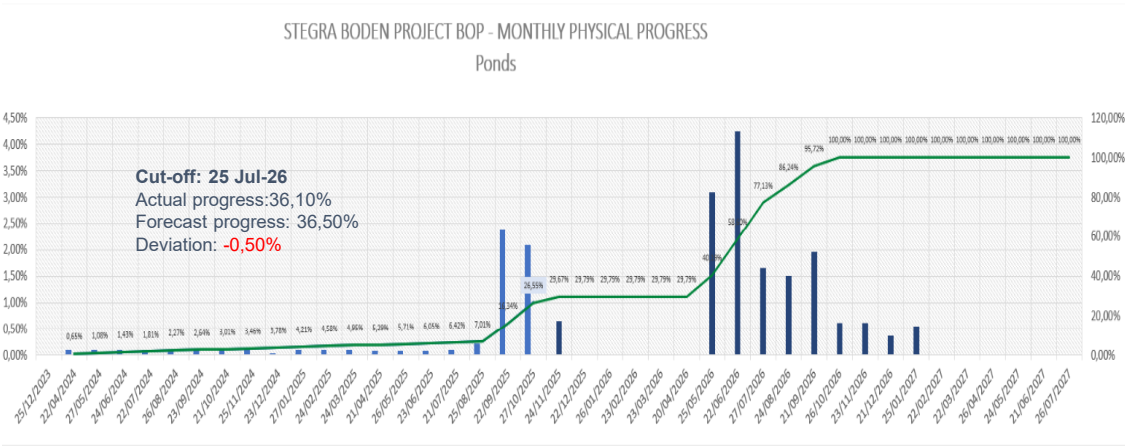

1+6 activities

- Week 30 - Completed excavation east ponds. **100% progress achieved**. Started excavation contact water pond. **15% progress achieved**
- Week 31 - Continue excavation East ponds. West pond 1 erosion protection cover installation. West Pond to be performed geomembrane test
- Week 32 - Continue excavation East ponds and Start excavation Contact water pond. West pond 1 erosion protection cover installation
- Week 33 - Continue excavation East ponds and Contact water pond
- Week 34- Continue excavation East ponds and Contact water pond
- Week 35- Continue excavation East ponds and Contact water pond
- Week 36- Continue excavation East ponds and Contact water pond

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
PRC	Remaining works for West pond 3 completion (CR pending)	IDOM, GRK and Stegra to expedite process
QAQC	ITP for West ponds pending revision by IDOM/Stegra. Works on hold. Pending geomembrane testing sub-contractor award	GRK to award sub-contractor for test

WORK AREA	ACTIVITY	STATUS	Qty. Accum.	% Accum.	30	W31	W32	W33	W34	W35	W36	Design	Procurement	Construction	Commissioning	Handover	Closeout
WEST PONDS	Filling erosion cover (m3)	FC	7.300					2.433	2.433	2.434							
	Complete the North dam pocket 2 (m3)	FC															
	gravity pipeline IN FACILITY (lm)	FC	160														
EAST PONDS	Excavation (m3)	FC	31.000		1.950	1.950	3.450	3.450	8.550	8.550	8.550						
		Actual	31.000	100%	6.000												
	Filling Moraine (m3)	FC	15.230							2.965	2.965						
		Actual	-	0%													
	Geotextile Protective Layer (m2)	FC	27.100														
		Actual	-	0%													
	Geomembrane double-sided textured (m2)	FC	27.100														
		Actual	-	0%													
	Filling erosion cover (m3)	FC	58.590														
		Actual		0%													
CONTACT WATER POND	gravity pipeline IN FACILITY (lm)	FC	581														
		Actual		0%													
	Embedded Pipes(lm)	FC	18														
		Actual		0%													
	Valve 1200 (st)	FC	11														
		Actual		0%													
	Unstressed reinforcement in concrete structures (kg)	FC	3.235														
		Actual		0%													
	EBE Concrete Castings (m3)	FC	40														
		Actual		0%													
CONTACT WATER POND	Excavation (m3)	FC	40.700		5.100	5.100	5.100	5.100	5.100	5.100	5.100						
		Actual	6.000	15%	6.000												
	Filling Moraine (m3)	FC	29.931														
		Actual		0%													
	Geotextile Protective Layer (m2)	FC	43.350														
		Actual		0%													
CONTACT WATER POND	Geomembrane double-sided textured (m2)	FC	43.350														
		Actual		0%													
	Erosion protection cover (m3)	FC	30.195														
		Actual		0%													

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Completion West Pond 1	30 Jun 2026	14 Aug 2026
Completion West Pond 3	30 Jun 2026	14 Aug 2026

Achievement Actual / Plan OR Forecast / Plan as percentage


On track / no issue Risk / Concern
Behind

Construction Manpower & Histogram for ongoing activities

Week 30 2026	GRK	ANFRA	ACTEMIUM	FERRMIX	CHART	SIEMENS	FORSSA	LBS	PROXA	KSH	STS	NORDIC
	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual
LNG	0				7					0		6
RAIL												
PONDS	6											
RW AREA	0						0					8
UGP RW AREA	6											
UGP0 (Ave 1 & Ave 2)	0											
UGP1 (Road 7 Ave 9.5)	5											
UGP3 (Road 6)	10											
UGP4 (Ave 9)	0											10
PDOP		6										
100 MW CABLE PULL (OFFSITE)			0									
100 MW CIVILS	0											
PB FOUNDATIONS	0											
PB ERECTION & FITUP				56								
TEMPORARY POWER ONSITE			0					0				
515	0					0						
511					0							
TEMPORARY PIPE BYPASS	0											
EARTHING WORKS	0											
Roads	0											
TWTP - Mechanical	0								1			
TWTP - Electrical											10	
TOTALS	27	6	0	56	7	0	0	0	1	0	10	24
BLTotal	60	0	0	65	30	0	0	0	0	0	29	100
Actual Week Average	131											
BL Week Average	285											
Forecast Average	285											

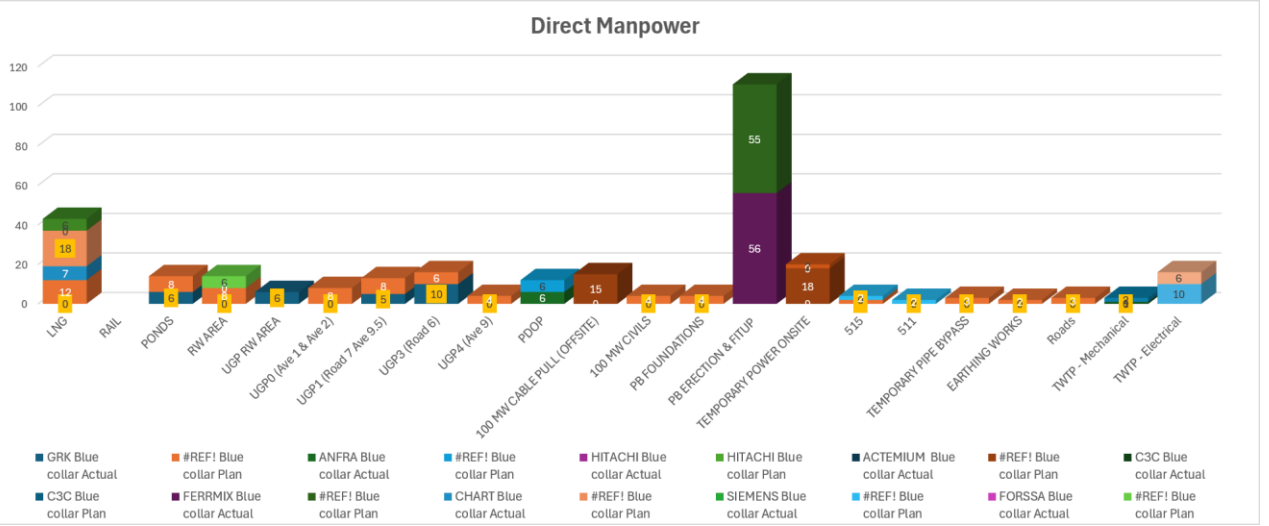

MANPOWER BOP - CONSTRUCTION PHASE
(MH / 225 Hours x Month)
Forecast / BL CCE06

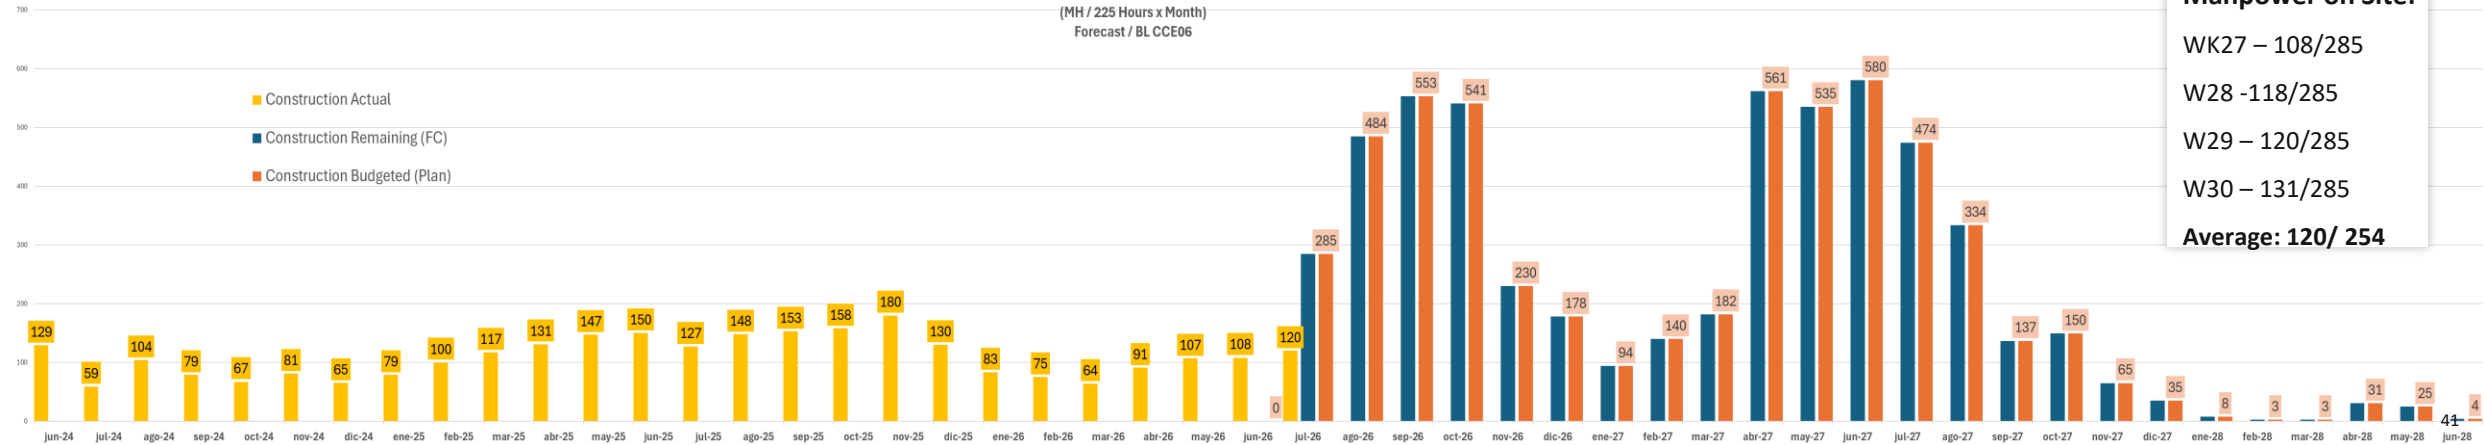

Manpower on Site:

WK27 – 108/285

W28 -118/285

W29 – 120/285

W30 – 131/285

Average: 120/ 254


Actions						
Sub-Area	Key issue / potential risk	Due Date	Owner	Description	Potential Impact	Mitigation
PB02	Erection of bridge & reinstall foundation PB02 to WTP1 blocked by Mc Dermott and Stegra	w42_25	STEGRA/ Mc Dermott	No access permission.	Delay to construction (pipes test)	Confirmation from stegra to proceed with erection
PB03	PB03. Foundation in the WTP2 area no possible to works by Mc Dermott	w45_25	STEGRA/ Mc Dermott	No access permission.	Delay to construction	Mc Dermott to be confirmed date to release the area
PB04	PB04: Foundation & Erection SS (columns and modules), due to constructability priorities of CAS/SMPT by Mc Dermott.	w36_25	STEGRA/ Mc Dermott	No access permission.	PB04 not ready as scheduled.	Agreement reached to execute foundation. Steel structure installation pending for permission.
Pipe Bridges	Pipebridge Piping Connections + Pending Fittings	w25_25	IDOM/STEGRA/FERR MIX	Lack of welding Resources and low productivity	Delay in connections and pending fittings	WK27 – Average 19 Welders, Ferrmix actual 793 inches/week
Rail	Unloading Station Tunnel (Section 2)	w35_26	IDOM DRP	Track 1 execution restricted for Tunnel	Construction delay	Review status weekly to make sure Tunnel is delivered on schedule. DRP confirmed August 24, 2026 as the completion date.
Rail	Road 2 retaining wall (Section 2)	w30_26	IDOM BOP / GRK	Track 1 execution restricted for retaining wall	Construction delay	Review weekly status to ensure the retaining wall is delivered on time w29 - IDOM provided GRK preliminary documentation via email. The documentation will be provided officially once the BoQ for the Rail memo 19 has been priced and comments from IDOM will be included..
Roads/UGP	Road 6.0 as laydown area for UGP	w34_26	IDOM BOP	Road 6.0 to be used as laydown area for execution of Road 6.1 and Road 6.2 UGP	Construction delay	w29 - CR has been executed by Stegra but works will start in approx w33-w35
Rail	Transversal and longitudinal drainage interface with loading station	w30_26	IDOM BOP/DRP	Interface between the loading station and the transversal and longitudinal drainage.	Construction delay	w28 - Stegra identified potential issues with IDOM's proposed solution and will coordinate with IDOM site team to optimize the solution. w29 - Stegra requested elevations for the modifications implemented to the transversal and longitudinal drainge. IDOM is checking internally and will revert.
Rail/Roads	Clash with existing power supply at Section 5 Rail	w30_26	IDOM BOP / Stegra SS	Existing power supply to plant crosses eastern ditch and rail at Section 5. Until a solution if proposed, rail groundworks cannot start.	Construction delay , redesign may be required.	w28 - Stegra provided the theoretical levels and IDOM has reviewed them. IDOM construction team to establish a protocol to confirm they can proceed with the excavations. w29 - IDOM safety to coordinate with GRK such that a protocol is established to confirm they can proceed with the excavations in the RAMS.
UGP	Work suspended - Preparation for Priority 1 piping tests Blocked	w30_26	IDOM BOP / Stegra	Work suspended - Preparation for Priority 1 piping tests	Construction delay	WK29 - Expedite agreement between STEGRA/GRK/IDOM
Pipe Bridges	Piping test are blocked for commercial issues	w30_26	IDOM BOP / Stegra	Work suspended - PB01 piping tests	Construction delay	WK29 - Expedite agreement between STEGRA/Ferrmix/IDOM
Ponds	East pond groundworks execution is blocked.	w30_26	IDOM BOP	East pond groundworks execution is blocked. IDOM to provide GRK a plan drawing indicating the areas where sulphides are present as well as approximate depth.	Consutrction delay	w29 - IDOM to provide GRK with a plan drawing indicating the locations where sulphites are present, also indicating the depth. IDOM to collaborate with GRK to perform tests on-site to identify the information required to prepare the plan drawing.
Ponds	West Pond 2 cannot be finished until the northern area is handed back by DRP.	w33_26	IDOM BOP/DRP	In 2025, DRP took over the northern wall area to use it as a laydown area. This area must be handed back to BOP in order to allow the raising of the northern wall and the completion of West Pond 2.	Construction delay	w28 - IDOM BOP meeting with IDOM DRP has been postponed to w29 w29 - IDOM BOP and IDOM DRP are still coordinating on when the handover will take place.
Temp Power	Actemium: Delay PB and NPB511 UG earthing completion	WK25_26	IDOM/STEGRA	Actemium: Delay PB and NPB511 UG earthing completion	Delay to energization	Pending contractual aggrement STEGRA/ACTEMIUM
Roads	Boden Energy switch houses	w38_26	Stegra SS	Switch houses are located at the same location than the service road over the East ditch. It is necessary either to remove the houses or to divert the road	Construction delay , redesign may be required.	w28 - Current plan is to execute the service road until the switch houses. w29 - IDOM to review the constructability for the ditch in this area and revert with feedback.

BOP | Construction Pictures - Pipe Bridge

- Piping welding works (all priorities) 535 Inches welded



PB03 Zone 1

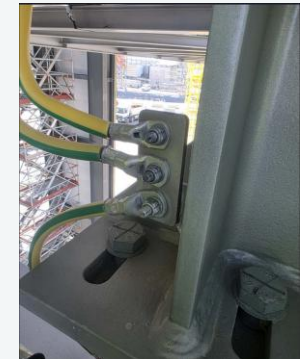

PB earthing connection

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - UG piping

- RW/FF area: UG piping works ongoing
- Road 6 Piping installation ongoing
- Scrap road 1 bedding ongoing



RW FF Area



Scrap road 1



Road 6

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - LNG Terminal

- Tubing completed
- Cable pulling and connection ongoing



Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - RW+FF Area

- UG piping installation ongoing




Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - PDOP

- Continued bedding in the cable channels
- Started electrical works in GIS and electrical channel between Transformers to GIS.
- Started STACCOM-T1 bedding for cables channels insulation + cables channel installation.

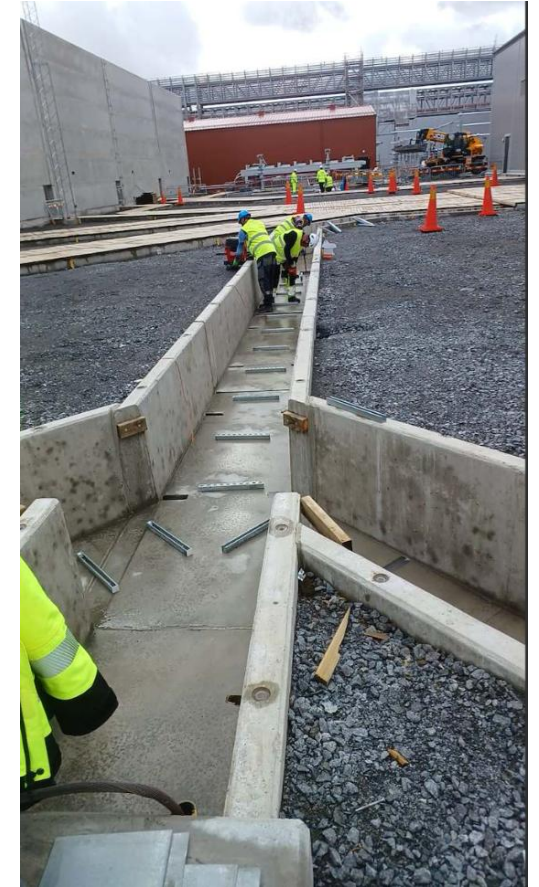

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures – Railways



Section 2 Unloading station



Section 3 Wet land view and
Terrace of Tracks 10, 11 and
12



Section 4A Scrap Yard Area for Track 1 (exterior) and Tracks
101 and 102 (internal)

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures – Ponds

East ponds excavation



East Ponds




Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

Actions

BOP – 6 Week Look Ahead

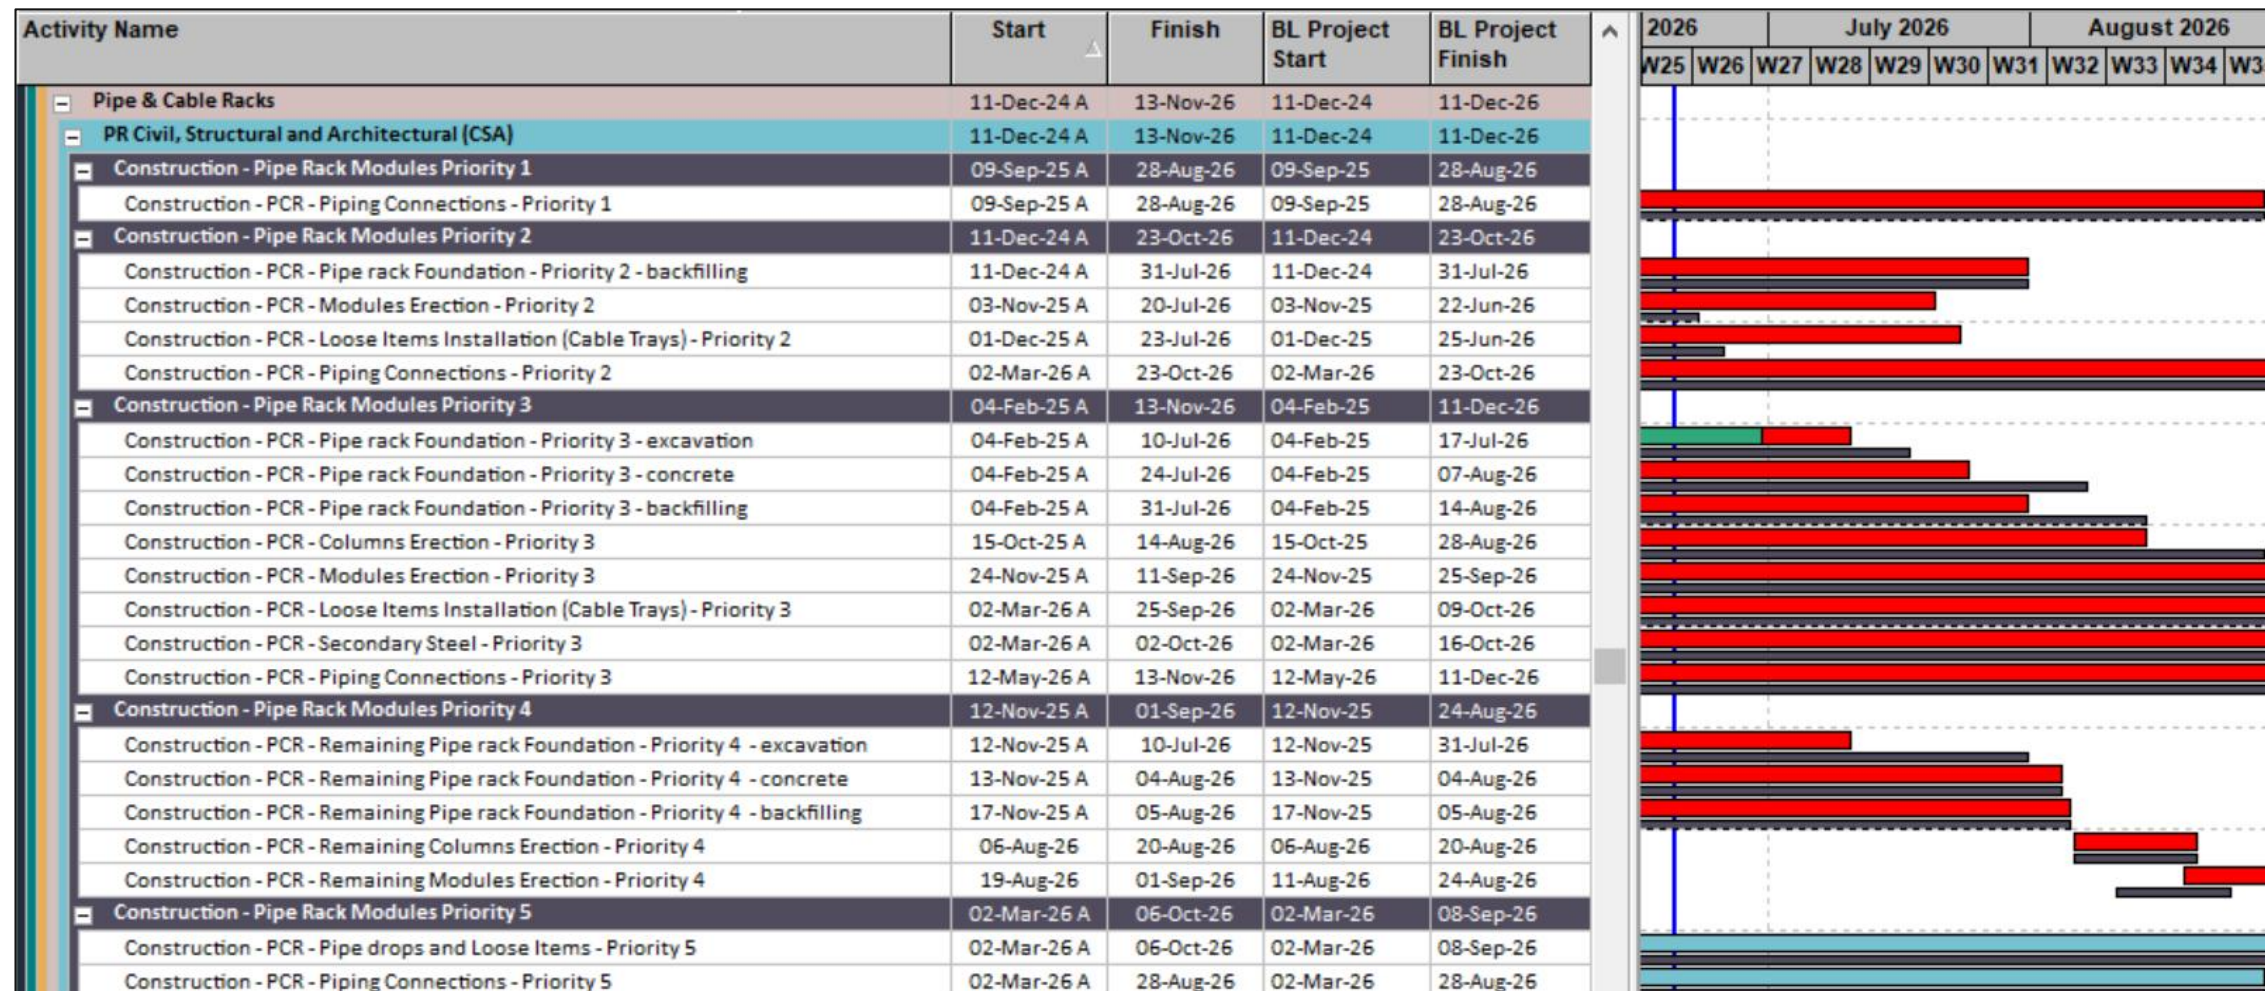

Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish												
					August 2026						September 2026					
					W30	W31	W32	W33	W34	W35	W36	W37	W38	W39	W40	
Temporary Water Supply	07-Sep-26	23-Apr-27	29-Jun-26	20-Jan-27												
Construction - Underground Networks - Route 0 - RW Chamber - Piping Arrangement - Temporal Solution	07-Sep-26	09-Oct-26	29-Jun-26	17-Jul-26												
Construction - Excavation - Inst Contact Water pipe CW - Test backfilling (RW Tank Overflow)	14-Sep-26	16-Oct-26	29-Jun-26	17-Jul-26												
Construction - Temporary Water Supply - TWTP Plant Operative	02-Nov-26	14-Apr-27	03-Aug-26	11-Jan-27												


Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish	August 2026						
					W30	W31	W32	W33	W34	W35	W36
Temporary Power Transformers 2x63 MVA / 100 MW	01-Oct-25 A	19-Aug-26	01-Oct-25	09-Jul-26							
33 kV distribution from ELA to NPB511 and ASP - ON SITE	01-Oct-25 A	07-Aug-26	01-Oct-25	26-Jun-26							
ELA to NPB511 and ASP - Earthing Works - Installation & Connection by Ferrmix	01-Oct-25 A	07-Aug-26	01-Oct-25	26-Jun-26							
Mechanical Completion & PreCom	10-Aug-26	19-Aug-26	29-Jun-26	09-Jul-26							
Pre Commissioning - E-House NPB511 (Temporary Set) for WTP1, ASP, WPS, NPB20x	10-Aug-26	19-Aug-26	29-Jun-26	09-Jul-26							

Actions

BOP – 6 Week Look Ahead

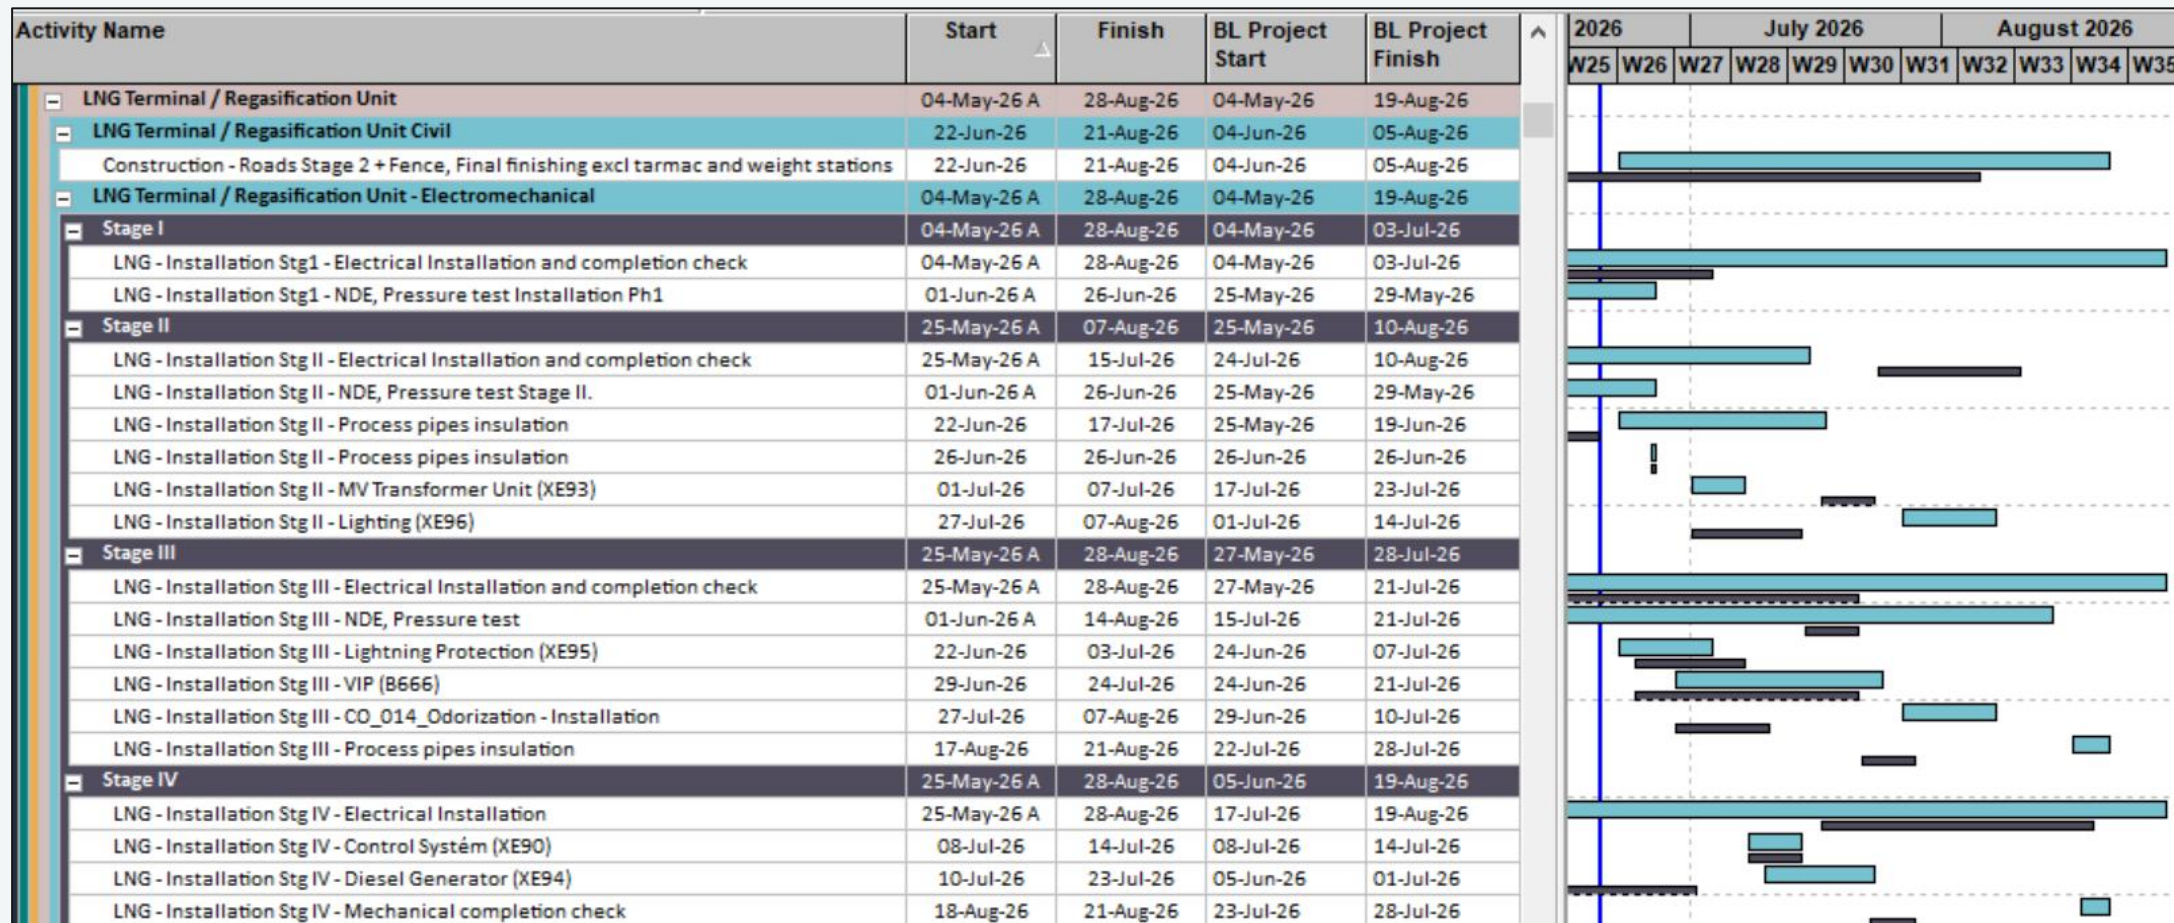

Actions

BOP – 6 Week Look Ahead

Activity Name	Start	Finish	BL Project Start	BL Project Finish	August 2026
					W30 W31 W32 W33 W34 W35 W36
Underground Networks	03-Oct-25 A	23-Oct-26	03-Oct-25	30-Aug-27	
Piping Route 0 to Route 5 & Others Areas UG Networks	03-Oct-25 A	23-Oct-26	03-Oct-25	23-Oct-26	
Underground Piping Route 0 (Av 1.1 - 2.1 to 2.5)	03-Oct-25 A	28-Aug-26	03-Oct-25	26-Jun-26	
Underground Piping Route 0 - Process & SW & CW	03-Oct-25 A	28-Aug-26	03-Oct-25	26-Jun-26	
Underground Networks - Route 0 - Testing (PT,HT,LT etc.)	03-Oct-25 A	28-Aug-26	03-Oct-25	26-Jun-26	
Underground Piping Route 1 (Road 7 + Av 9.5)	27-Jul-26	11-Sep-26	22-Jun-26	31-Jul-26	
Underground Piping Route 1 - Process & SW & CW	27-Jul-26	11-Sep-26	22-Jun-26	31-Jul-26	
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) A (Road 7)	27-Jul-26	07-Aug-26	22-Jun-26	03-Jul-26	
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) B, C, D (Road 7)	31-Aug-26	11-Sep-26	29-Jun-26	10-Jul-26	
Underground Networks - Route 1 - Testing (PT,HT,LT etc.) E, F, G (Av. 9.5)	27-Jul-26	07-Aug-26	20-Jul-26	31-Jul-26	
Underground Piping Route 5 (Road 7.5)	17-Nov-25 A	23-Oct-26	17-Nov-25	23-Oct-26	
Underground Piping Route 5 - Process & SW & CW	17-Nov-25 A	23-Oct-26	17-Nov-25	23-Oct-26	
Underground Networks - Route 5 - trench excavation (BoP and SIN)	17-Nov-25 A	25-Sep-26	17-Nov-25	25-Sep-26	
Underground Networks - Route 5 - Piping Installation & Welding (WFI from P1 to Others Areas - 90 ml)	24-Nov-25 A	09-Oct-26	24-Nov-25	09-Oct-26	
Underground Networks - Route 5 - Backfilling in trenches for underground piping	24-Nov-25 A	23-Oct-26	24-Nov-25	23-Oct-26	
Underground Piping Route 4 (Av 9.4 -9.3 -9.2)	03-Aug-26	09-Oct-26	20-Jul-26	16-Oct-26	
Underground Piping Route 4 - Process & SW & CW	03-Aug-26	09-Oct-26	20-Jul-26	16-Oct-26	
Underground Networks - Route 4 (A-B) (Av. 9.4 -9.3 - Av 6) - trench excavation	03-Aug-26	11-Sep-26	20-Jul-26	11-Sep-26	
Underground Networks - Route 4 (A-B) (Av. 9.4 -9.3 - Av 6) - Piping Install & Weld (WFI P1 / around 15 lines)	24-Aug-26	25-Sep-26	24-Aug-26	02-Oct-26	
Underground Networks - Route 4 (A-B) (Av. 9.4 -9.3 - Av 6) - Backfilling in trenches for underground piping	07-Sep-26	09-Oct-26	14-Sep-26	16-Oct-26	
Underground Piping Route 3	25-May-26 A	18-Sep-26	13-Jul-26	04-Sep-26	
Underground Piping Route 3 - Process & SW & CW	25-May-26 A	18-Sep-26	13-Jul-26	04-Sep-26	
Underground Networks - Route 3 (A Road 6.1/6.2) - excavation & trench	25-May-26 A	14-Aug-26	13-Jul-26	31-Jul-26	
Underground Networks - Route 3 (A Road 6.1/6.2) Piping Installation & Welding (WFI / WBD / WSI)	08-Jun-26 A	04-Sep-26	03-Aug-26	21-Aug-26	
Underground Networks - Route 3 (A Road 6.1/6.2) - Backfilling in trenches for underground piping	15-Jun-26 A	18-Sep-26	24-Aug-26	04-Sep-26	
Underground Piping Other Areas	27-Jul-26	11-Sep-26	08-Jun-26	11-Sep-26	
Other Areas - RW + FFW UGP area	27-Jul-26	11-Sep-26	08-Jun-26	11-Sep-26	
Other Areas - RW + FFW UGP area - Process (IDOM)	27-Jul-26	11-Sep-26	08-Jun-26	11-Sep-26	
UG Networks - Others Areas - RW + FF (A) - Testing (PT,HT,LT etc.)	27-Jul-26	07-Aug-26	08-Jun-26	19-Jun-26	
UG Networks - Others Areas - RW + FF (E) - trench excavation (BoP and SIN)	10-Aug-26	21-Aug-26	13-Jul-26	24-Jul-26	
UG Networks - Others Areas - RW + FF (B) - Testing (PT,HT,LT etc.)	10-Aug-26	21-Aug-26	27-Jul-26	07-Aug-26	
UG Networks - Others Areas - RW + FF (D) - Piping Installation & Welding (WFI / WRA)	10-Aug-26	28-Aug-26	10-Aug-26	28-Aug-26	
UG Networks - Others Areas - RW + FF (C) - Testing (PT,HT,LT etc.)	10-Aug-26	21-Aug-26	17-Aug-26	28-Aug-26	
UG Networks - Others Areas - RW + FF (E) - Piping Installation & Welding (WFI / WRA)	24-Aug-26	11-Sep-26	19-Aug-26	08-Sep-26	
UG Networks - Others Areas - RW + FF (D) - Testing (PT,HT,LT etc.)	31-Aug-26	11-Sep-26	31-Aug-26	11-Sep-26	
PDOP UG	22-Jul-26 A	16-Sep-26	27-Jul-26	16-Sep-26	
PDOP Electrical Connection	22-Jul-26 A	16-Sep-26	27-Jul-26	16-Sep-26	
Construction - PDOP Yard - Cable Trays installation	22-Jul-26 A	11-Aug-26	27-Jul-26	11-Aug-26	
Construction - PDOP STATCOM to Gen Main Transformer - Cable pulling	24-Aug-26	01-Sep-26	24-Aug-26	01-Sep-26	
Construction - PDOP 250MVA Trf. GIS Batch1 - Cable pulling	03-Sep-26	16-Sep-26	03-Sep-26	16-Sep-26	
