

Weekly Report W31



USE THE RIGHT CARRIER • KEEP IT LOW • KEEP PEOPLE CLEAR

PIPES MUST BE POSITIVELY RETAINED

Use a manufacturer-approved pipe carrier, cradle or rack. Forks alone are not a restraint system.

DEDICATED PIPE-CARRIER ATTACHMENT

Correctly locked and compatible with the telehandler

LOAD LOW AND CENTRED

Maintain visibility, stability and ground clearance

SEGREGATED TRAVEL ROUTE

No pedestrians inside the machine or load danger zone

01

SELECT

Approved carrier/attachment and adequate capacity at actual reach

02

SECURE

Lock attachment; retain pipes against rolling and sliding

03

TRAVEL

Boom low, speed controlled, route level and clear

04

CONTROL

Competent operator, banksman where needed, exclusion zone

STOP MOVEMENT

if the load shifts, visibility is lost, ground changes or anyone enters the zone

BOP-IDOM-EHSS – DASHBOARD Summary (Week 31)

For information


Lagging Performance Indicators

415 Days LTI Free!!!!

All Incidents & Risks



SIF Potential Classification

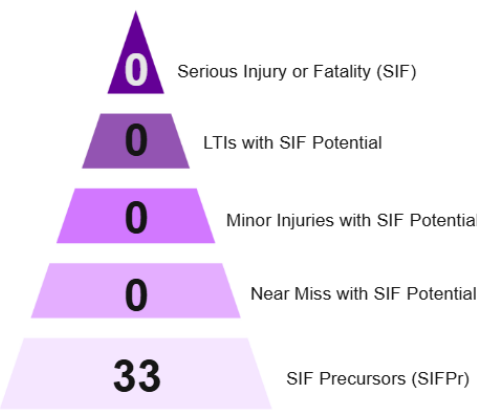

	Project to date	UE Construction	Benchmarking sector
LTIFR	1,53	5	2
TRIFR	5,10	N/A	N/A

Highlights/Downlights of the week:

- Reorganization of the HSE team




Leading Performance Indicators

	Week	Last week	Project to date
SITE WALKS	23	11	1014
OBSERVATIONS	99	66	9793
BBS INSPECTIONS	9	8	658
TARGET INSPECTIONS	23	18	369
NEAR-MISS	0	0	48
ENVIRONMENTAL IN	0	0	18
Environmental Corrective Actions Closed on Time	0	0	18
PERMITS TO WORK	45	53	877
RAMS APPROVED	10	2	103
REWARDS	0	4	41
SENDING OFFS	0	0	0

Observations by Resp. Main Contractor




Observations by Category




Total Actions Reported	Open Actions (Clickable)	Closed Actions	Closed Past Due	Open/Closed Overdue Actions (Clickable)
151	26	125	19	11



Observations by Reporting Company



Observations by Type




Site Walks by Reporting Company



CONFIDENTIAL

BOP-IDOM-EHSS – Highlights(Week 31)

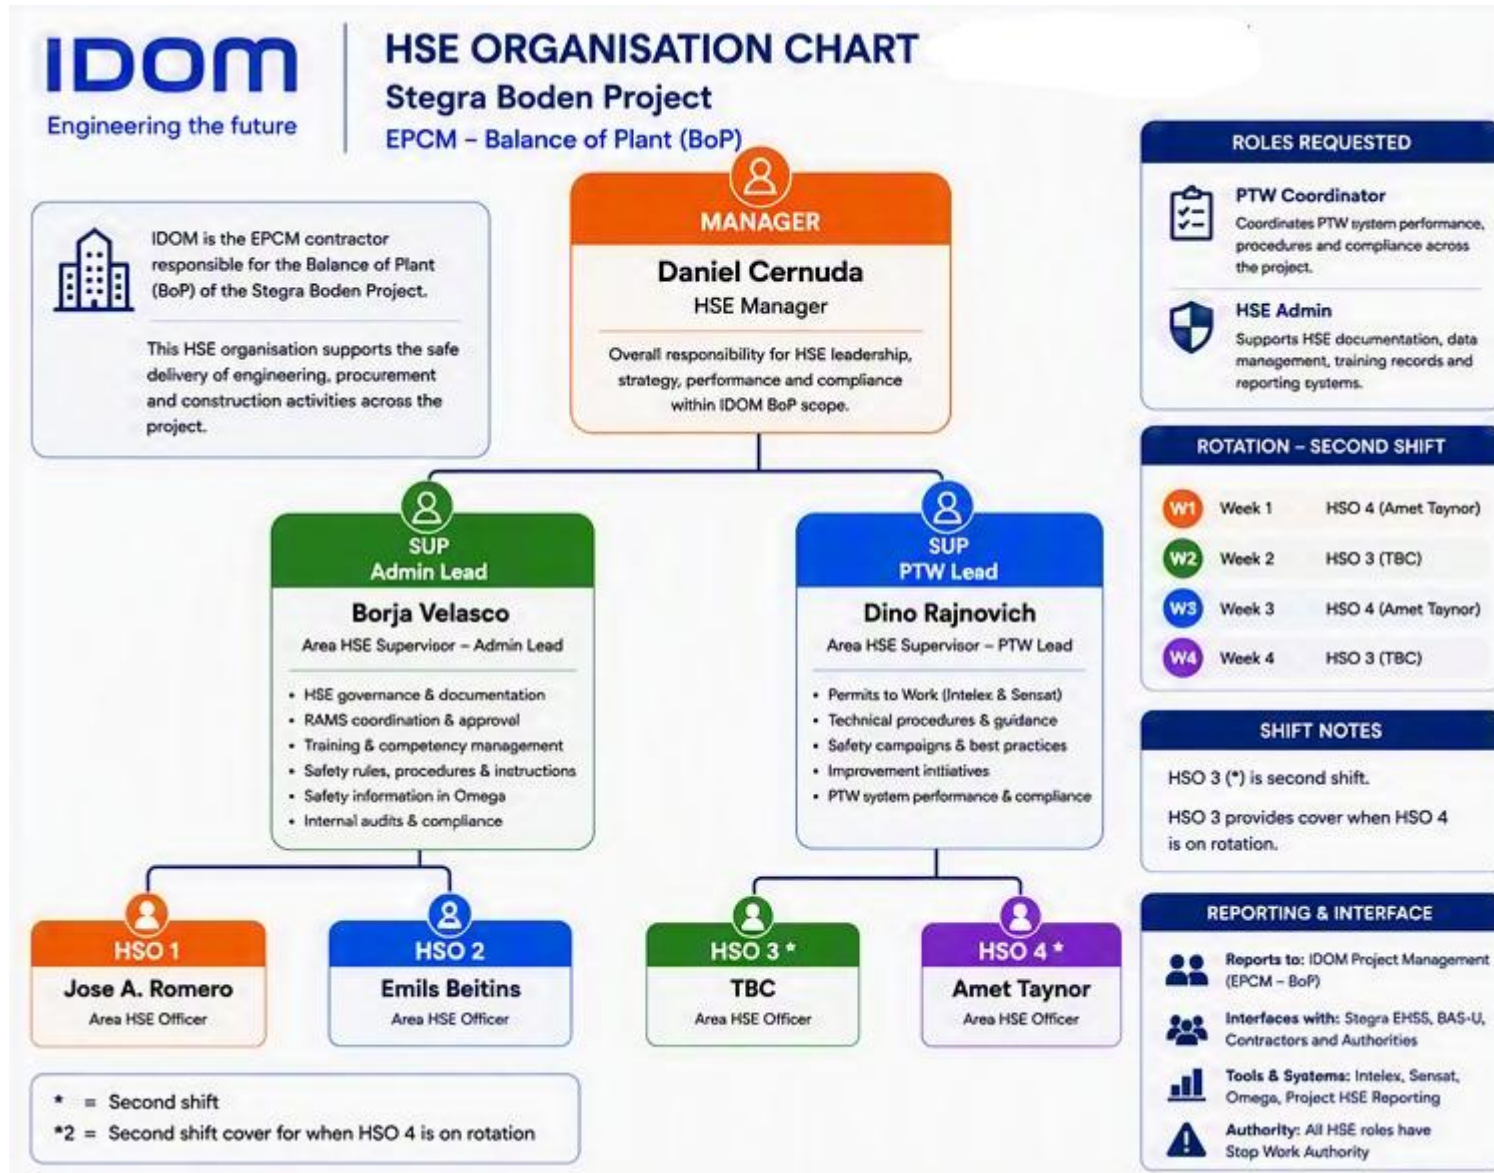


BOP-IDOM-EHSS – BBS Dashboard (Week 31)

Behaviour Based Safety Assessments

Last Update:
3 ago 2026 03:23

Checklist Name: Safe behaviour...
Related to Main Contractor: Todas
Major Area: BOP
From Week: 25W24
To Week: 26W31

Safety Performance With TRIF

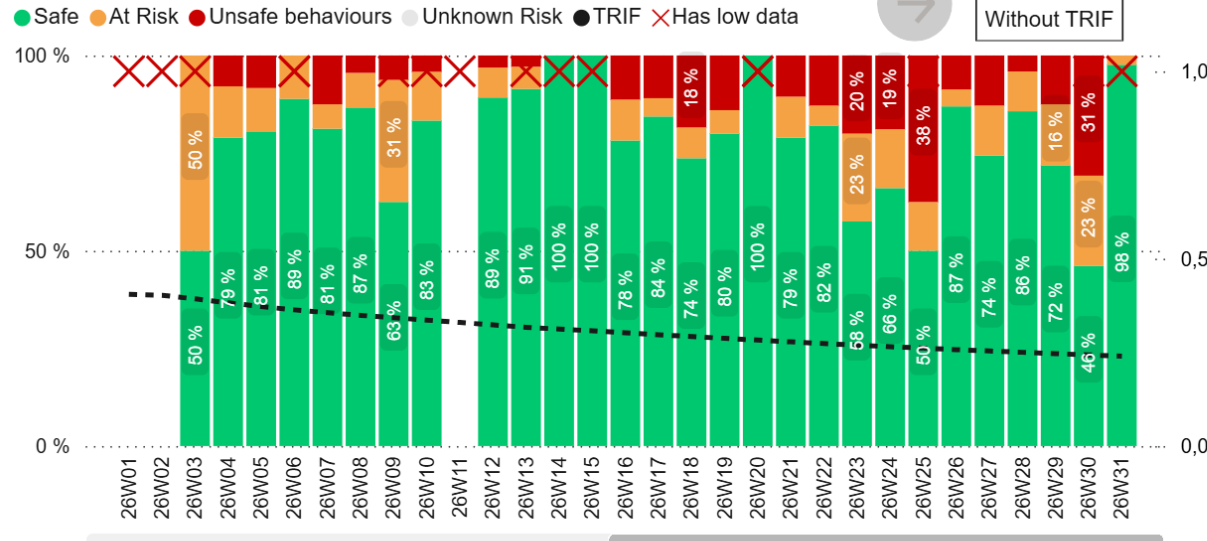

97,6%

Safety Performance (Last week)
▲ +22.4%
vs Previous period


0%

Unsafe behaviours (Last week)
▼ -11.3%
vs Previous period


58

Total assessments (Selected period)
▲ +3
vs Previous period


Safety Performance by Category

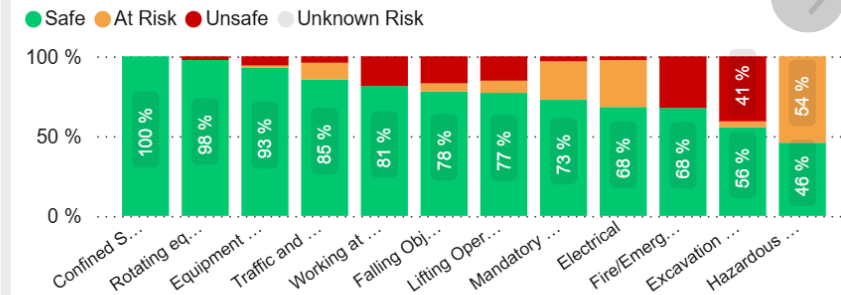


Assessment Timeline

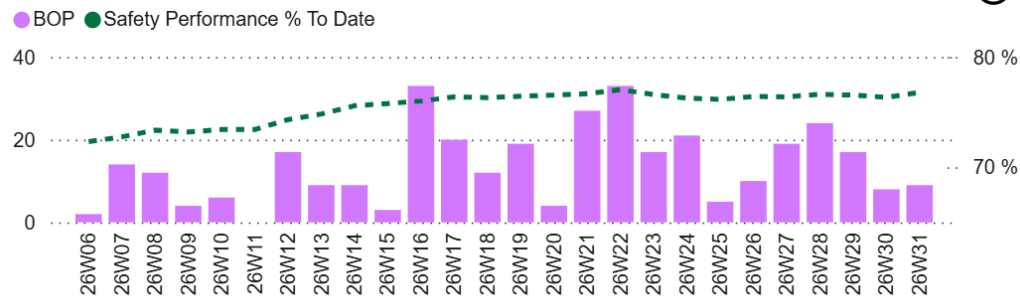

Assessments related to Main Contractor



Feedback distribution

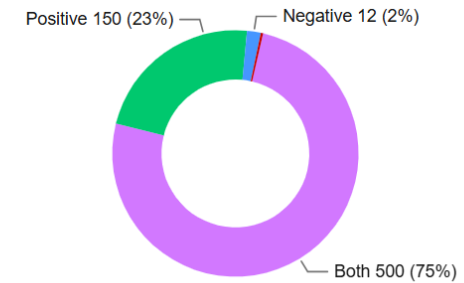

• PROJECT P-103475 · EPCM BODEN BOP

BOP Quality.

Centralized quality control workspace for the **Balance of Plant** scope of **STEGRA's** green steel facility in Boden — the world's first large-scale fossil-free steel plant. Inspection records, ITPs, audits, NCRs and procedures, governed by the IDOM site team.

QUICK LINKS

Team members

EXTERNAL TOOLS

 Airtable · QOC

 Airtable · NCR

 Airtable · NOI

 Omega 365 · EDMS

CLIENT	STAGE	QUALITY LEAD	LAST SYNC
--------	-------	--------------	-----------

QA/QC — Weekly Summary

KEY ACHIEVEMENTS

- 1 The geomembrane Air Pressure Test for the West Ponds has been completed. The corresponding Inspection Report will be issued and submitted for review. Subject to satisfactory review and approval of the Inspection Report, the document will be included as part of the corrective action plan supporting the closure of NCR-801, which was raised under the subject: "Failure of the EPCM to Manage the Contractor Regarding Geomembrane Installation." The approved report is expected to provide objective evidence that the integrity of the installed geomembrane has been verified in accordance with the project requirements and applicable inspection procedures.
- 2 The Stegra Audit Report has been received, and the findings have been internally assessed by the EPCM team. A clarification meeting is scheduled to take place this week to review the observations, align on the identified gaps, and agree on the actions required to develop and implement an appropriate mitigation plan.
- 3 The Chart Ferox pneumatic test package is currently under review (9-12, 15-18). Subject to successful completion of the review process, the system will be released for walkdowns during this week. The Notifications of Inspection (NOIs) for the pressure testing activities have not yet been received and remain pending submission by the Contractor. Timely issuance of the NOIs is required to allow inspection attendance and verification in accordance with the project quality requirements.

LOOK-AHEAD · W32

- 1 Fermix shall submit a detailed Test Pack Breakdown Structure, clearly defining the scope and contents of each Test Pack. The submission shall also include the proposed strategy for identifying, managing, and documenting any potential Golden Weld Joints, together with the applicable inspection, testing, and acceptance requirements.
- 2 GRK shall resubmit the consolidated Test Packs (TPs) for the Underground Works, Priority 1 scope, for EPCM review. To support compliance with the project requirements, IDOM QC has requested a dedicated workshop with GRK to provide guidance on the development of the Test Packs and the mandatory information to be included within each package.
- 3 Follow-up is ongoing for the closure of NCR-728. As part of the corrective actions, Actemium shall perform the required cable testing activities. The testing requirements and acceptance criteria have been prepared and issued by IDOM QC to ensure compliance with the project specifications and applicable standards.
- 4 IDOM QC has submitted the proposed closure package for NCR-753. The submission is currently pending review and response from Hitachi.
- 5 Following the Rail, Road, and Ponds Workshop, GRK shall submit the Quality Management Program for the moraine works, detailing the inspection and testing methodology to be implemented throughout the execution of the works. The Quality Management Program shall incorporate the inspection and testing requirements applicable to moraine materials, including material qualification, placement controls, compaction verification, acceptance criteria, frequencies of inspection and testing, documentation requirements, and hold/witness points, where applicable. IDOM QC has already provided the Contractor with the required Inspection and Testing Requirements and expects the Quality Management Program to be submitted for review and approval in a timely manner.

QA/QC — Major Risks

MAJOR RISKS

- 1 NCR-806: Incorrect Valve Type Installation and Missing Concrete Pads/Thrust Blocks on the Firefighting Water System (Priority 1, Zone 1) GRK shall urgently submit a Corrective Action and Mitigation Plan addressing the incorrect installation of valve types within the Firefighting Water System and the missing concrete pads and thrust blocks for the firefighting lines. The submission shall include: -Root cause analysis of the identified non-conformities. -Proposed corrective actions and implementation schedule. -Mitigation measures to manage any associated safety, operational, and construction risks. -Impact assessment on the project schedule and budget. -Recovery plan, where applicable, to minimize delays to the Priority 1 scope. -Due to the criticality of the Firefighting Water System and its impact on project readiness, the above documentation shall be submitted by GRK as soon as possible (ASAP) for EPCM and Stegra review.

QA/QC Site Quality


REPORT WEEK
W31


1
NEW NCR · W31
EPCM 0 · STEGRA 1


13
NCR OPEN
OF 109 TO DATE


65
QOC OPEN
OF 1017 TO DATE


88%
NCR CLOSED
96 OF 109 TO DATE

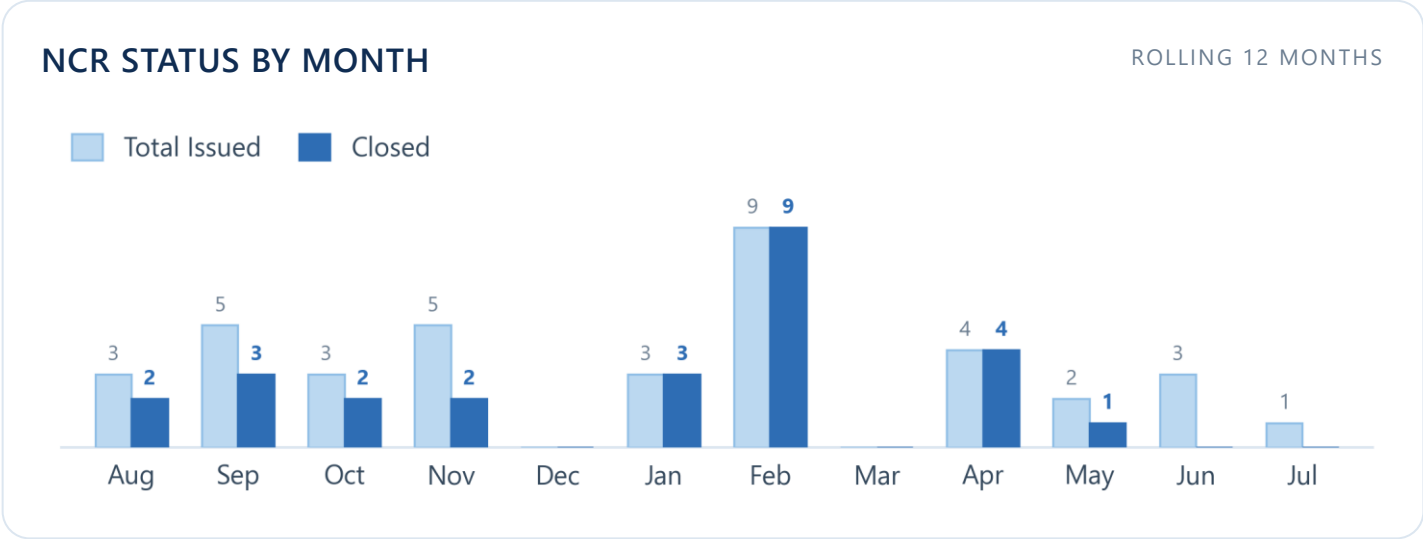

QUALITY OBSERVATIONS & NCR

OWNER	NEW	TO DATE	OPEN	>30D	>60D
QUALITY OBSERVATIONS · QOC					
EPCM	8	265	33	17	6
Stegra	1	752	32	14	16
TOTAL	9	1017	65	31	22
NON-CONFORMANCE · NCR					
EPCM	1	23	3	1	2
Stegra	0	86	10	2	6
TOTAL	1	109	13	3	8

TEST PACK STATUS

Ferrmix

CHART Ferro

GRK

Nordic Concrete

PLAN 0

SUB 2

REV 1

APR 1

CMP 1

AB 1

PLAN 18

SUB 15

REV 7

APR 7

CMP 7

AB 0

PLAN 0

SUB 9

REV 9

APR 0

CMP 0

AB 0

PLAN 0

SUB 0

REV 0

APR 0

CMP 0

AB 0

PLANNED → SUBMITTED → REVIEWED → APPROVED → COMPLETED → AS-BUILT

0%

39%

0%

0%

QA/QC — NOI & Site Activity


QUALITY PYRAMID



Site activities = NOIs + QOCs + site surveillance

WEEKLY NOI ISSUANCE BY CONTRACTORS

ROLLING 12 WEEKS

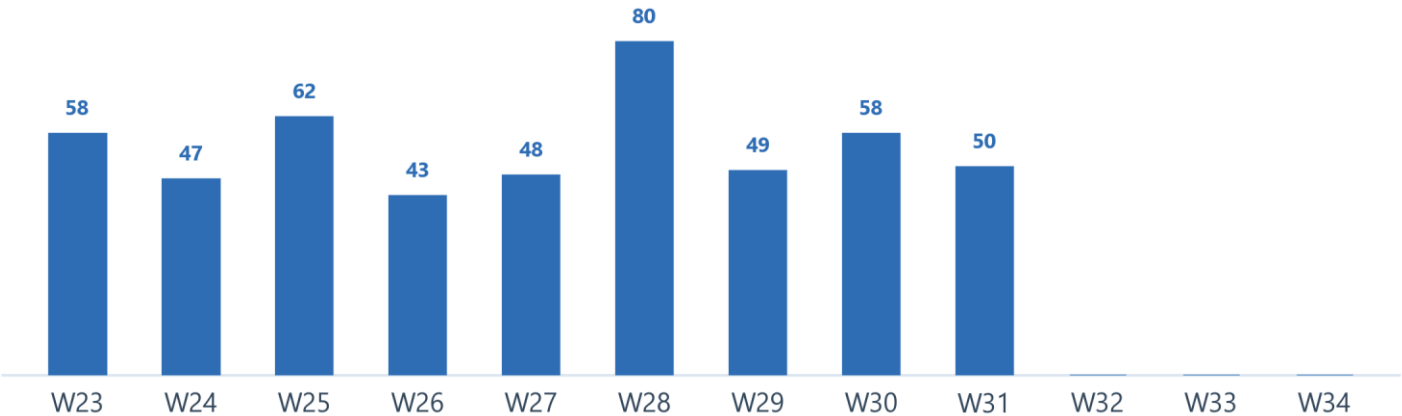

INSPECTION STATUS · W23–W34

Rejection rate 0% · KPI threshold ≤ 5%

METRIC	W23	W24	W25	W26	W27	W28	W29	W30	W31	W32	W33	W34
Accepted	58	47	62	43	48	80	49	58	50	0	0	0
Rejected	0	0	0	0	0	0	0	0	0	0	0	0
Postponed	0	0	0	0	0	0	0	0	0	0	0	0
Rejection Rate	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%	0%

QA/QC — Partial Handover

8 partial handovers between contractors · 5 in progress · 3 completed

5 IN PROGRESS

3 COMPLETED

PARTIAL HANDOVER BETWEEN CONTRACTORS

8 RECORDS

DEFINITION	SYSTEM	SUBSYSTEM	TAG NO	ITRS	TCCC	WALKDOWNS	PUNCH LIST	COMPLETED
GRK-Stegra-Municipality Piping	SIN-800-TEMP	SIN-800-01-TEMP	TEMP-BOP-1001-WRW-0800-10P1-NI	P-02A	TCCC	Done	None	Completed
GRK-Stegra-Municipality Civil	SIN-800-TEMP	TBD	TEMP-BOP-Civil_Works_ Temporary Line	C-25A	TCCC	—	—	—
GRK-Nordic RW Area	SIN-907A	SIN-907-01,02	RW Receiving &Pumping Station	TCCC	TCCC	Done	Yes	—
GRK -Nordic LNG Area	SIN-909A	SIN-909A-101	LNG-TCCC from GRK to NOR	TCCC	TCCC	Done	Yes	—
GRK-Fermix PB Area	SIN-980	SIN/980/01,02	Pipe Racks, Columns,Foundations 1-5	TCCC	TCCC	—	—	—
ANFRA/STS PDOP Area	SIN-987	SIN/987-02	PDOP Capacitor Bank Trenches	TCCC	TCCC	Done	Yes	—
Fermix/STS	SIN-980	SIN/980-01	Pipe Racks-Columns and Foundations	TCCC	TCCC	Done	—	Completed
Fermix/STS	SIN-980	SIN/980-02	Pipe Racks-Columns and Foundations	TCCC	TCCC	Done	—	Completed

Project Risk Update – Balance of Plant

- 41 total BOP Type 2 risks identified – 20 active, 1 draft, 0 parked, 0 submitted, 16 retired, 3 expired, 1 Canceled
- Out of 20 active risk – 0 critical, 5 major, 11 moderate, 4 minor risks assessed
- 60 total mitigation actions planned for all active risks – 4 overdue, 24 open, 30 closed, 2 canceled

Data Date: 17 July 2026

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R22	Construction & Site Execution	GNRL - Misaligned area schedules and complex multi-contractor interfaces lead to blocked BOP Workfront and delayed equipment deliveries resulting in schedule and cost impacts	30	- Sequence UGP and piping to avoid SMS install clashes; await SMS schedule (31/07/2026 - Open) @Marten Sonnerup - Interface Meeting with STM and BOP Construction team to align UGP works and SMS equipment deliveries. (31/07/2026 - Open) @Marten Sonnerup - Prepare reforecast schedule for BOP and Interface dates with STM and other areas (27/07/2026 - Open) @Reghardt Heunes / Comment: It is under discussion and waiting for the STM-McDermott rebaseline, which currently they are working on - Align and finalize with WTP1 and WTP2 for access dates (31/07/26 - Open) @Marten Sonnerup / Comment: Ongoing discussion, Changes in WTP2 (Eiffage contract descope) has led to a change in strategy, with Nordic (WTP2) now more aligned with Nordic (BOP). New alternatives are under discussion.	19
B1.BOP.R10	Construction & Site Execution	RAIL - Late Handover of STM Construction Areas (Scrapyard, CLP) – Impacting Rail	25	- Follow up on Micropiling progress in Scrapyard area (15/08/2026 – Open) @Roger Campbell / Comment : Work must be completed by mid-August to allow follow-on activities. Delays beyond early September will impact rail works and may place them on the critical path, with potential multi-month delays due to winter. The micro-piling contract has not yet been awarded by STM-McDermott, there might not be a short list in place; since execution takes ~8 weeks, award is required within the next few days to enable rail works to start in September as planned. Stegra have instructed STM-McDermott to provide an acceptable rebaseline.	23
B1.BOP.R548	Construction & Site Execution	Pipe Bridge (21) Modules Install blockage by STM and may need to be paused	21	- Finalize decision on BOP continuation of 19 modules and confirm if need by dates of utilities will still be met (31/07/2026 – Open) @Chris Van Der Berg	14
B1.BOP.R387	Construction & Site Execution	PDOP - Uncoordinated Installation of HV and Control Cables leading to blocked handover by HESE resulting in delay of permanent power	19	- HESE to review IFC prior to Production & Construction (31/08/2026 - Open) @Tomas Winter - HESE to define required documentation prior to Handover (31/08/2026 - Open) @Tomas Winter - [Stegra to] review and possibly revise [its] handover procedure to include electrical installation works (31/08/2026 - Open) @Tomas Winter	11
B1.BOP.R565	Project Delivery General	UGNW - Av 9 Underground piping installation may not be completed by end of 2026	19	- Award Avenue 9 scope to another contractor who is already working on site (to avoid loss of time due to running a tender and subsequent mobilisation) (31/07/2026 – Closed) @Tuncay Ozel	19

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.

Project Risk Update – Balance of Plant (2/2)

(Reviewed by Stegra and Idom Risk Management)


Status and summary comments as per *previous* week.

Risk ID	Function	Risk Title	Current Score	Risk Mitigation Actions	Predicted Score
B1.BOP.R323	Construction & Site Execution	PDNW - Resource shortfall for Power Distribution Network (Single Source E&I) may impact construction progress	14	- Engage additional E&I resources or contractors to meet required manpower levels (31/07/26 – Open) @Tuncay Ozel / Comment: The Call-Off package was shared with STS on 13 July, while the OMEGA workflow was launched to support Stegra’s internal approval. STS confirmation and the ongoing signature process remain pending. - Closely monitor workforce allocation between STM and BOP to avoid bottlenecks (30/04/27 – Open) @Guillaume Camerini	9
B1.BOP.R436	Supply Chain Management	TEMP - Availability of emergency Diesel Generator TG4	5	- TG4 is scheduled for late May, and the contract signing for mid-June. (14/08/26 – Open) @Tuncay Ozel / Comment: The bidder has confirmed updated proposal submission in W30. Subject to receipt and review of the revised proposal, TG4 is scheduled to be issued in W31.	5
B1.BOP.R484	Construction & Site Execution	PCRU - Pipe Bridge – Hydrotesting activities may get pushed into 2026–2027 winter period due to delayed prerequisites. (QLT)	15	- Develop an overall hydrotesting program, which final completion of last hydrotesting activity is before the start of the 2026–2027 winter.(30/09/26 – Open) @Javier Cervera / Comment: It is confirmed that glycol will not be used; therefore, no hydraulic piping tests will be conducted during winter.	11

*** Note: The current score reflects the effectiveness of existing controls. The predicted score represents the risk position after all planned mitigation actions have been fully implemented.



PIPE BRIDGE (Target W35)



NPB-511 (Target W37)



PROGRESS W30

- CR approved for Siemens repair works. Siemens confirmed start of repairs W32
- Inspections ongoing for Pipe Bridge earthing. ITP for testing released

BLOCKERS

- | | |
|--|-------------|
| <div></div> PB EARTHING DELAYS ON INSTALLATION, INSPECTION & TESTING → | FERRMIX |
| <div></div> ACTEMIUM ITR APPROVAL → | STEGRA |
| <div></div> GRK/FERRMIX ITR APPROVAL → | IDOM/STEGRA |

RESPONSIBLE

PENDING ACTEMIUM/EITECH ITRs

- | | |
|---|--------------------|
| -Pipe Bridge Underground Earthing → | 0% [Linked to (3)] |
| -NPB-511 underground Earthing → | 0% [Linked to (5)] |
| -ELA-01 roof trays → | 50% |
| -NPB-511 MV, LV & Control Cables → | 50% |
| -Temp Trafos to NPB-511 MV & Control Cables → | 50% |

PENDING GRK ITRs

- | | |
|---|-----|
| -Pipe rack foundations, Columns & groundworks → | 0% |
| -NPB-511 groundworks → | 0% |
| -Temporary transformers Groundworks → | 30% |

& Lightning mast

PENDING FERRMIX ITRs

- | | |
|--|-----|
| -Priority 1 zones 3-4-5-6 Structural & Cable racks → | 20% |
|--|-----|

PROGRESS

PROGRESS

BOP-IDOM-Temporary Water Progress

W31

4

Milestone

3

High priority

W33

Target

Status by Milestone

	Progress	Priority / target*
1 Permanent RW pipes around RW Chamber Approved commitment since 11 May by STEGRA PM; no action taken from GRK.	50%	High W33 1
2 Temporary spool + RW tank inlet CR-04387 raised 14 May. Commercial agreement still open. Since May, GRK only submitted price proposal on one occasion.	20%	High W32 2 3
3 Temporary lines TWTP → ASP CR-4359 raised 5 May for connection to ASP. Commercial agreement still open. Since May, GRK only submitted price proposal in 2occasions.	25%	High W31 2 3
4 RW tank watertightness test Test done W26. Test failed. C3C to come W34 to repair.	50%	Medium W34

*Targets can be achieved only if blockers are resolved W31.

BLOCKERS / CONTRAINS

1

Commercial action to GRK

GRK/Stegra to reach commercial agreement

2

CR Review resources

Add resources to reduce CR review time. Average review time in ACC 67 days


3

Strategic route GRK TEMP or NIWA

Strategic Decision Required: Proceed with the temporary water solution or transition to the permanent solution. NIWA to install → milestone 2 and 3. NIWA starts in October and finalize January as per contractual schedule

BOP | IDOM Level 1 Schedule

Progress

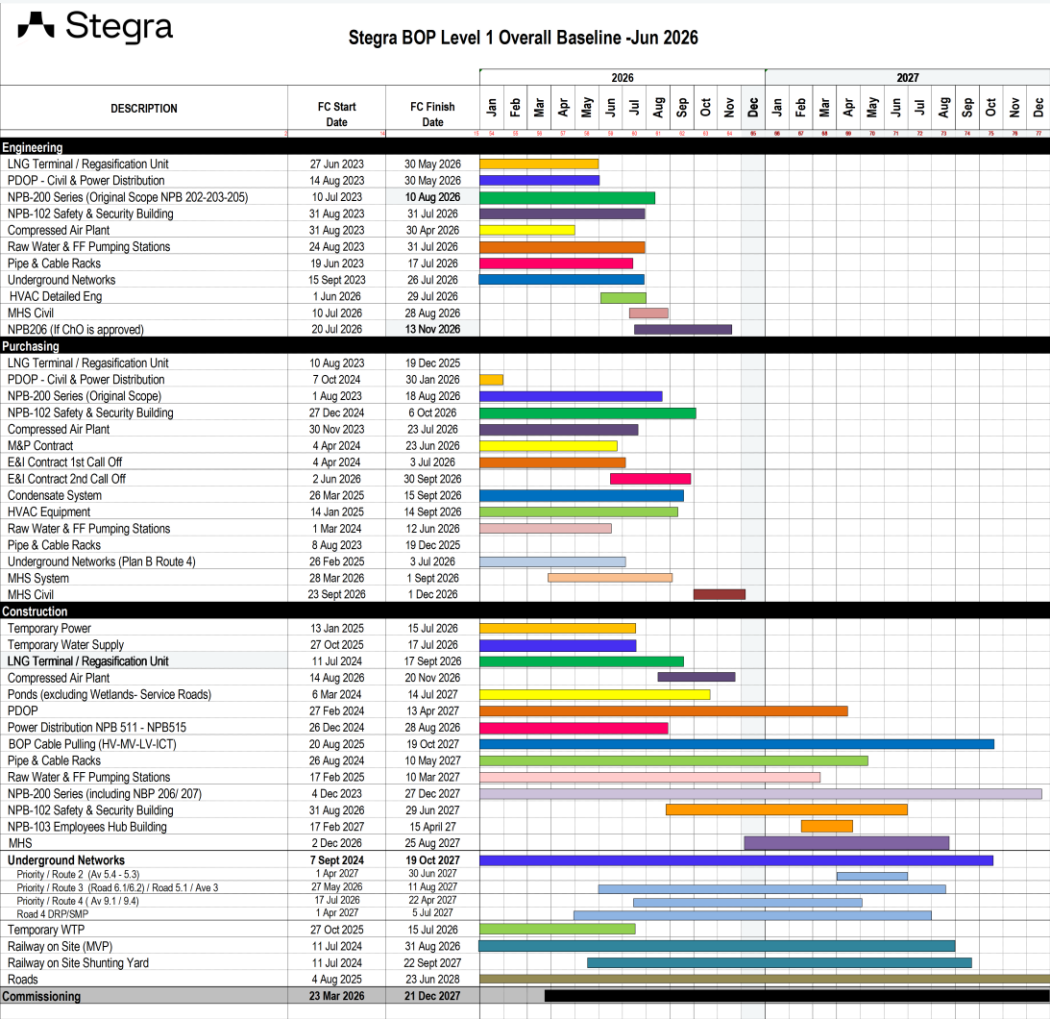

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind


BOP | IDOM Summary – Activities and Progress

Progress

Overall Progress		W31-26 (Last W) 27/07-01/08					W32-26 (Current W) 03/08-08/08
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering	Week	0,10%	0,28%	0,10%	100%	35%	0,03%
	Cumm.	97,27%	98,43%	97,27%	100%	99%	97,30%
Procurement (TG - Purchasing Process)	Week	0,21%	3,91%	0,21%	100%	5%	0,00%
	Cumm.	68,18%	80,75%	68,18%	100%	84%	68,18%
Manufacturing (On a Monthly Basis - Monthly Cut Off)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	94,20%	94,20%	94,20%	100%	100%	94,20%
Construction	Week	0,19%	0,65%	0,19%	99%	29%	0,47%
	Cumm.	52,05%	53,95%	52,05%	100%	96%	52,53%
Overall	Week	0,13%	0,55%	0,13%	99%	23%	0,28%
	Cumm.	68,35%	70,01%	68,35%	100%	98%	68,63%

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Temporary Water (Ready to Supply)	31 Jul 2026	30 Oct 2026
Temporary Power (Ready to Operate)	30 Jul 2026	30 Sep 2026
Power Supply from NPB-511 to ASP	31 Jul 2026	30 Sep 2026
Railway Groundworks Crossings Start	15 Jun 2026	17 Aug 2026

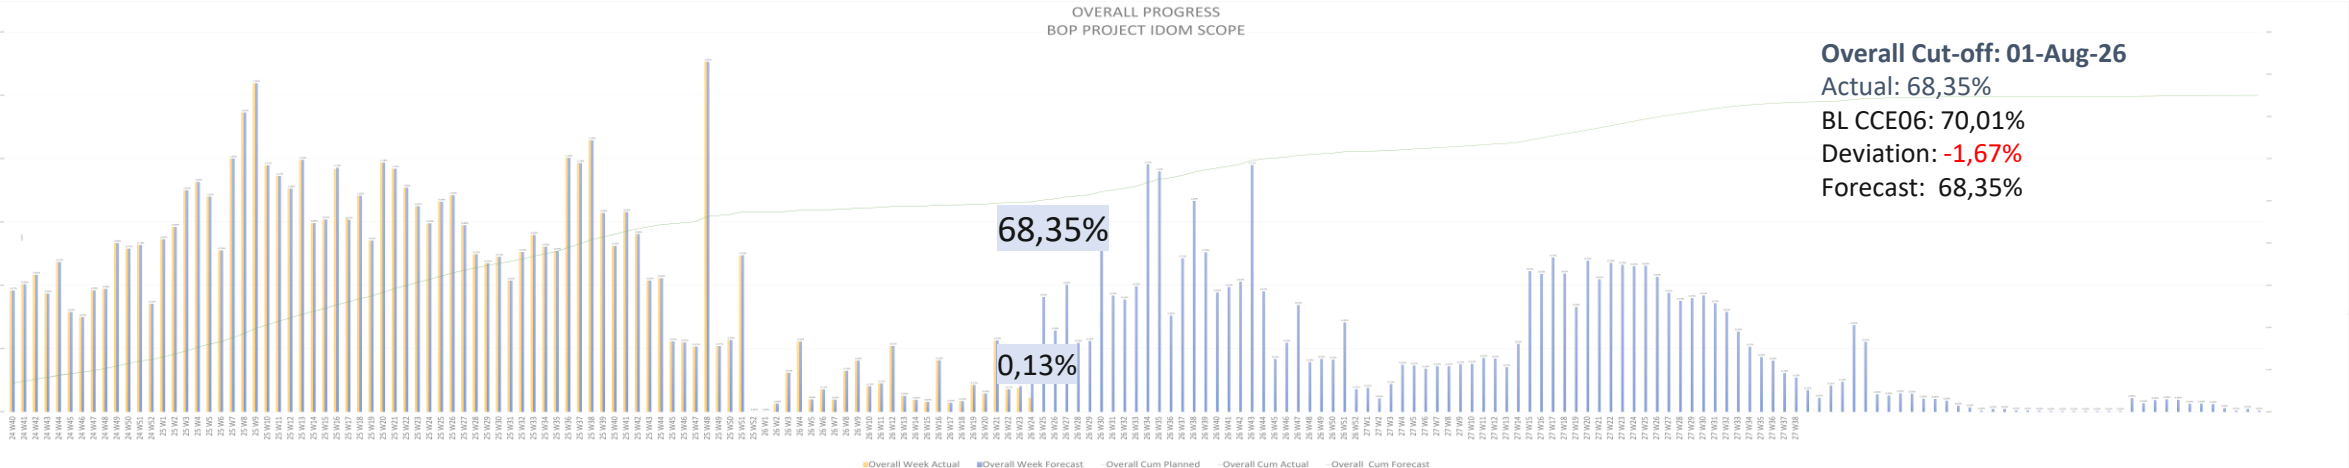


BOP | Construction progress - Planned vs. Actual

Weight	Activity	Cum Actual	Actual W31	Planned W31 (BL CCE06 TBA)	Forecast W31	Dev. Forecast Vs Actual	Dev. Planned Vs Actual	Forecast W32	Forecast W33	Forecast W34	Forecast W35	Forecast W36	Forecast W37	Deviation (Against Forecast)	Mitigation Actions
6.83%	Raw Water & FF Pumping Stations	74,65%	0,06%	0,00%	0,06%	0,00%	0,06%	0,02%	0,00%	0,00%	0,00%	0,18%	0,18%		
0.25%	Compressed Air Plant NPB-422	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
6.02%	LNG Terminal / Regasification Unit	87,02%	0,20%	2,55%	0,51%	-0,31%	-2,35%	0,67%	0,84%	1,48%	1,70%	0,46%	0,46%	1. Delay in electrical work for cable pulling 2. Delivery delay Control units	1. Chart is recovering the delay 2. Control units ETA W35
5.11%	PDOP Civil	92,82%	0,00%	0,96%	0,00%	0,00%	-0,96%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
1.76%	Power Distribution 51x	84,69%	0,00%	3,06%	0,61%	-0,61%	-3,06%	3,06%	3,06%	3,06%	3,06%	2,46%	0,00%	NPB515 start electrical works delay	In Week 32 will be hold a construction meeting with STS to review the schedule and take action if necessary to allow them to start the works
8.07%	NPB-200 Series	55,95%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
1.00%	NPB-102 Safety & Security Building	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%	0,00%		
17.84%	Pipe & Cable Racks	84,34%	0,34%	0,45%	0,34%	0,00%	-0,11%	0,38%	0,35%	0,36%	0,43%	0,25%	0,20%	Foundation missing	Expedite the Call-off with Nordic
21.06%	Underground Networks	17,55%	0,35%	1,06%	0,40%	-0,05%	-0,71%	1,18%	1,59%	2,04%	1,61%	1,42%	1,57%	1. RW/FF area: UG piping installation activities are underperforming 2. Completion of the Priority 0 RW chamber remains outstanding 3. Pressure testing for Priority 1 and Priority 3 not started	1. GRK will send a recovery schedule 2. CO to be review/approved by Stegra 3. Test pack to be submitted by GRK (support from IDOM)
9.61%	RailWay Package	33,70%	0,00%	0,70%	0,00%	0,00%	-0,70%	0,00%	0,00%	0,04%	0,09%	3,26%	3,68%	Civil contractor delayed mobilization/start of works	Based on the latest schedule received from GRK, works will start W33
22.45%	Ponds, Roads & Temporary utilities (SWECO scope)	34,18%	0,17%	0,12%	0,00%	0,17%	0,05%	0,27%	0,51%	0,49%	0,37%	0,44%	2,61%	1. Mechanical completion of Temporary Power and TWTP 2. Mechanical completion of Temporary TWTP 3 Temporary pipe pressure test	1. Completion of cable testing and earthing connection, Punch list B close out by Siemens. 2. Close commercial/contracting CR. 3 Test pack to be submitted by GRK (support from IDOM)
100.00%	Total	50,74%	0,19%	0,65%	0,19%	0,00%	-0,47%	0,47%	0,62%	0,75%	0,66%	0,84%	1,35%		

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

BOP - 8 Weeks Look Ahead

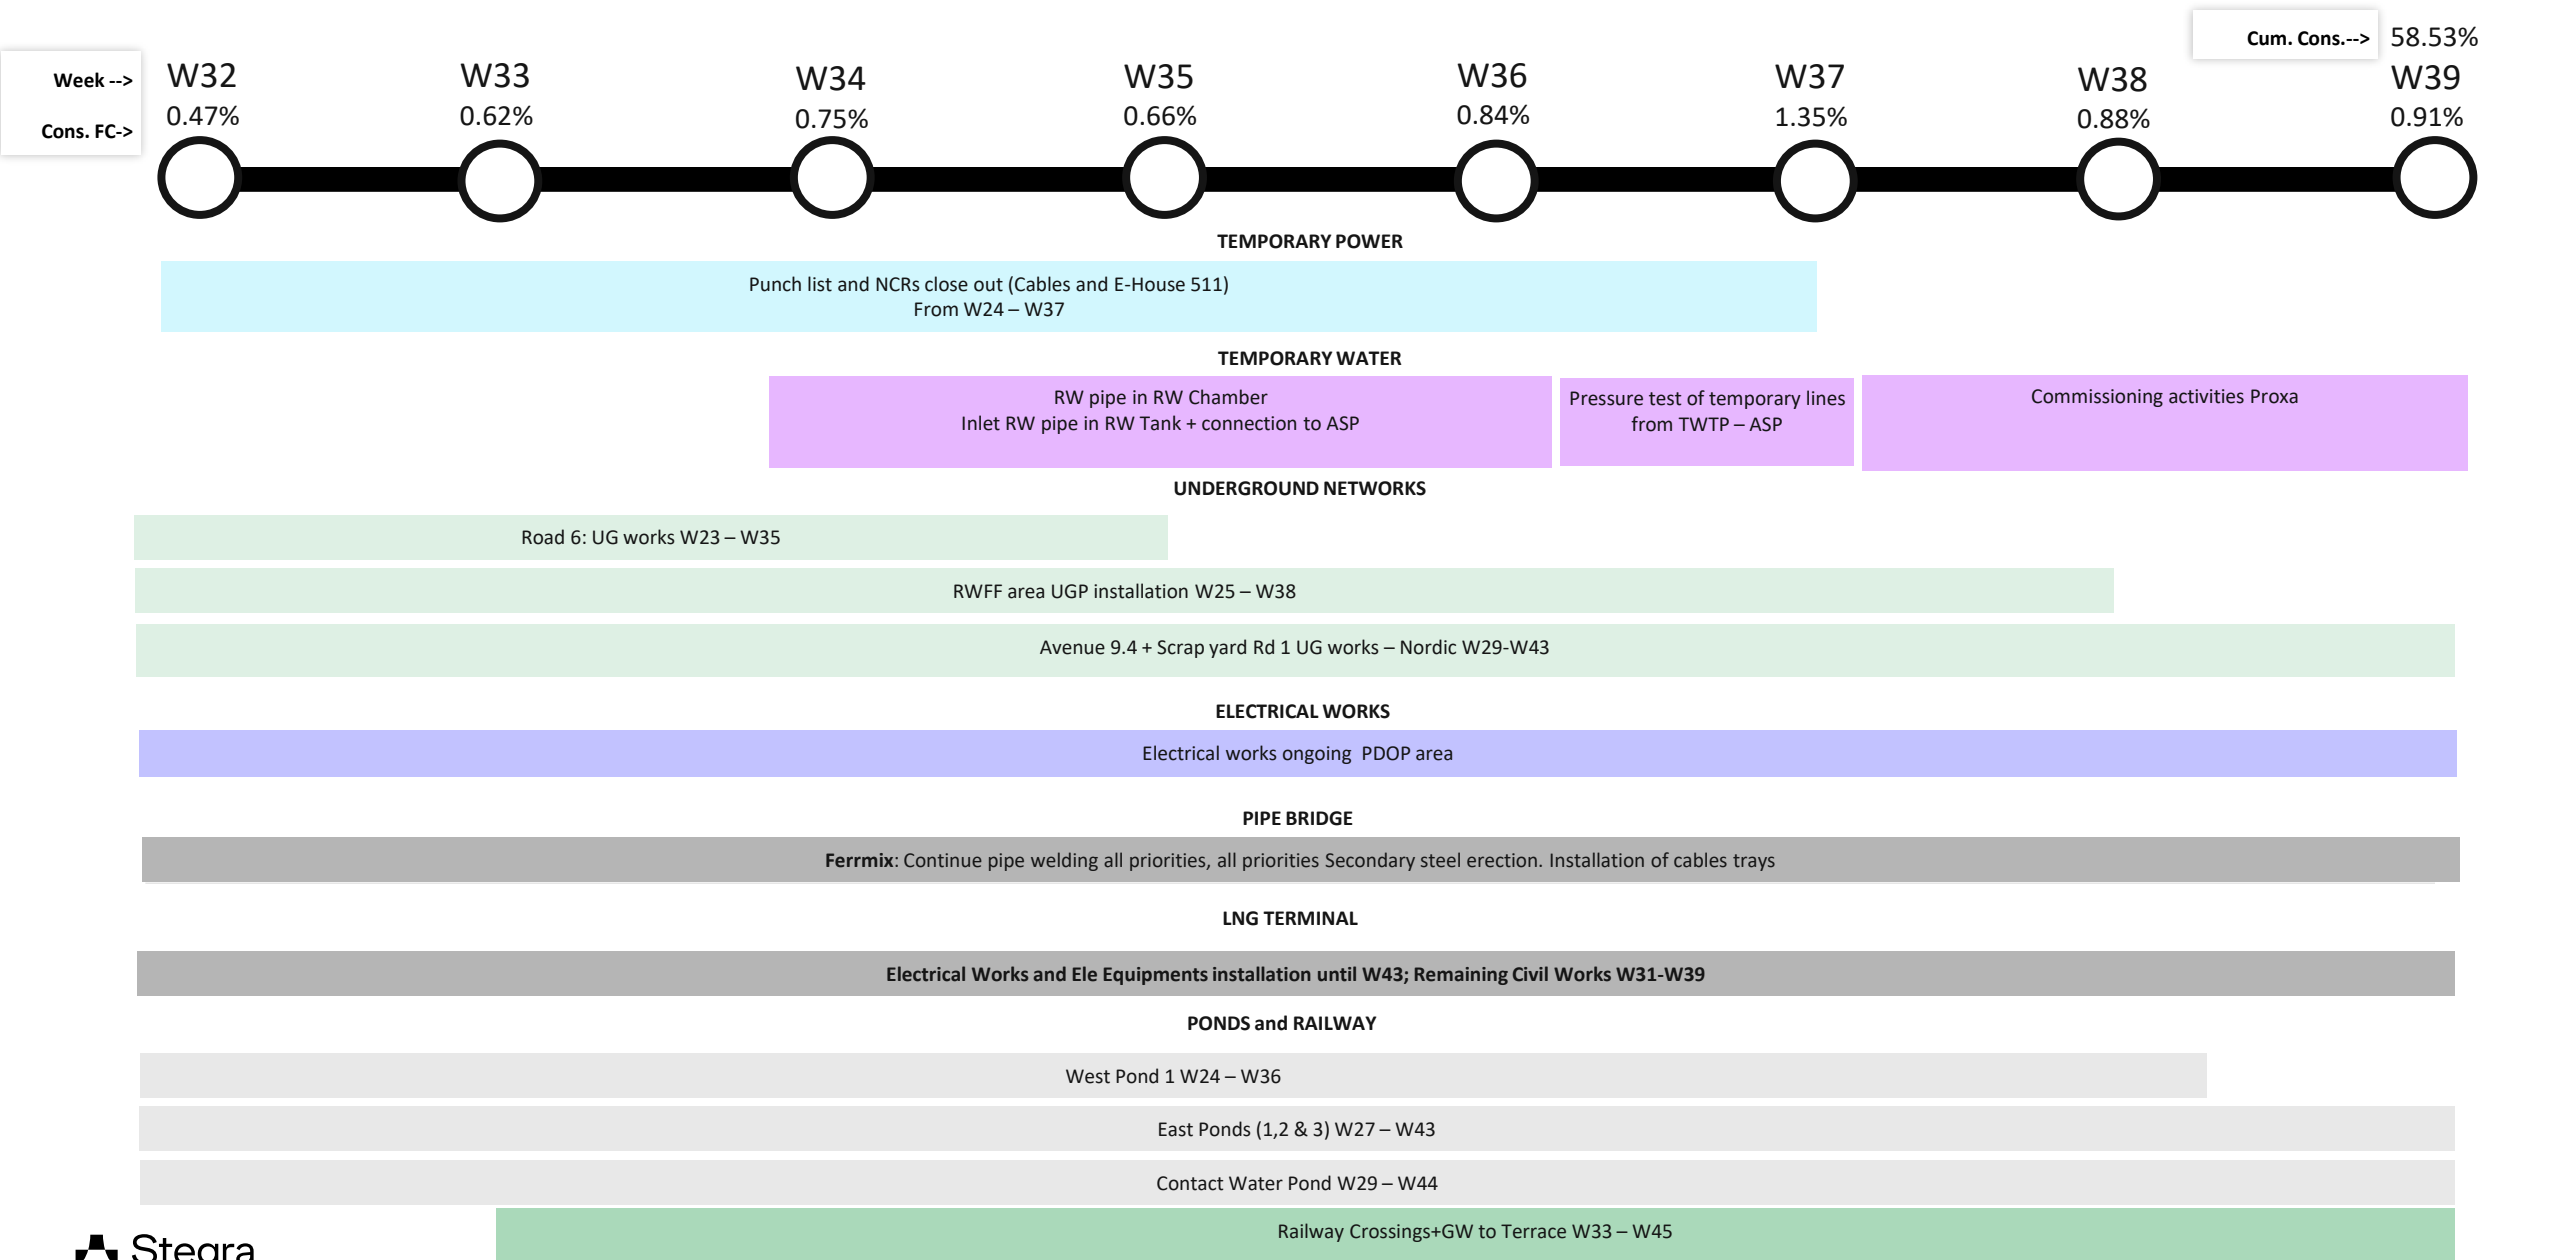

BOP | IDOM Summary – Activities and Progress -100 days look ahead

W30

Main deviations and mitigating actions

Discip	Red Activity	Due date	Mitigation Action
Proc	Chemical Dosing system for RW	W31	- PROXA: Submitted its final offer on 26/07/2026 for a total value of €629,006, together with the CRS. The documentation is currently under review. - KURITA: RFQ for Basic design sent. they confirm that will present the proposal on week 32. .
Proc	NPB-102: Security Bldg	W31	IDOM is updating the RFQ with the latest engineering information. - The procurement process has been extended by one month to improve tender quality and market competition. - Active bidders: Nordia, KSH, LC and MKL BAU. ---- Additional contractors continue to be approached. - Target: Receive a minimum of three fully compliant bids covering the complete project scope.
Proc	PB & Air Compressor found. - Retender	W31	- Call-off #3: PGB approved, Commercial and contractual alignment is ongoing. Nordic's proposal with updated BOQ, received. Updated A5, Appendices checked. - Last Proposal negotiation to be held this week. Commercial negotiation ongoing.
Proc	E&I Call-Off 1	W31	STS contract documents totally agreed. Contract to be signed on W30.
Proc	GW commitments	W31	- East ponds, Contact water pond and GW + crossings railway CR executed. Ponds KoM held in W25. GW workshop w31. - East ditch: predecessor for ROS GW in sections 4 and 5. CR: commitment on ACC is still pending for approval by Stegra.
Eng	Sweco	W30	- Road design packages expected before summer break will come after w36. No clear delivery dates available. - Rail Memo 20. Received only partially on 03/07. Missing service roads update and GW deliverables. Railway memo 21 will come after summer break. - Earthing. Ongoing discussions to clarify the scope. In parallel, Sweco is analyzing the existing information and preparing the team to start the production. - Fencing. Sweco raised two CR: CR-4433 for BOP/Steel Mill and a new one for HMP. Stegra eng will request alternative quotation. Hours provided by Sweco was too high: 4,250 hours for BOP.
Eng	Hydrogen pipeline crossing (Railway Section 4A)	W33	Sweco raised CR-04439 for the Geotechnical investigations, for CR-04441 for the culvert design and CR-04444 for the rest of the civil works. Stegra to execute the CO for Sweco to start the works when they are back from holidays. CRITICAL execution CR-04441 (culvert), design works shall start w33, including final number of pipes.
Con	Field Change Requests	W31	Stegra/IDOM to define the procedure on site for Filed Change Request and the Red-marked drawings, to establish how to include changes in the design due to construction reasons.
Con	PB Piping Connections + Pending Fittings	W35	WK30 2026- 14 welders working vs 20 forecast. 660 Forecast inches/week, Actual 482 inches/week
Con	GRK - Temporary power and WTP	W35	RW: temporary line in RW chamber CR discussion ongoing, RW tank filling pipe and overflow system Material delivery TBC, temporary pipes to TWTP to ASP CR discussion ongoing. Temporary power punch list close out ongoing

Last Week Key Achievements


- ✓ **Pipe Bridge: 482** Inches welded and 3% progress achieved during this week. Total 14.662 inches out of 20.841 welded done 70% progress achieved.
- ✓ **Cable pulling:** Total 16.212 out of 43.553 - **37% progress achieved**
- ✓ **Electrical supports** in PDOP area and GIS 95% installed



Progress

PDOP Progress		W31-26 (Last W) 27/07-01/08					W32-26 (Current W) 03/08-08/08
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	99,25%	100,00%	99,25%	100%	99%	99,25%
Construction - PDOP	Week	0,00%	0,96%	0,00%	100%	0%	0,00%
	Cumm.	92,91%	94,60%	92,91%	100%	98%	92,91%
Construction - NPB 511	Week	0,00%	3,06%	0,61%	0%	0%	3,06%
	Cumm.	84,69%	87,75%	85,30%	99%	97%	88,36%
Temporary Power		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Construction - Temporary Power	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	99,00%	99,00%	99,00%	100%	100%	99,00%

Main deviations and mitigating actions		
Discipline	RED Activity	Mitigating action
Con	Actemium: Delay PB and NPB511 UG earthing completion	Pending contractual agreement Stegra/Actemium
Con	SIEMENS: Delay to finalising NPB511 punch items	Siemens mobilization to site (expect WK33). 1 week is needed to close punches
Con	ELA01 Window to be open for STS pulling cable activity	McDermott/Stegra action
Con	Cable pulling on PB1 by STS	Cable trays on PB to be complete by Ferrmix

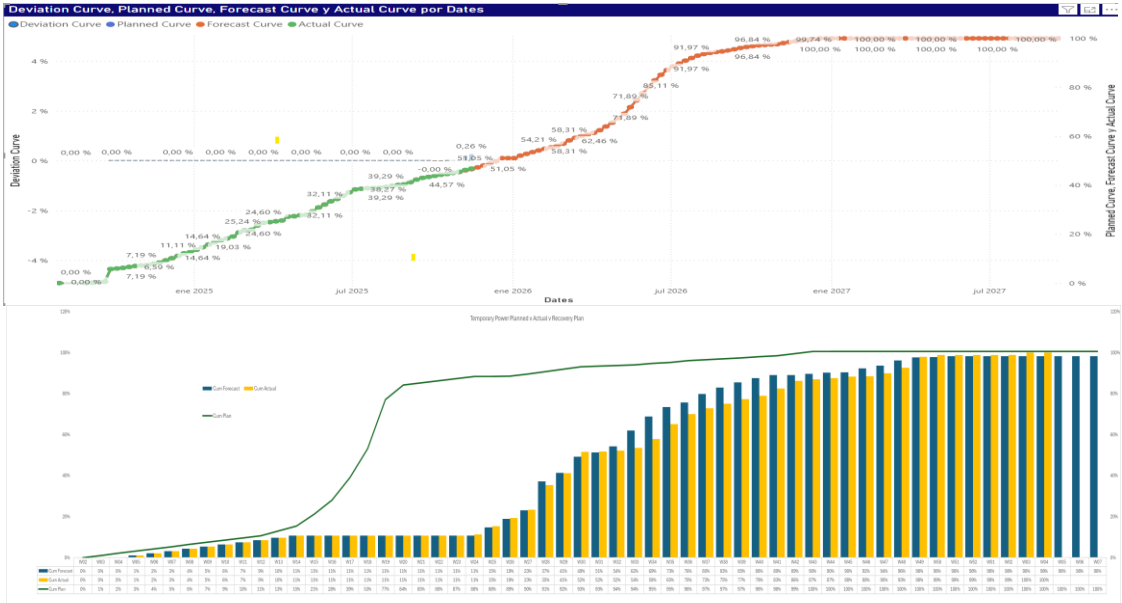

6-month key Waypoints		
Key Waypoints	Planned date	Forecast date
Mechanical Completion Temp Power	30 Jul 2026	30 Sep 2026
Electrical Works by STS Start	06 Jul 2026	27 Jul 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
Behind


Progress

LNG Progress

W31-26 (Last W)
27/07-01/08

W32-26
(Current W)
03/08-08/08

		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%
Construction -LNG	Week	0,20%	2,55%	0,51%	39%	8%	0,67%
	Cumm.	89,45%	96,51%	89,76%	100%	93%	90,43%

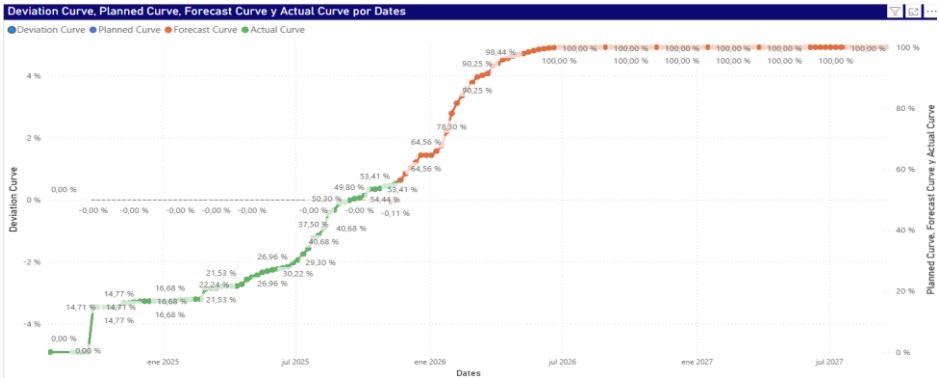

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Civil Works complete (remaining civil works)	17 July 2026	08 Oct 2026
Commence Control System Cabinet installation	08 Jul 2026	25 Aug 2026

Main deviations and mitigating actions


Discipline	RED Activity	Mitigating action
Mec	Pending 11 Pressure test to be performed	Expedite Test pack submission, review and approval
Civ	Interference between Nordic (civil works and UG network) and CHART (Mech and electrical works)	Interface management
Civ	Control Unit foundation to be levelled before equipment installation (W34).	Chart will provide shims required for final levelling.

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

Progress

PB & UGP Progress		W31-26 (Last W) 27/07-01/08					W32-26 (Current W) 03/08-08/08	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%	
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%	
Pipe Bridge (Foundation+Steel)	Week	0,34%	0,45%	0,34%	100%	76%	0,38%	
	Cumm.	85,50%	84,85%	85,50%	100%	101%	85,88%	

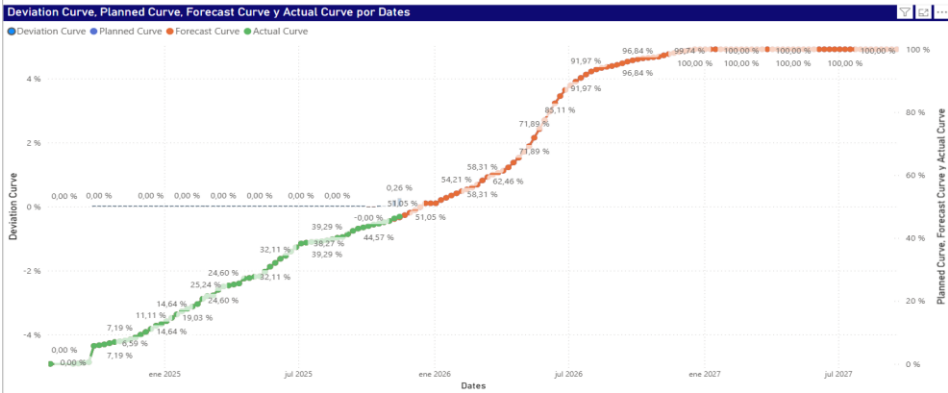

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Piping Connections - Priority 1 Finish	28 Aug 2026	28 Aug 2026
Piping Completion - Priority 1 Finish	23 Oct 2026	23 Oct 2026
Pipe rack Modules - Priority 4 Finish	24 Aug 2026	17 Nov 2026
Pipe rack Modules - Priority 3 Finish	25 Sep 2026	06 Nov 2026
Pipe rack Columns - Priority 4 Finish	20 Aug 2026	13 Nov 2026

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Con	Modules installation and piping erection (All priorities)	Call-off 3 Nordic to be signed by Stegra McDermott releasing area
Con	PB4 pipes routed through the elevator column (PB431 → SMP building)	Engineering solution
Con	Misaligned underground pipe stub-up (WRW system) (test pack PTRF006)	Engineering solution
Con	Connection with the Linde site to be clarified	Interface management

Achievement Actual / Plan OR Forecast / Plan as percentage


On track / no issue

Risk / Concern

Behind

Progress

PB & UGP Progress		W31-26 (Last W) 27/07-01/08					W32-26 (Current W) 03/08-08/08	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%	
Procurement (TG)	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	100,00%	100,00%	100,00%	100%	100%	100,00%	
UG Piping (Schedule)	Week	0,35%	1,06%	0,40%	87%	33%	1,18%	
	Cumm.	18,73%	21,32%	18,79%	100%	88%	19,97%	

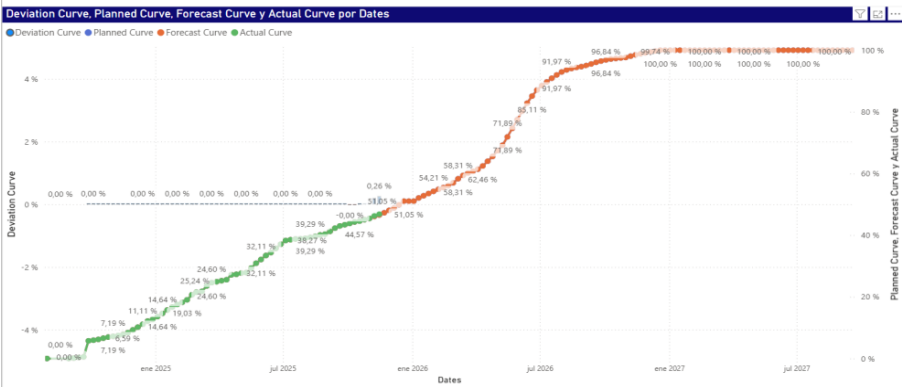

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
UGP – Route 0 testing complete	26 Jun 26	07 Sep 26
UGP – RW & FW Completion	06 Oct 26	06 Oct 26
UGP – Priority 4 and Scrap Yard Completion	10 Feb 27	1 Apr 27

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
Piping	Potable water tank connection from Av. 2.5 – Emergency Center interference.	Emergency center access to be modified by Site service
Piping	Pressure tests in Priority 1 to be done	Test pack ongoing. Pending CO approval
Piping	UG piping P0 and P1: NCR 806 - 28/07/2026 butterfly valves being installed instead of the specified gate valves	Engineering solution
Piping	RWFF area: UG piping to be installed in FF building area	TP to be submitted; CO to be signed. Pending contract award for Distric heating, Drain pumps lines and Heat tracing. Pending material change approval for ACO lines
Piping	Av9.4/9.1: working area restricted due to other Contractors' laydown area	Area to be released by Stegra

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue

Risk / Concern


Behind

BOP | Buildings & Other IDOM – Activities and Progress

Progress

Buildings & Others Progress

		W31-26 (Last W) 27/07-01/08					W32-26 (Current W) 03/08-08/08	
		ACT	Plan (BL CCE06 TBA)	FC	Ach. (Act./FC)	Ach. (Act./Plan)	FC	
Engineering (MDR)	Week	0,21%	0,21%	0,21%	100%	100%	0,00%	
	Cumm.	97,52%	97,52%	97,52%	100%	100%	97,52%	
Procurement (TG)	Week	0,85%	3,50%	0,85%	100%	24%	0,00%	
	Cumm.	80,96%	85,52%	80,96%	100%	95%	80,96%	
Construction - RWPS & FF	Week	0,06%	0,00%	0,06%	100%	100%	0,02%	
	Cumm.	74,79%	74,72%	74,79%	100%	100%	74,81%	
Construction - NPB 200	Week	0,00%	0,00%	0,00%	100%	100%	0,00%	
	Cumm.	55,95%	55,95%	55,95%	100%	100%	55,95%	

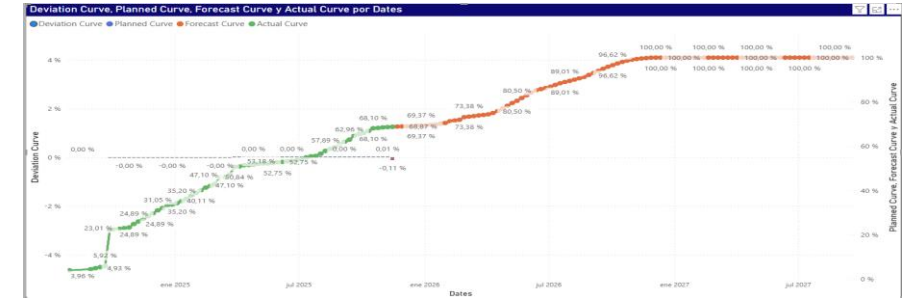

6-month key Waypoints

Key Waypoints	Planned date	Forecast date
Commence RW Pumping station structure erection	10 Sep 2026	10 Sep 2026
Commence FF Pumping station civil works	14 Sep 2026	14 Sep 2026
Commence RW Pumping station equip. installation	30 Nov 2026	30 Nov 2026
Commence FF Pumping station structure erection	19 Oct 2026	19 Oct 2026
Commence NPB205 civil work	19 Aug 2026	19 Aug 2026 (not signed)
Commence NPB102 civil work	31 Aug 2026	31 Aug 2026 (not signed)
Temporary WTP start operation	31 Jul 2026	30 Oct 2026

Main deviations and mitigating actions


Discipline	RED Activity	Mitigating action
Eng	NPB 207 – Crane Maintenance Workshop: Meeting conducted with STEGRA. Progress has been made but there are still open points.	Confirm whether building is required, define procurement strategy and utilities needs
	NPB 202 – Building on hold due to ongoing discussions concerning storage capacity and need for sprinkler system	Fire extinguishing system needed Pending building layout and rack distribution Chemical storage room layout, fire resistance requirements, containment method
	NPB 203 – Refractory Warehouse	Confirm design change insulated vs non-insulated building concept
	Chemical Container – oils and lubricants and Supplier container outside NPB 202: STEGRA engineering has retained three alternatives	Stegra to communicate power needed and any other utility depending on network under IDOM scope of design
	Review of fire detection and alarm and sprinkler system drawing by certified engineer - Pending to have a plan from certified engineer to complete the review of the BOP documentation. No review has been started yet.	Stegra to expedite this process to avoid major impacts to procurement, installation...
Con	RW Chamber temporary spool and RW Tank inlet pipe	CR to be approved

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
 ■ Behind

BOP | Railways Management (IDOM PCM – SWECO - GRK)

Progress Status

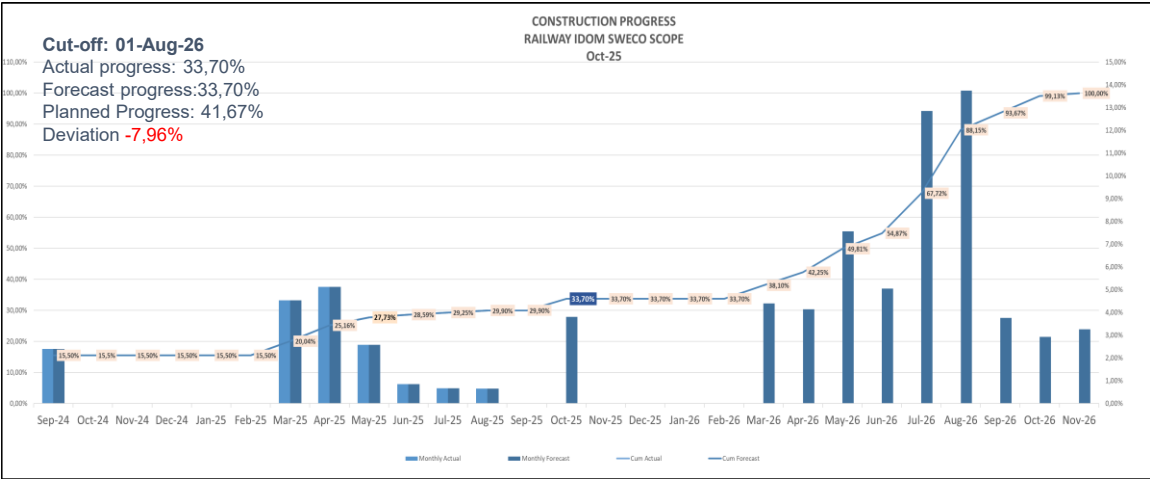

TOTAL RAILWAY	Unit	Total	Weight %	Contractor	Actual Progress	Category	WK30	WK31	WK32	WK33	WK34	WK35	WK36
Underbelt Layer (Rein.)	m3	72973	20%	GRK	31%	Period Forecast	9177	2955	10542	10542	8669	0	0
DCH. 15						Period Actual	0	0	0	0	0	0	0
Underballest Layer (Frost)	m3	118902	20%	GRK	30%	Period Forecast	3609	5390	14408	5605	0	13428	13428
DCH. 16						Period Actual	0	0	0	0	0	0	0
Catenary Poles/ Struts	ea	199	5%	GRK	33%	Period Forecast	12	0	20	12	16	0	0
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballast track	m	9602	15%	GRK	40%	Period Forecast	0	384	383	184	184	184	184
						Period Actual	0	0	0	0	0	0	0
Supplementation of ballast layer	m3	30296	15%	GRK	40%	Period Forecast	559	0	700	900	869	2250	2912
						Period Actual	0	0	0	0	0	0	0
Construction of new Ballasttles track	m	4403	5%	GRK	3%	Period Forecast	0	184	184	184	184	184	184
						Period Actual	0	0	0	0	0	0	0
Switches	ea	18	5%	GRK	39%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0
Hanging Works	ea	22	15%	GRK	27%	Period Forecast	0	0	3	0	0	1	1
						Period Actual	0	0	0	0	0	0	0
Concrete Channel Section 7 - Track 1	m	1000	1%	GRK	100%	Period Forecast	0	0	0	0	0	0	0
						Period Actual	0	0	0	0	0	0	0

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
CON	Section 3 Interference with Hydrogen pipe	Expected IFC drawing for culvert end of September 26 (SWECO)
CON	New pile deck in Scope of McDermott interfere with the pressure bern, east ditch and service road	Alternative 3 Hydrogen pipeline
CON	Scrap Yard micropilling Desing End of May (Done). Micropilling to be done by McDermott (Expected release area in June 27)	Blocking point only for railway truck. East ditch and service road on the limit boundary can start
CON	Activities planned to restart in Week 30 (Drainage piping)	Pending CO for East ditch
CON	Drainage network under Railway Truck 10,11,12 Section 3	DRP pipe laydown area to be moved

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
North railway Section 5 – Start works	06 Jul 2026	17 Aug 2026
North railway Section 4B – Start works	06 Jul 2026	24 Aug 2026
South railway Section 3 – Start works	27 Jul 2026	14 Sep 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Roads & Ditches Management (IDOM EPCM – SWECO – GRK)

Progress Status

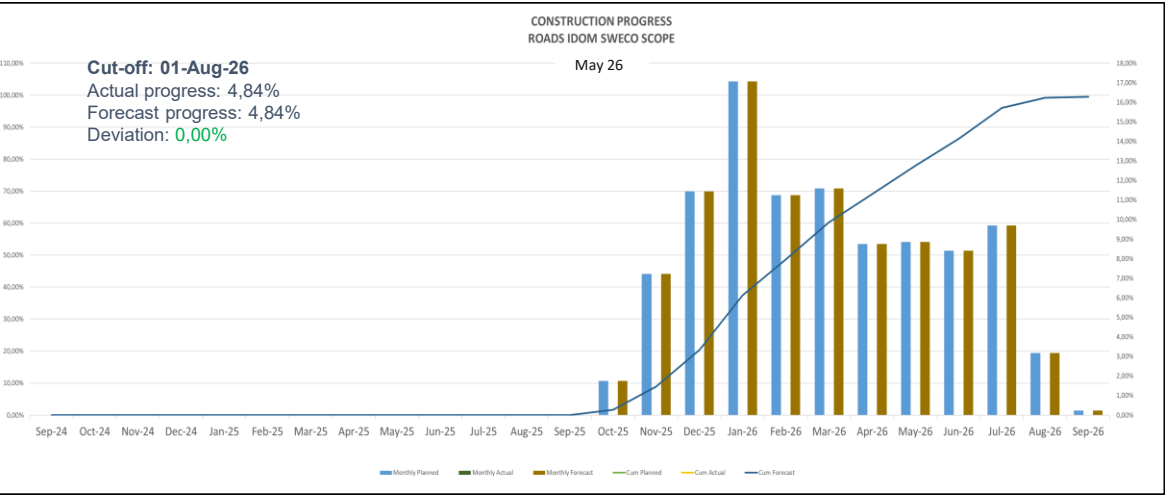

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action
CON	Av1 to be finitized	DRP rel��ase ��rea

Avenue/Roads	Activity name	Weight %	Weight % on Total	Progress	Category	WK30	WK31	WK32	WK33	WK34	WK35	WK36
						25/07/26	01/08/26	08/08/26	15/08/26	22/08/26	29/08/26	05/09/26
Av 1	Avenue 1	100%	5%	34%	% Cum Planned	34%	34%	34%	34%	34%	34%	34%
					% Cum Forecast	34%	34%	34%	34%	34%	34%	34%
					% Cum Actual	34%	34%	34%	34%	34%	34%	34%
Av 1	Roads - Avenue 1 - Clearing and levelling ground	23%		100%	Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	1	1	1	1	1	1	1
					% Cum Forecast	100%	100%	100%	100%	100%	100%	100%
					Period Actual							
					Cum Actual	1	1	1	1	1	1	1
Av 1	Roads - Avenue 1 - Laying of sub-base and base layers 1.1 & 1.2	10%		100%	% Cum Actual	100%	100%	100%	100%	100%	100%	100%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	18279	18279	18279	18279	18279	18279	18279
					% Cum Forecast	100%	100%	100%	100%	100%	100%	100%
					Period Actual							
Av 1	Roads - Avenue 1 - Laying of sub-base and base layers 1.3	6%		0%	Cum Actual	18279	18279	18279	18279	18279	18279	18279
					% Cum Actual	100%	100%	100%	100%	100%	100%	100%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	0	0	0	0	0	0	0
					% Cum Forecast	0%	0%	0%	0%	0%	0%	0%
Av 1	Roads - Avenue 1 - Application of wearing course (asphalt)	15%		0%	Period Actual							
					Cum Actual	0	0	0	0	0	0	0
					% Cum Actual	0%	0%	0%	0%	0%	0%	0%
					Period Forecast	0	0	0	0	0	0	0
					Cum Forecast	0	0	0	0	0	0	0

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Start sub-base laying Avenue 9.5	28 Sep 2026	19 Mar 2027
Start Road Ave 1 Laying subbase	20 Jul 2026	07 Aug 2026
Start sub-base laying Road 6	13 Jul 2026	14 Aug 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
Behind

BOP | Ponds Management (IDOM EPCM – SWECO – GRK)

Progress Status

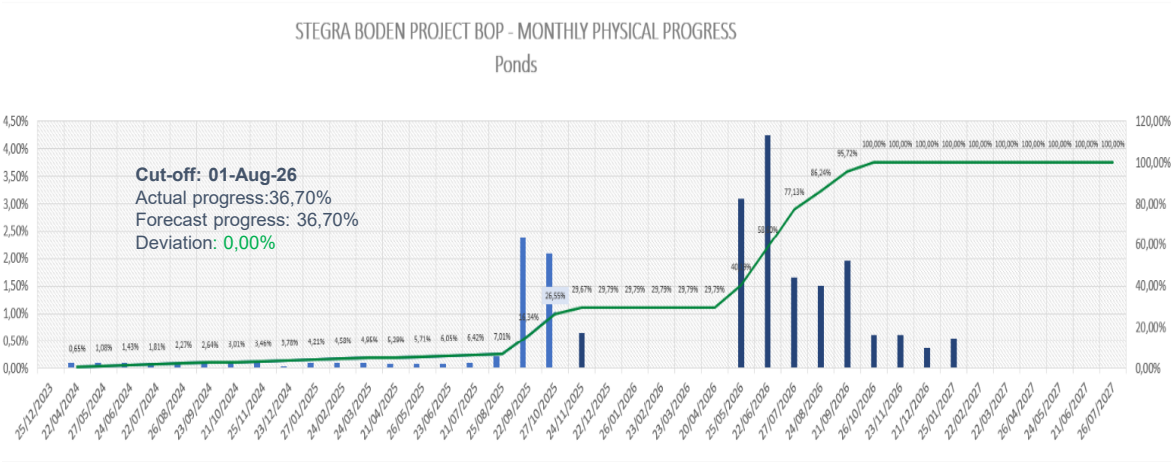

Main deviations and mitigating actions

Discipline	RED Activity	Mitigating action

WORK AREA	ACTIVITY	STATUS	Qty. Accum	% Accum	W31	W32	W33	W34	W35	W36	W37
WEST PONDS	Filling erosion cover (m3)	FC	7,300			3,000	3,000	1,300			
	Complete the North dam pocket 2 (m3)	Actual									
	Gravity pipeline in facility (lm)	Actual	160								
EAST PONDS	Excavation (m3)	FC	31,000	100%							
	Filling Moraine (m3)	Actual	15,230			2,965	2,965	2,965	2,965	2,965	
	Geotextile Protective Layer and Geomembrane double-sided textured (m2)	FC	7,100	0%							1,775
	Filling erosion cover (m3)	Actual	31,168	0%							
	Gravity pipeline in facility (lm)	FC	581								
	Embedded Pipes(lm)	Actual	18	0%							
	Valve 1200 (st)	FC	11	0%							
	Unstressed reinforcement in concrete structures (kg)	Actual	3,235	0%							
	EBE Concrete Castings (m3)	FC	40	0%							
	Excavation (m3)	Actual	10,200	25%	5,100	5,100	5,100	5,100	5,100	5,100	5,100
CONTACT WATER POND	Filling Moraine (m3)	FC	29,931	0%							
	Geotextile Protective Layer and Geomembrane double-sided textured (m2)	Actual	20,000	0%						2,850	2,850
	Erosion protection cover (m3)	FC	27,422	0%							
	Pipeline of PE pipes, sewer pipes (lm)	Actual	39	0%							
		FC		0%							

6-month key Waypoints


Key Waypoints	Planned date	Forecast date
Completion West Pond 1	30 Jun 2026	21 Aug 2026
Completion East Ponds	15 Dec 2026	06 Nov 2026
Complete Contact water pond	14 Jul 2027	20 Nov 2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
Behind

BOP | Engineering

Progress

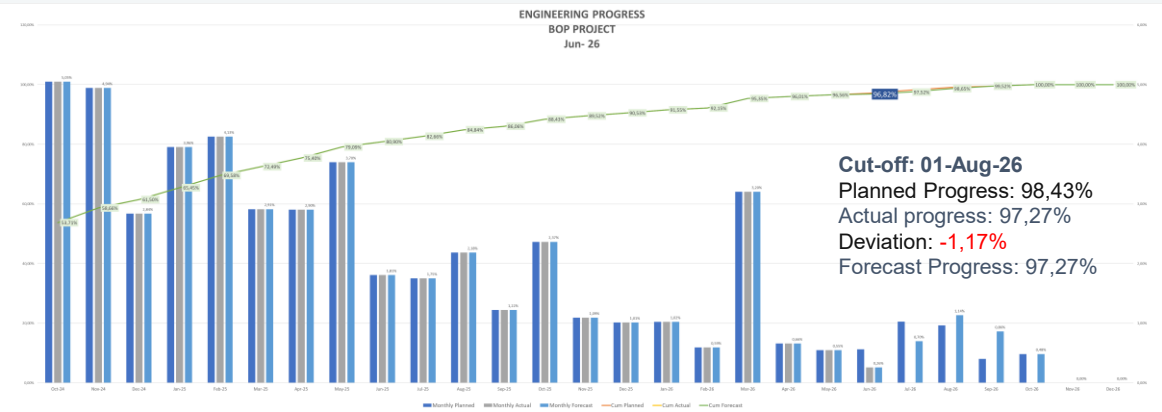

Plan deviations

RED Activity	Plan date	Fcst date	CP impact	Mitigating action	Who	When
UG system PB02 and other areas excav. dwg.	Sep-26	Sep-26	Y	- Monitoring Sweco contractual commitments - Splitting UG works in several contractors	Sweco IDOM Stegra	


Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
IDOM Integration Drawings & Excavation models UGP	IDOM has communicated to Sweco the deadlines by which they must provide the inputs for UGP design of all areas pending combined drawings and excavation models. Upcoming deadlines for Sweco: - CSP-WTP2 Area (Av. 6.0-6.1): 08-05-2026 (Delivered) - Priority 4 (Av. 9.3-9.4): 13-05-2026 (Delivered) - Priority 3 zone D (Av. 2.0): 20-05-2026 (Delivered) - Priority 5 (Road 7.5): 20-05-2026 (Delivered) - Finishing Area: 29-05-2026 (Delivered) - DRP-SMP area (Road 4): 26-06-2026 → Sweco to deliver drawings in September. 2D and 3D models were provided in w27 - DRP-Scrap yard area (Av. 9.1-9.2): 17-06-2026 (Delivered)	IDOM/Stegra	Sep-26	Open	Ongoing
Underground Piping Priority 0 Underground Piping Priority 4 Underground Piping Road 5.1 and 5.2	- Prio 0: Final revision removing holds in the roundabout in Av. 1 is moved to September. - Prio 4: IDOM is progressing with combined UGP IFC drawings. SWECO analyzed the possibility of reducing overall material and installation costs by modifying the design to reduce the meters of linear drainage/contact water gulleys. Stegra has approved the proposal and has instructed Sweco to proceed with the cheapest option. - Road 5.1 and 5.2: IDOM and Sweco UGP IFC drawings have holds from pipes going to NPB 207 – the design for this building is not developed. IDOM shall resubmit the IFC for combined drawings for Road 5. Sweco design is available.	IDOM/Stegra	Sep-26	Open	Ongoing

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
 Behind

BOP | Sweco Engineering Management (IDOM EPCM – SWECO)

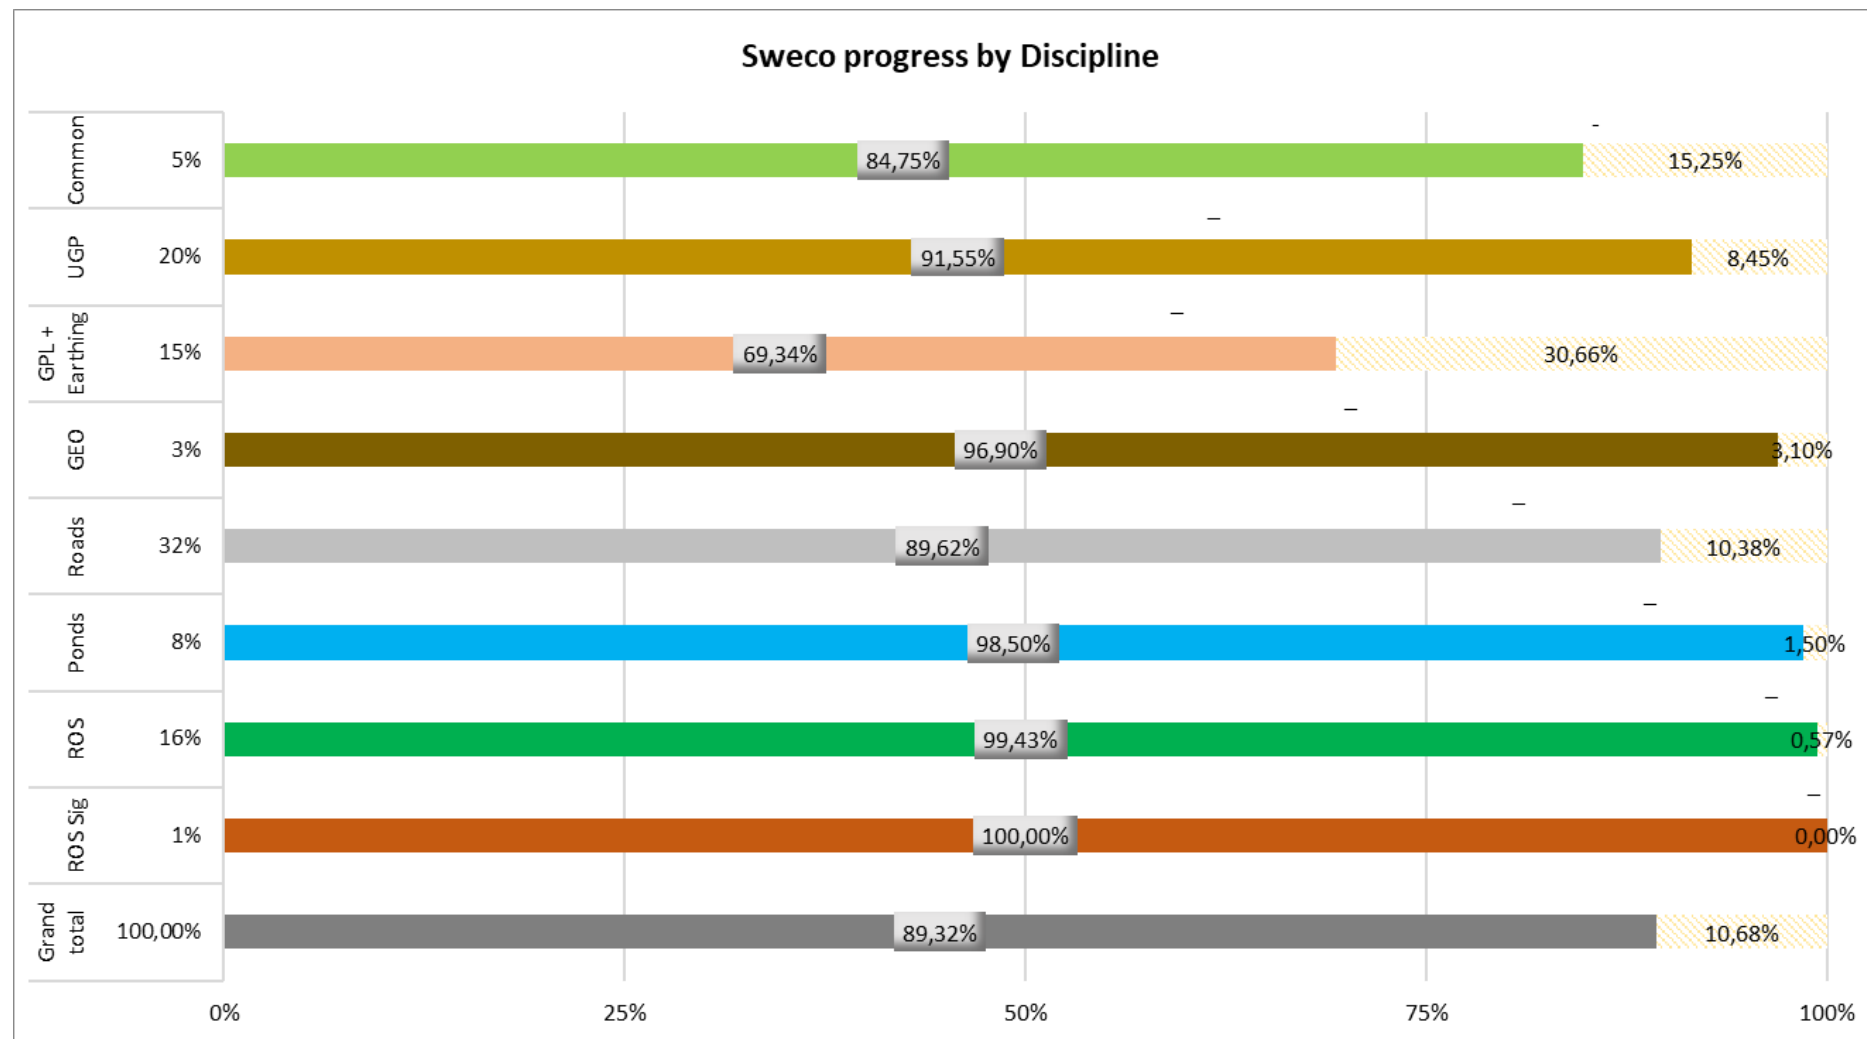

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue Risk / Concern
Behind


BOP | Sweco UGP Construction Readiness

Sweco UGP

Sweco							
Phase	Package	Construction Sta	Construction En	IFR	IFC	BoQ	Comments
1	Road 7.1 (Priority 1)	abr-26	ago-26	-	23/01/2026	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Av. 9.5 (Priority 1)	abr-26	jul-26	-	21/01/2025	14/11/2025	Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 7.5 + Road 9 (Priority 5)	abr-26	jul-26	-	10/12/2025	14/11/2025	- There is an area on-hold for the pipes going into STM cold mill and the railway area (BOD-SIN-UPB-CIV-DRWGA-00015) - Package 1 BoQ (no dedicated BoQ for Priority 5)
1	Road 6.2	abr-26	jul-26	-	11/02/2026	17/04/2026	Package 2 BoQ is already available in IFC (Dedicated BoQ for Road 6 delivery date is indicated)
1	RW+FW tanks area + Road 8	abr-26	ago-26	-	23/01/2025	18/03/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Scrap road 1	abr-26	ago-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
1	Av. 9.3-9.4 + Av. 6.0	may-26	-	21/01/2026	12/05/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due clashes with McDermott in Av. 9.3 (BOD-SIN-UPB-CIV-DRWGA-00023 + BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 (Av. 6 not included)
2	Road 5.1	jul-26	oct-26	-	05/12/2025	26/03/2026	- Area on-hold due to missing TOPs to NPB207 (BOD-SIN-UPB-CIV-DRWGA-00022) - Package 5.1 BoQ includes all of Road 5 (no dedicated BoQ for Road 5.1)
2	Av. 9.1-9.2	jul-26	mar-27	16/12/2026	08/07/2026	08/05/2026	- IFC drawings in Omega are available, however there will be a new revision due to adjustments in UGP due to the slope designed in Av. 9.1 (east of DRP) (BOD-SIN-UPB-CIV-DRWGA-00027) - Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4
2	ELA01 & PDOP	jul-26	oct-26	-	21/01/2026	08/05/2026	Current BoQ available is Package 4 from 23-01-2026. It includes Av. 9.1-9.4 and scrap roads
2	Parking 1 area	jul-26	oct-26	23/01/2026	29/05/2026	08/07/2026	- IFC drawings in Omega are available, however there will be a new revision due to UGP being on-hold in this area (BOD-SIN-UPB-CIV-DRWGA-00017 + BOD-SIN-UPB-CIV-DRWGA-00013) - Package 0 (no dedicated BoQ for UGP in Parking 1). BoQ available is in IFR from 30/09/2025
4	Road 4 + Av. 2.0	abr-27	oct-27	11/07/2025	30/08/2026	30/08/2026	Drawings in Omega are IFC but there will be an additional revision due to multiple adjustments (TOP changes, etc.)
4	Av. 6	abr-27	oct-27	25/03/2026	12/05/2026	08/05/2026	
4	Av. 5	abr-27	oct-27	11/02/2025	01/04/2026	20/05/2026	Drawings are IFC in Omega, however there will be another revision due to TOP & design changes due to McD STM
4	Av. 4.1	abr-27	ago-27	-	11/02/2026	27/05/2026	
4	Av. 3.4	abr-27	ago-27	-	11/02/2026	03/06/2026	
4	Av. 3.2 + 3.3 + Road 5.3	abr-27	ago-27	-	11/02/2026	02/04/2026	

BOP | Procurement

Progress

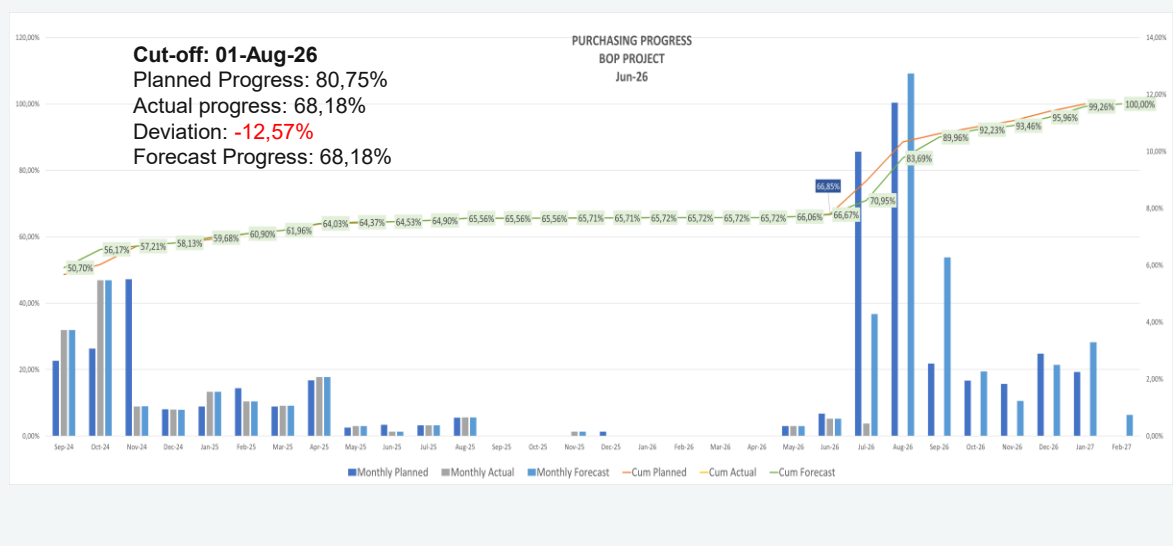

Plan deviations

RED Activity	Plan date	Fcst date	CP impact?	Mitigating action	Who	When
RW + FFPS steel struct. and cladding (ROS)	05/02/26	08/07/26	Y	LNTP: Confirmed by KSH Contract: Approved by both parties Approval of TG4 by PGB w19, contract to be signed w21.	Stegra	TBC
M&P Contractor (ROS)	19/12/25	13/09/26	Y	Awaiting NIWA's confirmation or comments on the proposed schedule. IDOM has also shared with NIWA the list of deliverables regarding pre-commissioning, cold and hot commissioning. TG4 PGB approval for w21.	Stegra IDOM	TBC
E&I Contractor (ROS)	19/12/25	28/08/26	Y	Initially, the plan was for the works to begin in June; however, since the approval process for TG4 may take approximately six weeks (GPB), it has been postponed to late June or early July. TG4 will be issued on W16. LOI approved(PGB) w19 and to be shared with STS w20.	Stegra	TBC

Key issues/potential risks and mitigation actions

Key issue / potential risk	Mitigation action	Owner	Due date	Status	Progress
Packages that will be proposed by Stegra-BOP as critical for ramp up (PGB):	- E&I - STS to submit the final version of A5 and A7, and IDOM final version of A1, all the contract documents to be shared in W26. - UG Piping Av. 9&6: Nordic to submit the last version of A7 and Nordic and Stegra to confirm all the contract documentation already shared by IDOM. - M&P Package – Contract signed. - RW&FF SS: Contract signed.				

BOP | Procurement (IDOM)

Main Packages Status



PACKAGE NUMBER	ITEMS	NEXT TG	TG FORECAST	Expected value MMEUR	TG4 forecast date	Contract signing forecast date	Forecast Arrival on Site
							(ROS forecast)
BOD-BOP-019EA	Underground Services & Roads Avenue 9.1, 2,3,4 Road 4	TG4	20/05/2026	35.9	20/05/2026	30/06/2026	01/07/2026
MISC	Remaining Civil Works	TG3	19/06/2026		10/07/2026	30/07/2026	30/08/2026
BOD-BOP-027C	HVAC engineering for BOP	TG5	22/05/2026	0.2	Approved 05/05/2026	15/05/2026	13/08/2026
	Engineering as priority						
BOD-BOP-020A	M&P Contractor	TG4	21/04/2026	4.3	21/04/2026	Signed 23/06/2026	30/08/2026 TBC
		(NIWA)					
BOD-BOP-020C	E&I Contractor	TG4	15/04/2026	32.7	15/04/2026	03/07/2026	06/07/2026
		(STS)					
BOD-BOP-051B	RW and FFPS Steel structure and Cladding	TG4	30/03/2026	0.9	Approved 11/05/2026	Signed 23/06/2026	15/08/2026
		(KSH)					
BOD-BOP-043	MHS for Slag and DRP by-products	TG3	29/05/2026	13.9	23/06/2026	14/07/2026 TBC	01/12/2026

Achievement Actual / Plan OR Forecast / Plan as percentage

On track / no issue
 Risk / Concern
 Behind

Construction Manpower & Histogram for ongoing activities

Week 31 2026	GRK	ANFRA	ACTEMIUM	FERRMIX	CHART	SIEMENS	FORSSA	LBS	PROXA	KSH	STS	NORDIC
	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual	Blue collar Actual
LNG	0				8					0		4
RAIL												
PONDS	6											
RW AREA	0						0					5
UGP RW AREA	7											
UGPO (Ave 1 & Ave 2)	0											
UGP1 (Road 7 Ave 9.5)	0											
UGP3 (Road 6)	8											
UGP4 (Ave 9)	0											11
PDOP		4										
100 MW CABLE PULL (OFFSITE)			0									
100 MW CIVILS	0											
PB FOUNDATIONS	0											
PB ERECTION & FITUP				55								
TEMPORARY POWER ONSITE			0					0				
515	0					0						
511						0						
TEMPORARY PIPE BYPASS	0											
EARTHING WORKS	0											
Roads	0											
TWTP - Mechanical	0							0				
TWTP - Electrical											10	
TOTALS	21	4	0	55	8	0	0	0	0	0	10	20
BL Total	60	0	0	65	30	0	0	0	0	0	29	100
Actual Week Average	118											
BL Week Average	285											
Forecast Average	285											

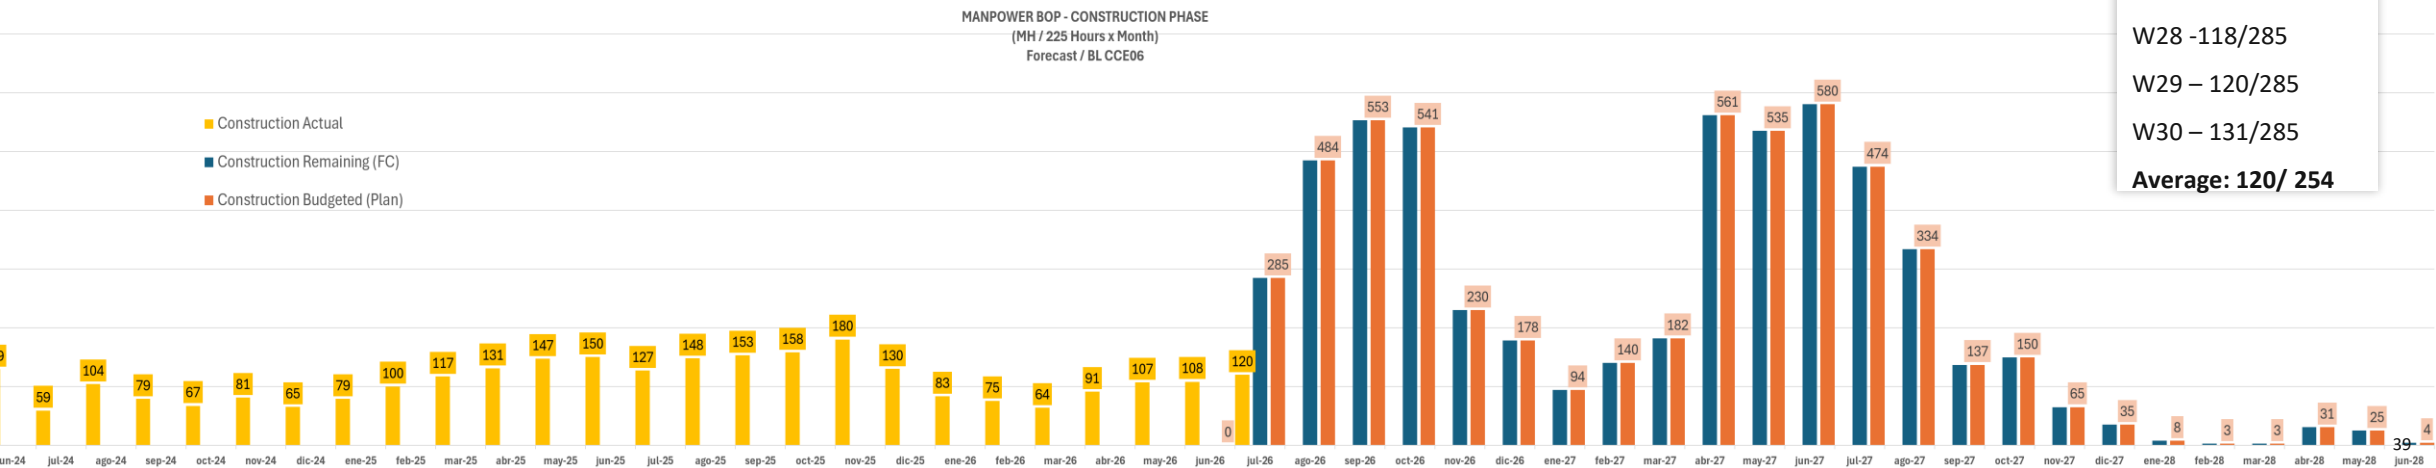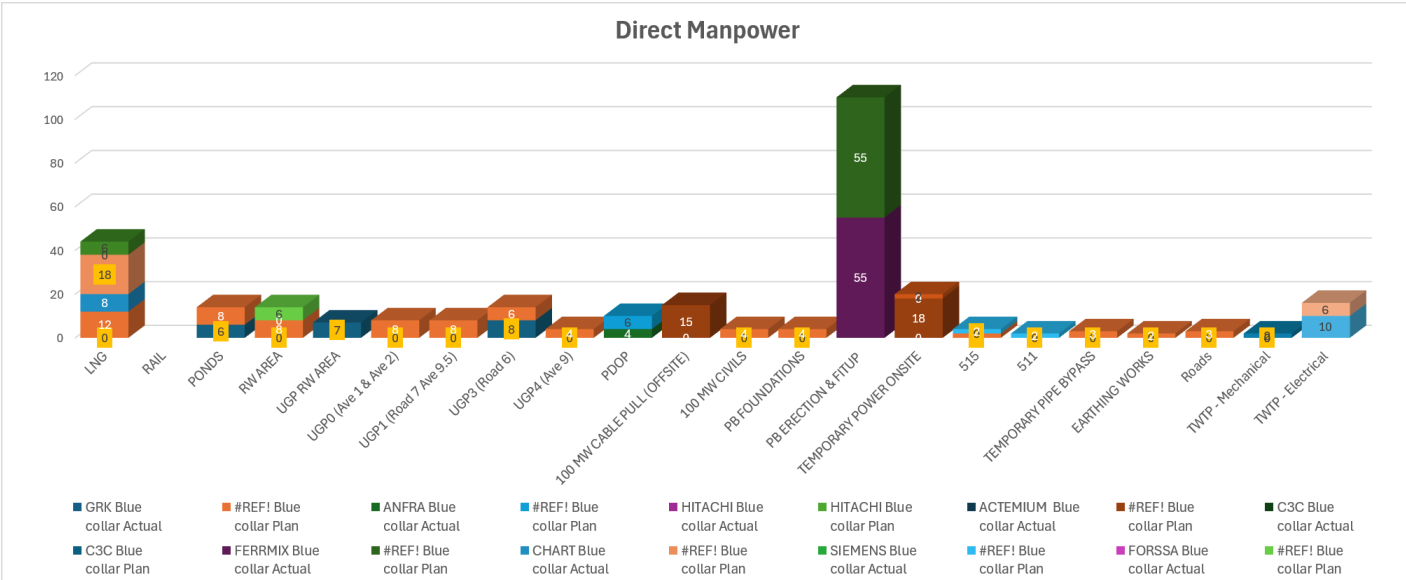

Manpower on Site:

WK27 – 108/285

W28 -118/285

W29 – 120/285

W30 – 131/285

Average: 120/ 254

BOP | Construction Pictures - Pipe Bridge

- Piping welding works (all priorities) 482 Inches welded



PB01

Achievement Actual / Plan OR Forecast / Plan as percentage

■ On track / no issue
 ■ Risk / Concern
■ Behind

BOP | Construction Pictures - UG piping

- RW/FF area: UG piping works ongoing
- Road 6 Piping installation ongoing
- Scrap road 1 Piping installation ongoing
- Av9.4 Excavation started



Scrap Rd1



Rd6.1/6.2




Av9.4

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - LNG Terminal

- Cable pulling and connection ongoing
- Civil works ongoing

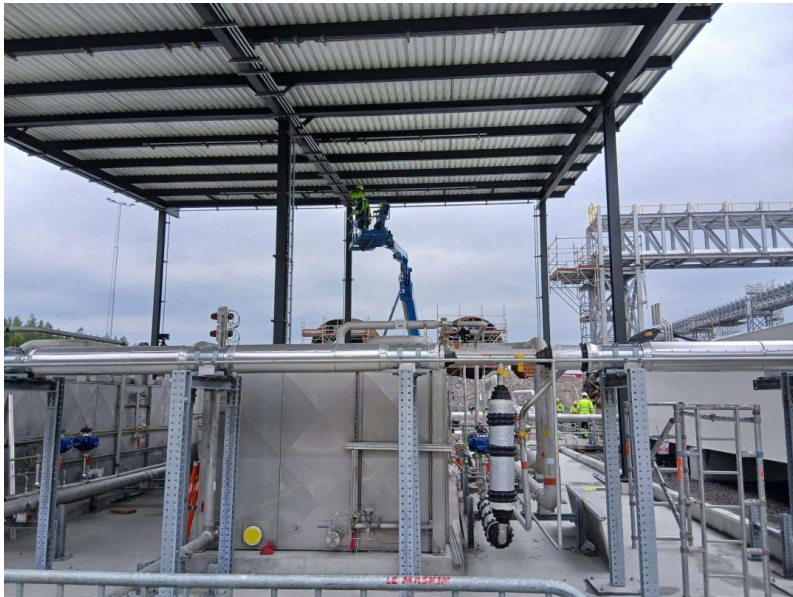

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - RW+FF Area

- UG piping installation ongoing
- Minor Remaining civil Works completed




Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures - PDOP

- Electrical supports installation in GIS and in electrical ducts between Transformers and GIS.
- Installation between T8-GIS

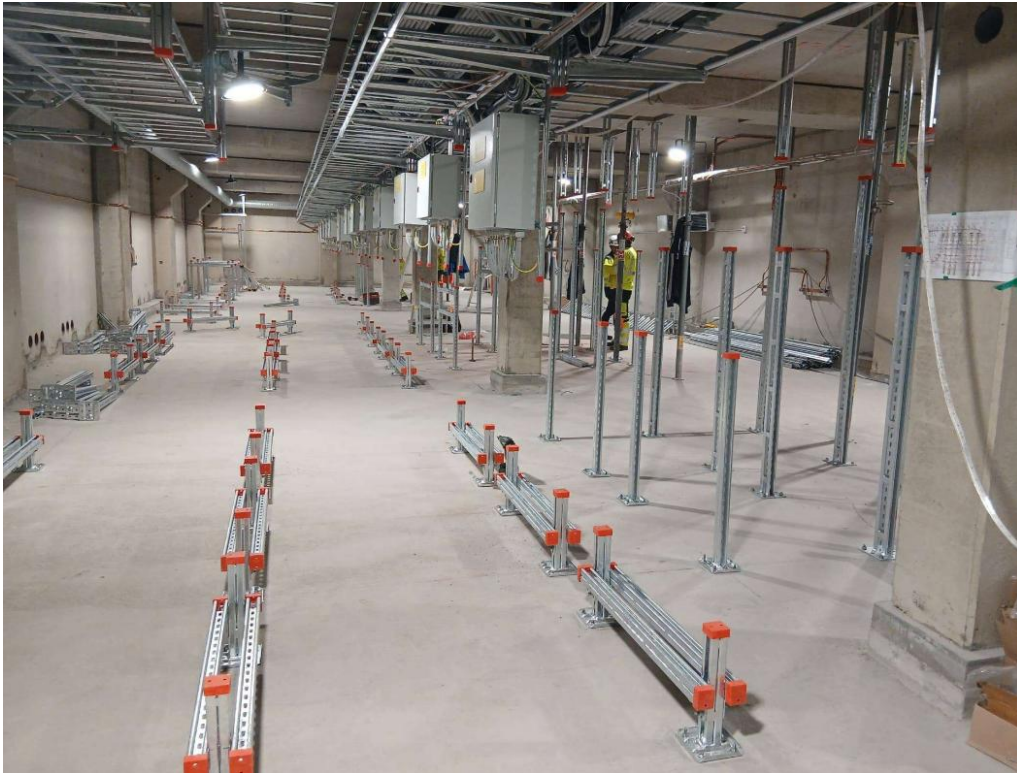

Achievement Actual / Plan OR Forecast / Plan as percentage

 On track / no issue  Risk / Concern
 Behind

BOP | Construction Pictures – Ponds

Contact Water Pond excavation ongoing



East ponds



Contact water pond



West ponds

BOP – 6 Week Look Ahead

Activity ID	Activity Name	Remaining Duration	Start	Finish	BL Project Start	BL Project Finish	August 55					September 56	
							W31	W32	W33	W34	W35	W36	W37
Balance of Plant EPC Project Schedule - Current			211	11-Dec-24 A	28-May-27	11-Dec-24	28-May-27						
Balance of Plant and Power Distribution (BOP)			211	11-Dec-24 A	28-May-27	11-Dec-24	28-May-27						
Construction			211	11-Dec-24 A	28-May-27	11-Dec-24	28-May-27						
Temporary Power Transformers 2x63 MVA / 100 MW			8	10-Aug-26	19-Aug-26	06-Jul-26	09-Jul-26						
Mechanical Completion & PreCom			8	10-Aug-26	19-Aug-26	06-Jul-26	09-Jul-26						
PS-COM-GEN-760	Pre Commissioning - E-House NP8511 (Temporary Set) for WTP1, ASP, WPS, NP820x		8	10-Aug-26	19-Aug-26	06-Jul-26	09-Jul-26						
LNG Terminal / Regasification Unit			56	04-May-26 A	12-Oct-26	04-May-26	28-Aug-26						
LNG Terminal / Regasification Unit Civil			45	27-Jul-26	25-Sep-26	22-Jun-26	21-Aug-26						
LNG-CON-CIV-60	Construction - Roads Stage 2 + Fence, Final finishing excl tarmac and weight stations		45	27-Jul-26	25-Sep-26	22-Jun-26	21-Aug-26						
LNG Terminal / Regasification Unit - Electromechanical			56	04-May-26 A	12-Oct-26	04-May-26	28-Aug-26						
LNG-CON-MEC-1022	LNG - Installation Stg III - CO_014_Odorization - Installation		3	14-Aug-26	18-Aug-26	27-Jul-26	07-Aug-26						
LNG-CON-MEC-0998	LNG - Installation Stg1 - NDE, Pressure test Installation Ph1		20	01-Jun-26 A	21-Aug-26	01-Jun-26	26-Jun-26						
LNG-CON-MEC-1017	LNG - Installation Stg II - NDE, Pressure test Stage II.		20	01-Jun-26 A	21-Aug-26	01-Jun-26	26-Jun-26						
LNG-CON-MEC-1000	LNG - Installation Stg II - Process pipes insulation		20	29-Jun-26 A	21-Aug-26	26-Jun-26	26-Jun-26						
LNG-CON-MEC-1018	LNG - Installation Stg II - Process pipes insulation		20	29-Jun-26 A	21-Aug-26	22-Jun-26	17-Jul-26						
LNG-CON-MEC-1027	LNG - Installation Stg IV - Control System (XE90)		5	19-Aug-26	25-Aug-26	08-Jul-26	14-Jul-26						
LNG-CON-MEC-1025	LNG - Installation Stg IV - Mechanical completion check		4	25-Aug-26	28-Aug-26	18-Aug-26	21-Aug-26						
LNG-CON-MEC-1014	LNG - Installation Stg III - VIP (B666)		20	03-Aug-26	28-Aug-26	29-Jun-26	24-Jul-26						
LNG-CON-MEC-1023	LNG - Installation Stg III - NDE, Pressure test		5	01-Jun-26 A	28-Aug-26	01-Jun-26	14-Aug-26						
LNG-CON-MEC-1024	LNG - Installation Stg III - Process pipes insulation		5	29-Jun-26 A	28-Aug-26	17-Aug-26	21-Aug-26						
LNG-CON-MEC-1013	LNG - Installation Stg II - Lighting (XE96)		10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26						
LNG-CON-MEC-1001	LNG - Installation Stg1 - Electrical Installation and completion check		50	04-May-26 A	02-Oct-26	04-May-26	28-Aug-26						
LNG-CON-MEC-1016	LNG - Installation Stg III - Electrical Installation and completion check		50	25-May-26 A	02-Oct-26	25-May-26	28-Aug-26						
LNG-CON-MEC-1029	LNG - Installation Stg IV - Electrical Installation		11	25-May-26 A	12-Oct-26	25-May-26	28-Aug-26						
LNG-CON-MEC-1021	LNG - Installation Stg II - Electrical Installation and completion check		6	25-May-26 A	12-Oct-26	25-May-26	15-Jul-26						
Temporary Water Supply			25	07-Sep-26	09-Oct-26	29-Jun-26	17-Jul-26						
IF-CON-CIV-2080	Construction - Underground Networks - Route 0 - RW Chamber - Piping Arrangement - Temporal Solution		25	07-Sep-26	09-Oct-26	29-Jun-26	17-Jul-26						
Raw Water Pumping Station Building			35	13-Aug-25 A	11-Sep-26	13-Aug-25	30-Jul-26						
Raw Water - Civils, Structural and Architectural (CSA)			35	13-Aug-25 A	11-Sep-26	13-Aug-25	30-Jul-26						
WPS-CON-CIV-0080	RW Bld. Construction - Ground Floor Beams & Slab		6	13-Aug-25 A	03-Aug-26	13-Aug-25	17-Jul-26						
WPS-CON-CIV-170	RW Bld. Construction - Backfilling Work		10	31-Aug-26	11-Sep-26	27-Jul-26	30-Jul-26						
Raw Water Tank			15	24-Nov-25 A	14-Aug-26	24-Nov-25	22-Jun-26						
WPS-CON-MEC-390	RW Tank Construction - Tank Testing (leaks and settlement)		15	24-Nov-25 A	14-Aug-26	24-Nov-25	22-Jun-26						
Power Distribution			72	07-Jan-25 A	03-Nov-26	07-Jan-25	30-Sep-26						
PDOP Supply 170kV Substation PDOP			20	16-Jul-26 A	21-Aug-26	22-Jun-26	30-Jul-26						
PS-CON-CIV-710	Construction - PDOP Trenches/ GIS to T8		20	16-Jul-26 A	21-Aug-26	22-Jun-26	10-Jul-26						
PS-CON-CIV-720	Construction - PDOP Trenches/ T8 to Statcom		20	20-Jul-26 A	21-Aug-26	10-Jul-26	30-Jul-26						
PS-CON-CIV-730	Construction - PDOP Trenches/ Statcom to T1		20	20-Jul-26 A	21-Aug-26	10-Jul-26	30-Jul-26						
PDOP Hitachi-Schneider			72	07-Jan-25 A	03-Nov-26	07-Jan-25	30-Sep-26						
PS-CON-ELE-0090	Construction - SMP - Installation of Final Control cabling		0	03-Nov-25 A	27-Jul-26	03-Nov-25	26-Jun-26						
PS-CON-CIV-280	Construction - Structural Works including building service - Statcom		11	10-Mar-25 A	10-Aug-26	10-Mar-25	22-Jun-26						
PS-CON-ELE-0110	Construction - SMP - Installation Works - Remaining Install 170 kV GIS & termination of Control Cables		17	21-Nov-25 A	21-Aug-26	21-Nov-25	03-Jul-26						
PS-CON-ELE-0240	Construction - MEP Building Services - GIS Building		20	07-Jan-25 A	21-Aug-26	07-Jan-25	22-Jun-26						
PS-CON-STR-0070	Construction - Equipment Set in Place - GIS Building		26	28-Jan-26 A	31-Aug-26	28-Jan-26	22-Jun-26						
PS-CON-STR-110	Construction - Equipment Installation - GIS Building		1	01-Sep-26	01-Sep-26	23-Jun-26	23-Jun-26						

Actions

BOP – 6 Week Look Ahead

Activity ID	Activity Name		Remaining Duration	Start	Finish	BL Project Start	BL Project Finish		August 55					September 56		
									W31	W32	W33	W34	W35	W36	W37	
	PS-CON-ELE-0050	Construction - SMP - Install Power Transformer SAT - Unit T 1, 5, 6	38	13-Apr-26 A	16-Sep-26	13-Apr-26	23-Sep-26									
	PS-CON-STR-0110	Construction - SMP - Installation Capacitor Banks 150 kV	42	27-Jul-26	22-Sep-26	02-Jul-26	18-Sep-26									
	PS-CON-ELE-0230	Construction - Equipment Installation - Transformer Pits	43	20-Apr-26 A	23-Sep-26	13-Apr-26	02-Sep-26									
	PS-CON-STR-0050	Construction - Equipment Set in Place including electrical works - Statcom	46	17-Feb-26 A	28-Sep-26	17-Feb-26	22-Jun-26									
	PS-CON-ELE-0040	Construction - SMP - Install Power Transformer SAT - Unit T 2, 3, 4	48	13-Apr-26 A	30-Sep-26	13-Apr-26	02-Sep-26									
	PS-CON-ELE-0060	Construction - SMP - Install Power Transformer SAT - Unit T 7	0	04-May-26 A	14-Oct-26	04-May-26	30-Sep-26									
	PS-CON-STR-180	Construction - Equipment Installation including electrical works- Statcom	72	17-Feb-26 A	03-Nov-26	17-Feb-26	22-Jun-26									
	NPB515 - (SLG, LNG, GANZ, MHS, RAILWAY)		25	31-Jul-26	03-Sep-26	27-Jul-26	28-Aug-26									
	PS-CON-PIP-0030	Construction - E&I - Substation NPB-515	25	31-Jul-26	03-Sep-26	27-Jul-26	28-Aug-26									
	Water Ponds		206	20-Jul-26 A	28-May-27	22-Jun-26	28-May-27									
	Stormwater Ponds East		40	03-Aug-26	25-Sep-26	22-Jun-26	25-Sep-26									
	PN-CON-SWC-1015	Stormwater Ponds East 1-G roundworks	25	03-Aug-26	04-Sep-26	22-Jun-26	21-Aug-26									
	PN-CON-SWC-1064	Stormwater Ponds East 2-G roundworks	25	03-Aug-26	04-Sep-26	22-Jun-26	04-Sep-26									
	PN-CON-SWC-1114	Stormwater Ponds East 3-G roundworks	25	03-Aug-26	04-Sep-26	22-Jun-26	04-Sep-26									
	PN-CON-SWC-1016	Stormwater Ponds East 1-Piping Installation (connection between ponds)	15	07-Sep-26	25-Sep-26	24-Aug-26	11-Sep-26									
	PN-CON-SWC-1065	Stormwater Ponds East 2-Piping Installation (connection between ponds)	15	07-Sep-26	25-Sep-26	07-Sep-26	25-Sep-26									
	PN-CON-SWC-1115	Stormwater Ponds East 3-Piping Installation (connection between ponds)	15	07-Sep-26	25-Sep-26	07-Sep-26	25-Sep-26									
	Stormwater Ponds West		25	10-Aug-26	11-Sep-26	22-Jun-26	07-Aug-26									
	PN-CON-SWC-1280	Stormwater Ponds West 1-Embankment - Crushed Rock Installation	10	10-Aug-26	21-Aug-26	22-Jun-26	03-Jul-26									
	PN-CON-SWC-1220	Stormwater Ponds West 2-Crushed Rock - Pond Bottom Installation	15	10-Aug-26	28-Aug-26	06-Jul-26	24-Jul-26									
	PN-CON-SWC-1240	Stormwater Ponds West 2-Embankment - Crushed Rock Installation	10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26									
	Contact Water Pond		181	20-Jul-26 A	28-May-27	07-Sep-26	28-May-27									
	PN-CON-SWC-1295	Contact Water Pond-Groundworks	15	20-Jul-26 A	25-Sep-26	07-Sep-26	25-Sep-26									
	PN-CON-SWC-1290.1	Contact Water Pond-Excavation Previous works /Surcharge placement and removal- Phase 2	80	07-Sep-26	28-May-27	07-Sep-26	28-May-27									
	Wetlands		40	10-Aug-26	02-Oct-26	10-Aug-26	02-Oct-26									
	PN-CON-SWC-1330	Wetlands-Groundworks	40	10-Aug-26	02-Oct-26	10-Aug-26	02-Oct-26									
	Pipe & Cable Racks		113	11-Dec-24 A	07-Jan-27	11-Dec-24	25-Nov-26									
	PR Civil, Structural and Architectural (CSA)		110	11-Dec-24 A	29-Dec-26	11-Dec-24	20-Nov-26									
	PB-CON-CIV-0030	Construction - PCR - Pipe rack Foundation - Priority 3 - excavation	5	04-Feb-25 A	28-Aug-26	04-Feb-25	10-Jul-26									
	PB-CON-MEC-50	Construction - PCR - Piping Connections - Priority 1	25	09-Sep-25 A	28-Aug-26	09-Sep-25	28-Aug-26									
	PB-CON-CIV-290	Construction - PCR - Pipe rack Foundation - Priority 3 - concrete	20	04-Feb-25 A	28-Aug-26	04-Feb-25	24-Jul-26									
	PB-CON-MEC-90	Construction - PCR - Piping Connections - Priority 5	30	02-Mar-26 A	04-Sep-26	02-Mar-26	28-Aug-26									
	PB-CON-CIV-300	Construction - PCR - Pipe rack Foundation - Priority 3 - backfilling	25	04-Feb-25 A	04-Sep-26	04-Feb-25	31-Jul-26									
	PB-CON-STR-70	Construction - PCR - Columns Erection - Priority 3	18	15-Oct-25 A	18-Sep-26	15-Oct-25	14-Aug-26									
	PB-CON-CIV-270	Construction - PCR - Pipe rack Foundation - Priority 2 - backfilling	5	11-Dec-24 A	02-Oct-26	11-Dec-24	31-Jul-26									
	PB-CON-STR-0020	Construction - PCR - Modules Erection - Priority 2	21	03-Nov-25 A	09-Oct-26	03-Nov-25	20-Jul-26									
	PB-CON-CIV-380	Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - excavation	46	12-Nov-25 A	13-Oct-26	12-Nov-25	10-Jul-26									
	PB-CON-MEC-0020	Construction - PCR - Loose Items Installation (Cable Trays) - Priority 2	13	01-Dec-25 A	14-Oct-26	01-Dec-25	23-Jul-26									
	PB-CON-STR-0030	Construction - PCR - Modules Erection - Priority 3	20	24-Nov-25 A	16-Oct-26	24-Nov-25	11-Sep-26									
	PB-CON-CIV-400	Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - concrete	46	13-Nov-25 A	22-Oct-26	13-Nov-25	04-Aug-26									
	PB-CON-MEC-60	Construction - PCR - Piping Connections - Priority 2	20	02-Mar-26 A	23-Oct-26	02-Mar-26	23-Oct-26									
	PB-CON-CIV-410	Construction - PCR - Remaining Pipe rack Foundation - Priority 4 - backfilling	44	17-Nov-25 A	29-Oct-26	17-Nov-25	05-Aug-26									
	PB-CON-MEC-0030	Construction - PCR - Loose Items Installation (Cable Trays) - Priority 3	30	02-Mar-26 A	30-Oct-26	02-Mar-26	25-Sep-26									
	PB-CON-STR-190	Construction - PCR - Secondary Steel - Priority 3	30	02-Mar-26 A	06-Nov-26	02-Mar-26	02-Oct-26									
	PB-CON-STR-150	Construction - PCR - Pipe Drops and Loose Items - Priority 2	15	06-Jul-26 A	10-Nov-26	07-Oct-26	27-Oct-26									

Actions

BOP – 6 Week Look Ahead

Activity ID	Activity Name	Remaining Duration	Start	Finish	BL Project Start	BL Project Finish	August					September	
							55					56	
							W31	W32	W33	W34	W35	W36	W37
PB-CON-MEC-70	Construction - PCR - Piping Connections - Priority 3	60	12-May-26 A	18-Dec-26	12-May-26	13-Nov-26							
PB-CON-STR-180	Construction - PCR - Pipe drops and Loose Items - Priority 3	40	01-Jul-26 A	29-Dec-26	28-Sep-26	20-Nov-26							
PR Mechanical Electrical and Piping		44	13-Jul-26 A	07-Jan-27	15-Oct-26	25-Nov-26							
PB-CON-MEC-320	Construction - PCR - Cable Trays Drops Installation - Priority 2	15	13-Jul-26 A	19-Nov-26	16-Oct-26	05-Nov-26							
PB-CON-MEC-300	Construction - PCR - Cable Trays Drops Installation - Priority 3	30	13-Jul-26 A	07-Jan-27	15-Oct-26	25-Nov-26							
PR OEM Equipment installations, Equipment test and Pre commissioning		55	27-Jul-26	09-Oct-26	31-Aug-26	20-Oct-26							
PB-CON-MEC-350	Construction - PCR - Piping Pressuring test + Restatement (RFC) - Priority 5	10	27-Jul-26	07-Aug-26	30-Sep-26	13-Oct-26							
PB-CON-MEC-270	Construction - PCR - Piping Heat Tracing, Painting Touch up and Insulation - Priority 5	5	07-Sep-26	11-Sep-26	14-Oct-26	20-Oct-26							
PB-CON-MEC-330	Construction - PCR - Piping Pressuring test + Restatement (RFC) - Priority 1	30	31-Aug-26	09-Oct-26	31-Aug-26	09-Oct-26							
Site Railway Network		117	27-May-25 A	21-Jan-27	27-May-25	09-Dec-26							
Site Railway Network - Railway (MVP)		117	27-May-25 A	21-Jan-27	27-May-25	09-Dec-26							
RAS-CON-GEN-2390	Construction - North Railway - Section 7 - Cable wells - (Installation of buried cables, cable ducts, multiducts)	10	14-Jul-25 A	28-Aug-26	14-Jul-25	24-Jul-26							
RAS-CON-GEN-2970	Construction - North Railway - Section 7 - Cable wells - (earthing ducts)	10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26							
RAS-CON-GEN-3230	Construction - North Railway - Section 4 A - Construction East Ditch	35	29-Aug-26	08-Oct-26									
RAS-CON-GEN-1660	Construction - North Railway - Section 7 - Track 103 - Installation Hanging Work - Wire	97	27-May-25 A	21-Jan-27	27-May-25	09-Dec-26							
Site Railway Network - Railway Shunting Yard		42	31-Aug-26	27-Oct-26	27-Jul-26	27-Oct-26							
RAS-CON-GEN-3090	Construction - Railway Shunting Yard - South Railway - East Part - Groundworks (Excavations for drainage and Foundation)	10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26							
RAS-CON-GEN-2460	Construction - Railway Shunting Yard - South Railway - West Part - Groundworks (Excavations for drainage and Foundation)	40	02-Sep-26	27-Oct-26	02-Sep-26	27-Oct-26							
Underground Networks		135	03-Oct-25 A	09-Feb-27	03-Oct-25	23-Oct-26							
Piping Route 0 to Route 5 & Others Areas UG Networks		135	03-Oct-25 A	09-Feb-27	03-Oct-25	23-Oct-26							
IF-CON-CIV-1680	UG Networks - Others Areas - RW + FF (A) - Testing (PT,HT,LT etc.)	10	27-Jul-26	07-Aug-26	22-Jun-26	03-Jul-26							
IF-CON-CIV-1160	Underground Networks - Route 3 (A Road 6.1/6.2) - excavation and trench	15	25-May-26 A	14-Aug-26	25-May-26	31-Jul-26							
IF-CON-CIV-240	Underground Networks - Route 1 - Testing (PT,HT,LT etc.) A (Road 7)	10	10-Aug-26	21-Aug-26	06-Jul-26	17-Jul-26							
IF-CON-CIV-360	UG Networks - Others Areas - RW + FF (E) - trench excavation (BoP and SIN)	10	10-Aug-26	21-Aug-26	06-Jul-26	17-Jul-26							
IF-CON-CIV-1170	Underground Networks - Route 3 (A Road 6.1/6.2) - Piping Installation & Welding (WFI / WBD / WSI)	5	08-Jun-26 A	21-Aug-26	08-Jun-26	21-Aug-26							
IF-CON-CIV-1580	UG Networks - Others Areas - RW + FF (C) - Testing (PT,HT,LT etc.)	10	10-Aug-26	21-Aug-26	06-Jul-26	17-Jul-26							
IF-CON-CIV-1630	UG Networks - Others Areas - RW + FF (B) - Testing (PT,HT,LT etc.)	10	10-Aug-26	21-Aug-26	06-Jul-26	17-Jul-26							
IF-CON-CIV-220	Underground Networks - Route 0 - Testing (PT,HT,LT etc.)	25	03-Oct-25 A	28-Aug-26	03-Oct-25	24-Jul-26							
IF-CON-CIV-1540	UG Networks - Others Areas - RW + FF (D) - Piping Installation & Welding (WFI / WRA)	15	06-Jul-26 A	28-Aug-26	06-Jul-26	24-Jul-26							
IF-CON-CIV-1790	Underground Networks - Route 1 - Testing (PT,HT,LT etc.) E, F, G (Av 9.5)	10	17-Aug-26	28-Aug-26	10-Jul-26	23-Jul-26							
IF-CON-CIV-2030	Underground Networks - Route 3 (A Road 6.1/6.2) - Backfilling in trenches for underground piping	10	15-Jun-26 A	04-Sep-26	15-Jun-26	04-Sep-26							
IF-CON-CIV-390	UG Networks - Others Areas - RW + FF (E) - Piping Installation & Welding (WFI / WRA)	15	24-Aug-26	11-Sep-26	20-Jul-26	07-Aug-26							
IF-CON-CIV-1480	Underground Networks - Route 4 (A-B) (Av 9.4-9.3 - Av 6) - trench excavation	30	03-Aug-26	11-Sep-26	20-Jul-26	11-Sep-26							
IF-CON-CIV-1530	UG Networks - Others Areas - RW + FF (D) - Testing (PT,HT,LT etc.)	10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26							
IF-CON-CIV-1770	Underground Networks - Route 3 (A Road 6.1/6.2) Testing (PT,HT,LT etc.)	20	17-Aug-26	11-Sep-26	07-Sep-26	02-Oct-26							
IF-CON-CIV-1780	Underground Networks - Route 1 - Testing (PT,HT,LT etc.) B, C, D (Road 7)	10	31-Aug-26	11-Sep-26	27-Jul-26	07-Aug-26							
IF-CON-CIV-1500	Underground Networks - Route 4 (A-B) (Av 9.4-9.3 - Av 6) - Piping Install & Weld (WFI P1 / around 15 lines)	25	24-Aug-26	25-Sep-26	24-Aug-26	02-Oct-26							
IF-CON-CIV-1510	Underground Networks - Route 4 (A-B) (Av 9.4-9.3 - Av 6) - Backfilling in trenches for underground piping	25	07-Sep-26	09-Oct-26	14-Sep-26	16-Oct-26							
IF-CON-CIV-180	Underground Networks - Route 5 - trench excavation (BoP and SIN)	84	17-Nov-25 A	02-Dec-26	17-Nov-25	25-Sep-26							
IF-CON-CIV-310	Underground Networks - Route 5 - Piping Installation & Welding (WFI from P1 to Others Areas - 90 m)	10	24-Nov-25 A	29-Dec-26	24-Nov-25	09-Oct-26							
IF-CON-CIV-200	Underground Networks - Route 5 - Backfilling in trenches for underground piping	10	24-Nov-25 A	09-Feb-27	24-Nov-25	23-Oct-26							
PDOP UG		12	22-Jul-26 A	11-Aug-26	27-Jul-26	11-Aug-26							
PS-CON-ELE-340	Construction - PDOP Yard - Cable Trays installation	12	22-Jul-26 A	11-Aug-26	27-Jul-26	11-Aug-26							
BOP E&I Ducts		20	24-Aug-26	18-Sep-26	20-Jul-26	14-Aug-26							
IF-CON-CIV-710	UG Electr. - Duct Bank - E-HOUSE 511 / RAW WATER AREA - construction	20	24-Aug-26	18-Sep-26	20-Jul-26	14-Aug-26							

Actions

BOP – 6 Week Look Ahead

Activity ID	Activity Name	Remaining Duration	Start	Finish	BL Project Start	BL Project Finish							
							August 55					September 56	
							W31	W32	W33	W34	W35	W36	W37
BOP Cable Pulling		30	12-Aug-26	22-Sep-26	22-Jun-26	22-Sep-26							
IF-CON-ELE-620	BOP Cables - MV - ELA01 to NPB 511 - permanent routing at ELA	10	17-Aug-26	28-Aug-26	22-Jun-26	03-Jul-26							
IF-CON-ELE-610	BOP Cables - HV - PDOP-Transformers - laying, glanding & termination	30	12-Aug-26	22-Sep-26	12-Aug-26	22-Sep-26							
Scope Waiting for Cho Approvals		10	07-Sep-26	18-Sep-26	13-Jul-26	24-Jul-26							
Roads		10	07-Sep-26	18-Sep-26	13-Jul-26	24-Jul-26							
RO-CON-SWC-1140	Roads - Road 6 - Laying of sub-base and base layers	10	07-Sep-26	18-Sep-26	13-Jul-26	24-Jul-26							
